



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 1, 2019

Work Accomplished Last Two Weeks

October 18, 2019 through October 24, 2019.

- ✓ Installed 843 LFT of 16" Ductile Iron Pipe (DIP) from Station # 122+92 to Station # 131+35 on South Main Street (Rte.17), Middletown.
- ✓ Installed 625 LFT of 16" DIP from Station # 46+50 to Station # 40+25 on Talcott Ridge Drive, Middletown.
- ✓ Saw-cut 550 LFT of trench on Main Street (Rte.17) Durham. At Station # 142+09.

October 25, 2019 through October 30, 2019.

- ✓ Installed 196 LFT of 16" DIP from Station # 40+25 to Station # 38+29 on Talcott Ridge Drive, Middletown.
- ✓ Installed 523LFT of 16" DIP from Station # 131+35 to Station # 136+58 on Main Street (Rte.17), Durham.
- ✓ Installed (3) Fire Hydrants on Talcott Ridge Drive, Middletown. Stations # 51+40, 44+53 and 40+54.

Work Planned for Next Two Weeks

November 3, 2019 through November 8, 2019.

Main Street, Durham: Installation approximate Station # 136+50 to Station # 141+00.

Talcott Ridge Drive, Middletown: Installation approximate Station # 38+59 to Station # 35+00.

- ✓ Sunday November 3, through Friday November 8, 2019: 7:00 pm – 5:00 am. Install 16" DIP on Main Street (Rte. 17), Durham.
- ✓ Monday November 4, through Friday November 8, 2019: 7:00 am – 3:30 pm. Install 16" DIP on Talcott Ridge Drive, Middletown.
- ✓ Friday November 8, 2019: 8:00 am – 3:00 pm. Saw-Cut Main Street (Rte.17), Durham.

November 10, 2019 through November 15, 2019.

Main Street, Durham: Installation approximate Station # 141+00 to Station # 147+00.

Talcott Ridge Drive: Installation approximate Station # 35+00 to Station # 31+00.

- ✓ Monday, November 11, through Friday, November 15, 2019: 7:00 pm. – 5:00 am. Install 16" DIP on Main Street (Rte.17), Durham.
- ✓ Tuesday, November 12, through– Friday November 15, 2019: 7:00 am – 3:30 pm. Install 16" DIP on Talcott Ridge Drive, Middletown.
- ✓ Friday November 15, 2019: 8:00 am – 3:00 pm. Saw cut Main Street (Rte.17), Durham.



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 1, 2019

Construction Schedule 2019 Construction Activities:

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south almost to Royal Oak Drive in Durham.
 - Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown. This work will begin at the intersection with Route 17.
 - Clearing of the Water Storage Middletown.
 - Installation of the Pressure Relief Valve and Vault in Durham.
 - Installation of the water main on Route 17 from Old Cemetery Road in Durham to Wallingford Road (Route 68) in Durham.
- All remaining construction activities will occur in 2020 or 2021.

Mainline Water Line (28,272 feet total)

Start Date: September 8, 2019

Installed	
Feet	%
4,235	14.97

Ready for connection	
Feet	%
0	0.0%

Planned Work Location/Limits

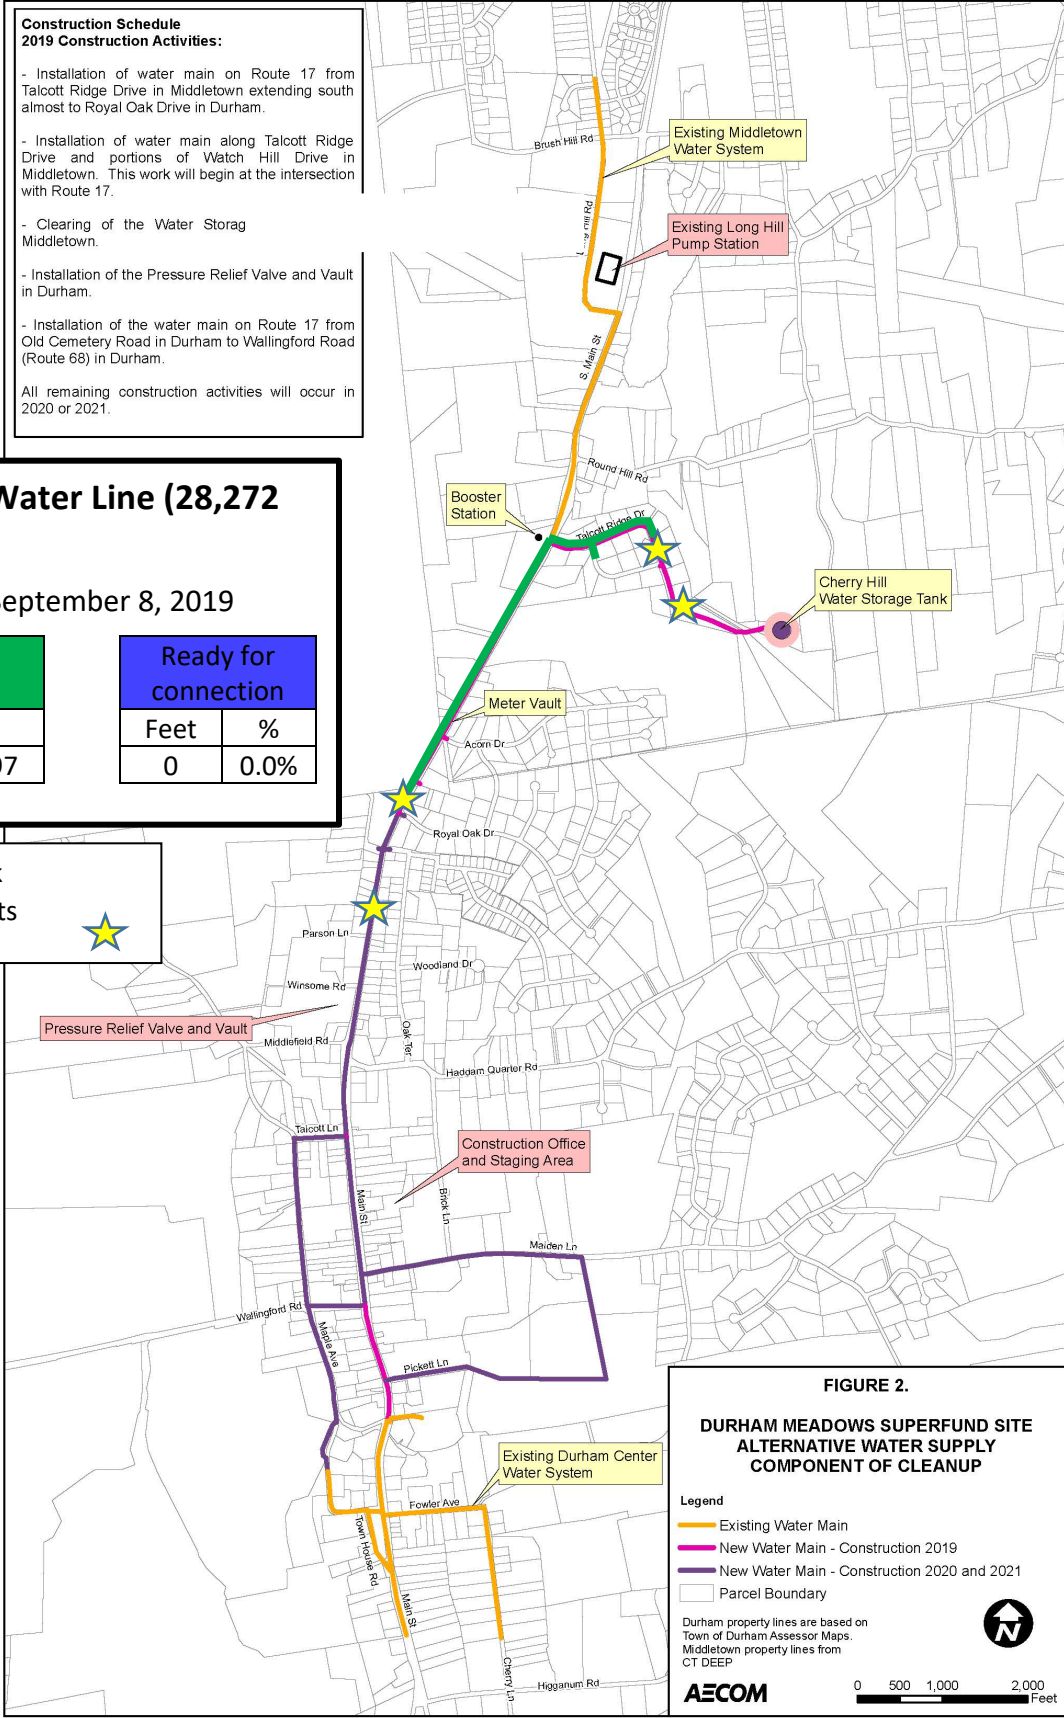


FIGURE 2.

DURHAM MEADOWS SUPERFUND SITE ALTERNATIVE WATER SUPPLY COMPONENT OF CLEANUP

Legend

- Existing Water Main
- New Water Main - Construction 2019
- New Water Main - Construction 2020 and 2021
- Parcel Boundary

Durham property lines are based on Town of Durham Assessor Maps.
Middletown property lines from CT DEEP



AECOM

0 500 1,000 2,000 Feet

© \Projects\HAZ\WASTE\04\53\OUR\WAFS\Fig_2_Recommended\hshstructure.mxd



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 1, 2019


Curb Stops (211 total)

Start Date: August 24, 2020

Installed		Ready for connection	
Each	%	Each	%
0	0.0%	0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.



Homes Connected (115 total)


Start Date: October 27, 2020

Connected	
Homes	%
0	0.0%



Cherry Hill Tank Construction (72 feet)

Start Date: June 11, 2020

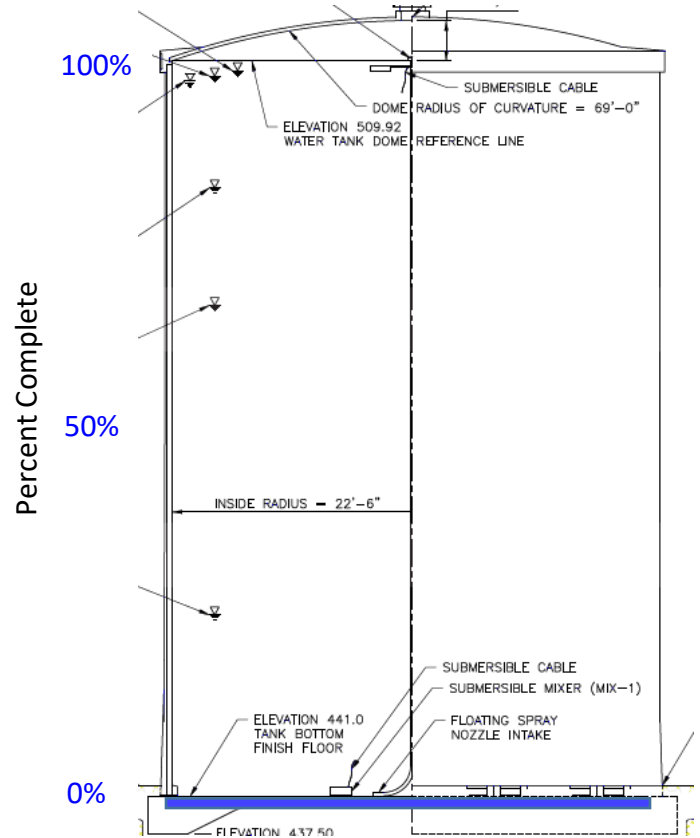



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 1, 2019



Compacting pipe trench at approximately STA # 135+00 on Main Street (Rte. 17), Durham.



Installing 16" DIP at approximately STA # 135+00 on Main Street (Rte.17), Durham.



Compaction Testing at STA # 43+29 on Talcott Ridge Drive, Middletown.
