



## Bi-Weekly Progress Report

# Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 15, 2019

### Work Accomplished Last Two Weeks

#### November 3, 2019 through November 8, 2019.

- ✓ Installed 880 LFT of 16" Ductile Iron Pipe (DIP) from Station # 136+58 to Station # 145+38 on Main Street (Rte.17), Durham.
- ✓ Installed 624 LFT of 16" DIP from Station # 38+29 to Station # 32+05 on Talcott Ridge Drive, Middletown.
- ✓ Saw-cut 407 LFT of trench on Main Street (Rte.17) in Durham, from Station # 148+23 to Station # 152+30.

#### November 11, 2019 through November 14, 2019.

- ✓ Installed 26 LFT of 16" DIP from Station # 32+05 to Station # 31+79 on Talcott Ridge Drive, Middletown.
- ✓ Installed 183 LFT of 20" DIP from Station # 31+79 to Station # 29+96 on Talcott Ridge Drive, Middletown.
- ✓ Installed 8"x 8" Tapping sleeve and valve at Station # 756+48 on Talcott Ridge Drive at Watch Hill Drive Middletown.
- ✓ Installed 809 LFT of 16" DIP from Station # 145+38 to Station # 153+47 on Main Street (Rte.17), Durham.

### Work Planned for Next Two Weeks

#### November 17, 2019 through November 22, 2019.

**Main Street, Durham:** Installation 16" DIP approximate Station # 153+65 to Station # 161+00

**Watch Hill Drive, Middletown:** Installation 8" DIP approximate Station # 600+00 to Station # 604+34

**Talcott Ridge Drive, Middletown:** Installation 8" DIP approximate Station # 47+30 to Station # 52+00.

- ✓ Friday November 15, 2019: 8:00 am – 3:00 pm. Saw-Cut Main Street (Rte.17), Durham.
- ✓ Sunday November 17, through Friday November 22, 2019: 7:00 pm – 5:00 am. Install 16" DIP on Main Street (Rte. 17), Durham.
- ✓ Monday November 18, through Friday November 22, 2019: 7:00 am – 3:30 pm. Install 8" DIP on Watch Hill Drive, Middletown.
- ✓ Friday November 22, 2019: 8:00 am – 3:00 pm. Saw-Cut Main Street (Rte.17), Durham.

#### November 25, 2019 through November 27, 2019. **No Night Work.**

**Main Street, Durham/ South Main Street, Middletown:** Installation of Hydrants and Street Crossings.

**Talcott Ridge Drive, Middletown:** Installation approximate Station # 47+30 to Station # 52+00.

- ✓ Monday November 25, 2019 through Tuesday November 26, 2019: 8:00 am – 3:30 pm. Hydrants/Street Crossings, Route 17, Durham/Middletown.
- ✓ Monday November 25, 2019 through Wednesday November 27, 2019: 7:00 am – 3:30 pm. Install 8" DIP on Talcott Ridge Drive, Middletown.



# Bi-Weekly Progress Report

## Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 15, 2019

### Construction Schedule 2019 Construction Activities:

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south almost to Royal Oak Drive in Durham.
- Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown. This work will begin at the intersection with Route 17.
- Clearing of the Water Storage Tank Site in Middletown.
- Installation of the Pressure Relief Valve and Vault in Durham.

All remaining construction activities will occur in 2020 or 2021.

### Mainline Water Line (28,272 feet total)

Start Date: September 8, 2019

Installed	
Feet	%
7,741	27.38

Ready for connection	
Feet	%
0	0.0%

Planned Work  
Location/Limits

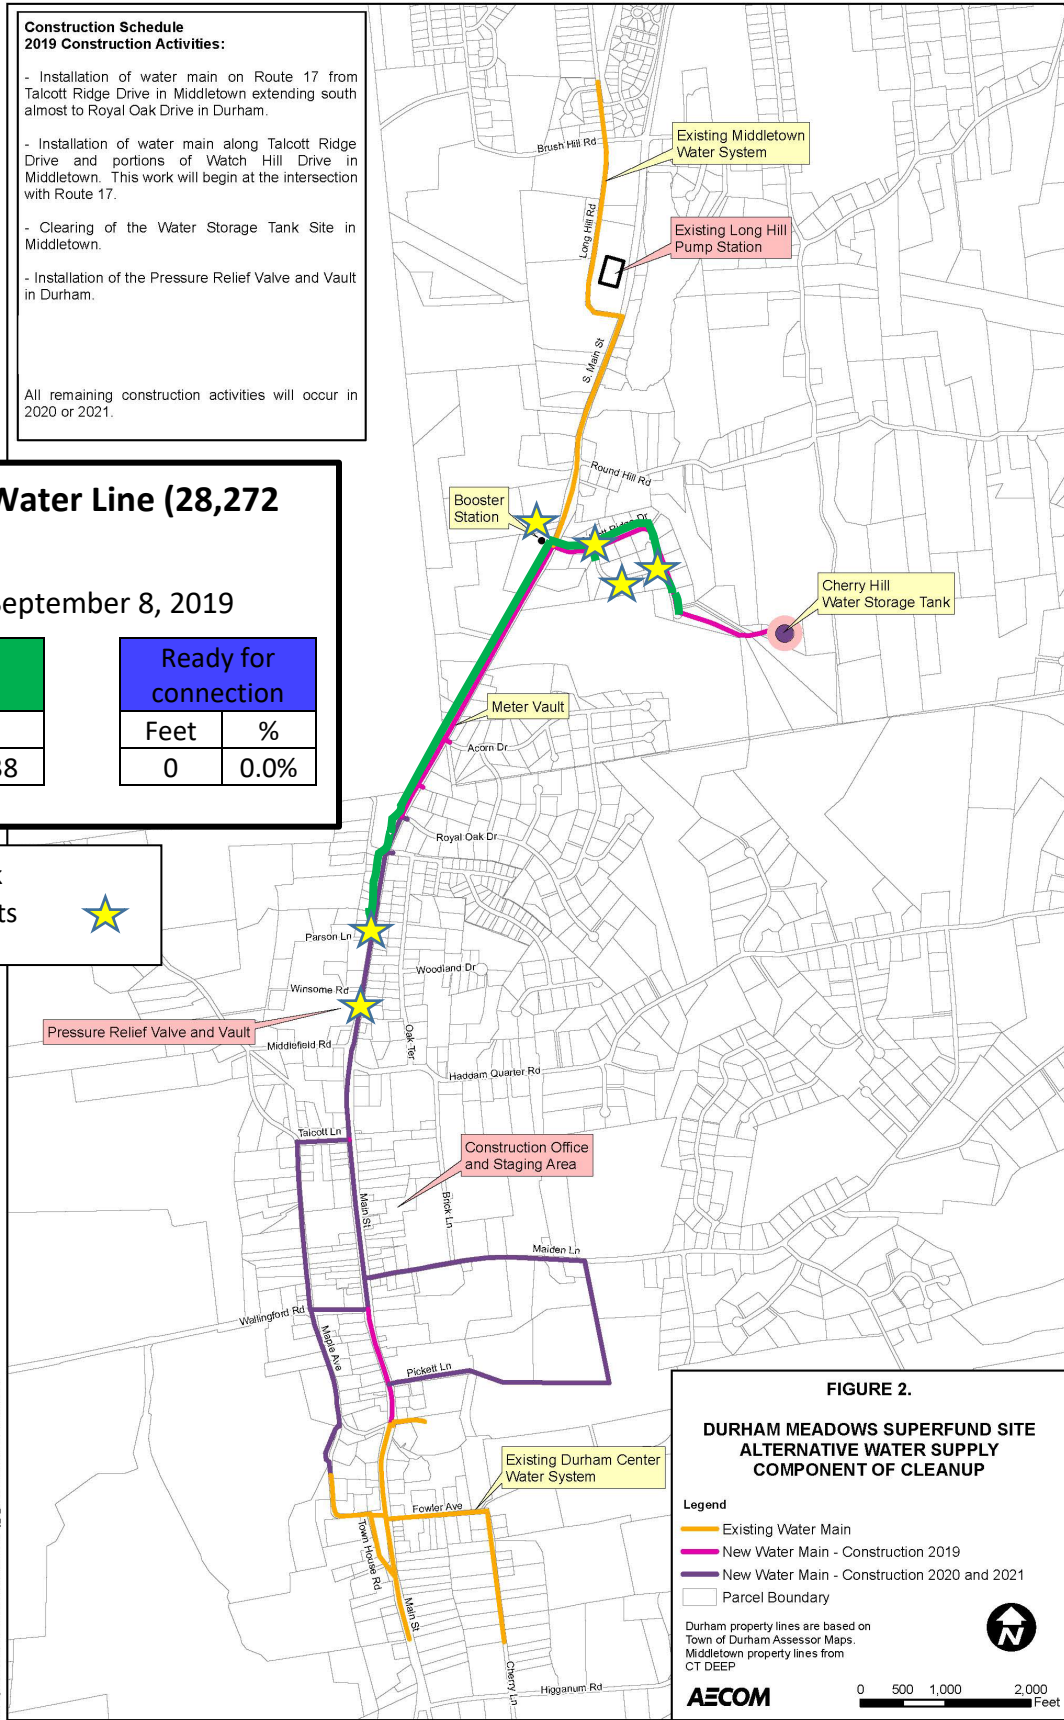


FIGURE 2.

### DURHAM MEADOWS SUPERFUND SITE ALTERNATIVE WATER SUPPLY COMPONENT OF CLEANUP

Legend

- Existing Water Main
- New Water Main - Construction 2019
- New Water Main - Construction 2020 and 2021
- Parcel Boundary

Durham property lines are based on Town of Durham Assessor Maps. Middletown property lines from CT DEEP



AECOM

0 500 1,000 2,000 Feet



# Bi-Weekly Progress Report

## Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 15, 2019


### Curb Stops (211 total)

Start Date: August 24, 2020

Installed		Ready for connection	
Each	%	Each	%
0	0.0%	0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.

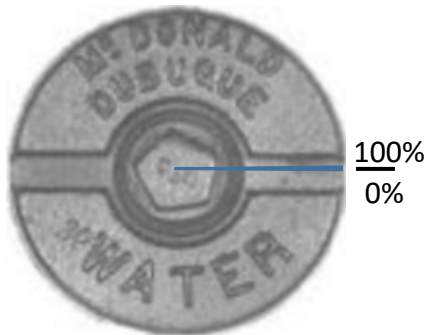

### Homes Connected (115 total)


Start Date: October 27, 2020

Connected	
Homes	%
0	0.0%



### Cherry Hill Tank Construction (72 feet)

Start Date: June 11, 2020

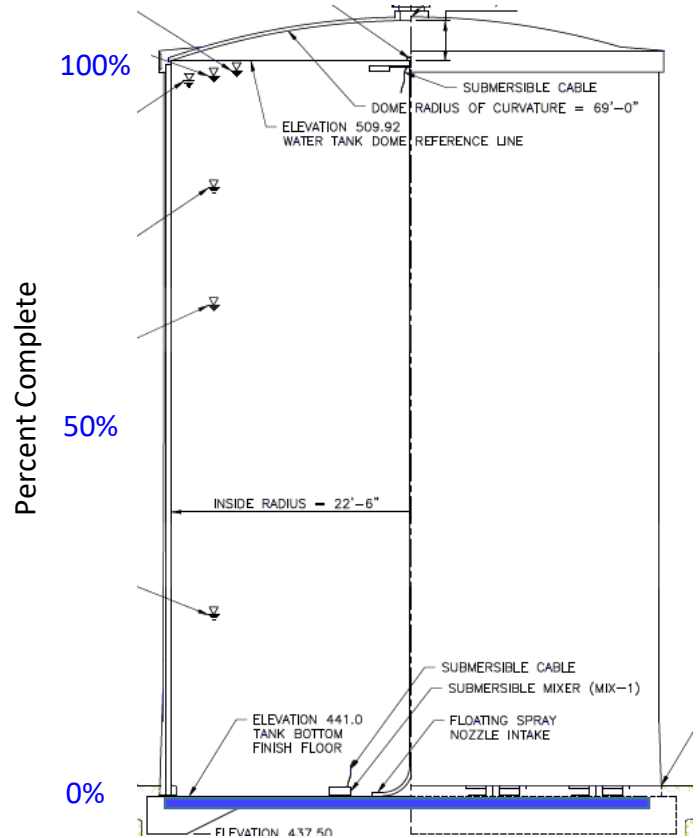



# Bi-Weekly Progress Report

## Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 15, 2019



Spreading stone base on Rt 17 Durham approx. STA 146+00



Installing 16" DIP on Rt 17 Durham approx STA # 140+00
