



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 29, 2019

Work Accomplished Last Two Weeks

November 15, 2019 through November 22, 2019.

- ✓ Installed 430 LFT of 16" Ductile Iron Pipe (DIP) from Station # 600+04 to Station # 604+34 on Watch Hill Drive, Middletown.
- ✓ Installed Fire Hydrant at Station # 604+34 on Watch Hill Drive and Station # 36+41 on Talcott Ridge Drive, Middletown.
- ✓ Installed 132 LFT of 8" DIP from Station # 756+46 to Station # 755+14 on Talcott Ridge Drive, Middletown.
- ✓ Installed 661 LFT of 16" DIP from Station # 153+47 to Station # 160+08 on Main Street (Rte.17), Durham.

November 25, 2019 through November 27, 2019.

- ✓ Installed 284 LFT of 8" DIP from Station # 755+14 to Station # 752+30 on Talcott Ridge Drive, Middletown.
- ✓ Installed 46 LFT of 8" DIP on Winsome Road and 26 LFT of 8" DIP on Parsons Lane, Durham.
- ✓ Installed Fire Hydrant on Winsome Road, Durham.
- ✓ Installed 32 LFT of 20" DIP from Station # 29+30 to Station # 29+63 on Talcott Ridge Drive, Middletown.
- ✓ Removed Material and Equipment from the Cul-De-Sac on Talcott Ridge Drive, Middletown and the State of Ct. Salt Shed Property.

Work Planned for Next Two Weeks

December 2, 2019 through December 6, 2019.

- Clearing tank access road and tank site, Middletown.
- Street crossing at the intersection of Little Lane and Oak Terrace, Durham.
- Street Crossings at Meter Vault.

December 9, 2019 through December 13, 2019.

- Installing Street Crossings at Talcott Ridge Dr and Rt 17.
- Clearing tank site, Middletown.
- Check trenches on Rte. 17 in Durham and Middletown and skim coat where needed prior to winter shutdown.



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 29, 2019

Construction Schedule
2019 Construction Activities:

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south almost to Royal Oak Drive in Durham.
- Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown. This work will begin at the intersection with Route 17.
- Clearing of the Water Storage Tank Site in Middletown.
- Installation of the Pressure Relief Valve and Vault in Durham.
- Installation of the water main on Route 17 from

All remaining construction activities will occur in 2020 or 2021.

Mainline Water Line (28,272 feet total)

Start Date: September 8, 2019

Installed		Ready for connection	
Feet	%	Feet	%
9,326	32.99	0	0.0%

Planned Work Location/Limits

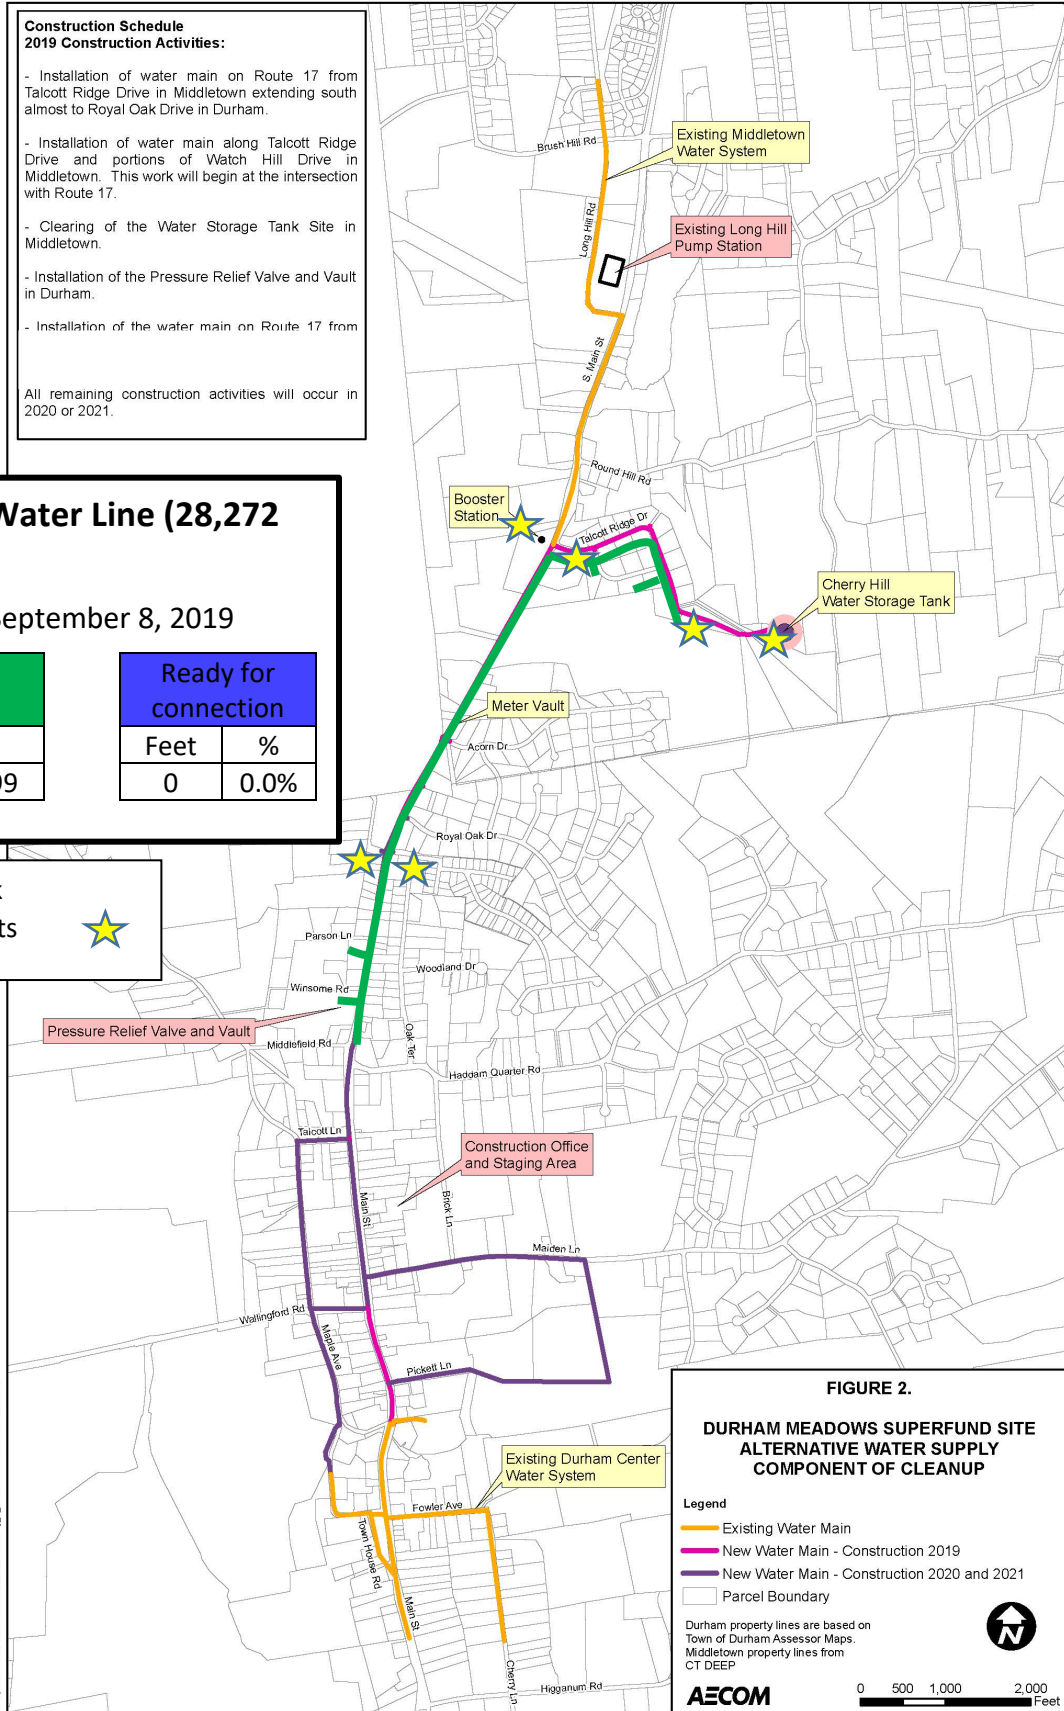


FIGURE 2.

DURHAM MEADOWS SUPERFUND SITE ALTERNATIVE WATER SUPPLY COMPONENT OF CLEANUP

Legend

- Existing Water Main
- New Water Main - Construction 2019
- New Water Main - Construction 2020 and 2021
- Parcel Boundary

Durham property lines are based on Town of Durham Assessor Maps. Middletown property lines from CT DEEP



AECOM

0 500 1,000 2,000 Feet

© Project#2402019045030URWAPSP02_2_RecommenedItrastucture.mxd



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 29, 2019


Curb Stops (211 total)

Start Date: August 24, 2020

Installed		Ready for connection	
Each	%	Each	%
0	0.0%	0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.

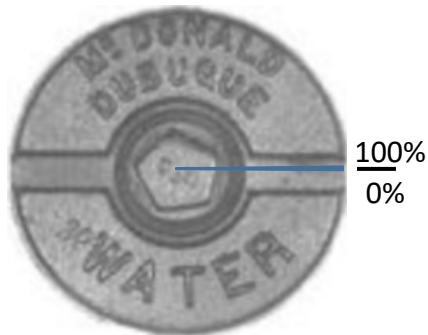

Homes Connected (115 total)


Start Date: October 27, 2020

Connected	
Homes	%
0	0.0%



Cherry Hill Tank Construction (72 feet)

Start Date: June 11, 2020

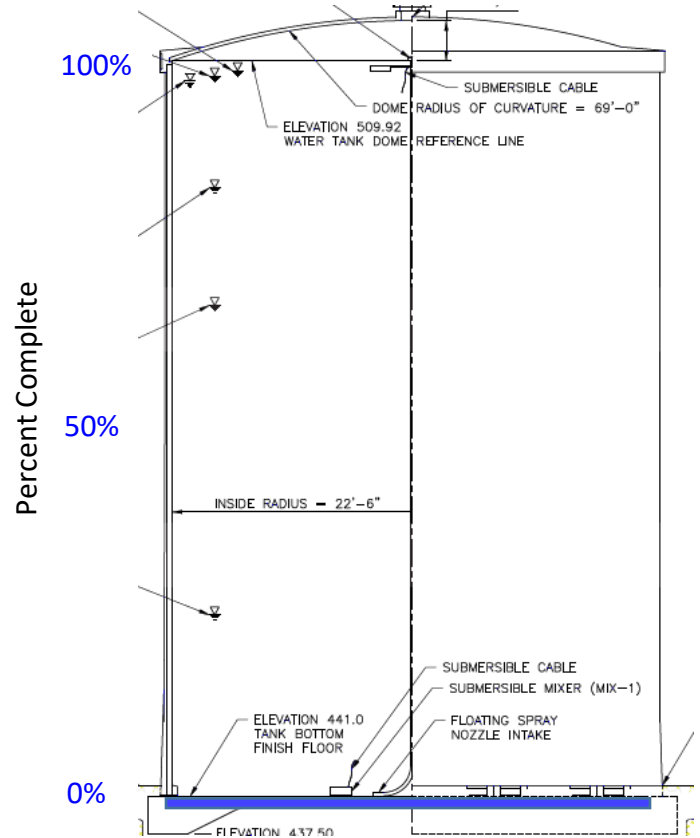



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

November 29, 2019



Installing 8" DI pipe STA 151+50 Parsons Lane



Compaction of Sand Bedding STA 155+80
