



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

October 18, 2019

Work Accomplished Last Two Weeks

October 6, 2019 through October 11, 2019.

- ✓ Installed 401 LFT of 16" Ductile Iron Pipe (DIP) from Station # 111+88 to Station # 115+89 on South Main Street (Rt. 17), Middletown.
- ✓ Installed Fire Hydrant at Station # 113+98 on South Main Street (Rt. 17), Middletown.
- ✓ Installed 257 LFT of 16" DIP from Station # 51+92 to Station # 49+35 on Talcott Ridge Drive, Middletown.
- ✓ Saw-cut 687 LFT of trench on South Main Street (Rt. 17), Middletown and continuing into Durham.

October 14, 2019 through October 18, 2019.

- ✓ Installed 703 LFT of 16" DIP from Station # 115+89 to Station # 122+92 on South Main Street (Rt. 17) Middletown.
- ✓ Installed 285 LFT of 16" DIP from Station # 49+35 to Station # 46+50 on Talcott Ridge Drive, Middletown.

Work Planned for Next Two Weeks

October 20, 2019 through October 25, 2019.

- ✓ Sunday – Thursday: 7:00 pm – 5:00 am. Install 16" DIP on South Main Street (Rte.17) Middletown and continuing into Durham from Station # 122+92 to 130+92.
- ✓ Monday – Friday: 7:00 am – 3:30 pm. Install 16" DIP on Talcott Ridge Drive, Middletown from Station # 46+50 to 41+50.
- ✓ Friday: 8:00 am – 3:00 pm. Saw-Cut Main Street (Rte.17) Durham.

October 27, 2019 through November 1, 2019.

- ✓ Sunday – Thursday: 7:00 pm – 5:00 am. Install 16" DIP on Main Street (Rte.17) Durham from Station # 130+92 to 138+92.
- ✓ Monday – Friday: 7:00 am – 3:30 pm. Install 16" DIP on Talcott Ridge Drive, Middletown from Station # 41+50 to 36+50.



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

October 18, 2019

Construction Schedule 2019 Construction Activities:

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south almost to Royal Oak Drive in Durham.
- Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown. This work will begin at the intersection with Route 17.
- Clearing of the Water Storage Tank Site in Middletown.
- Installation of the Pressure Relief Valve and Vault in Durham.

All remaining construction activities will occur in 2020 or 2021.

Mainline Water Line (28,272 feet total)

Start Date: September 8, 2019


Installed	
Feet	%
2,869	10.15

Ready for connection	
Feet	%
0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.

Planned Work
Location/Limits

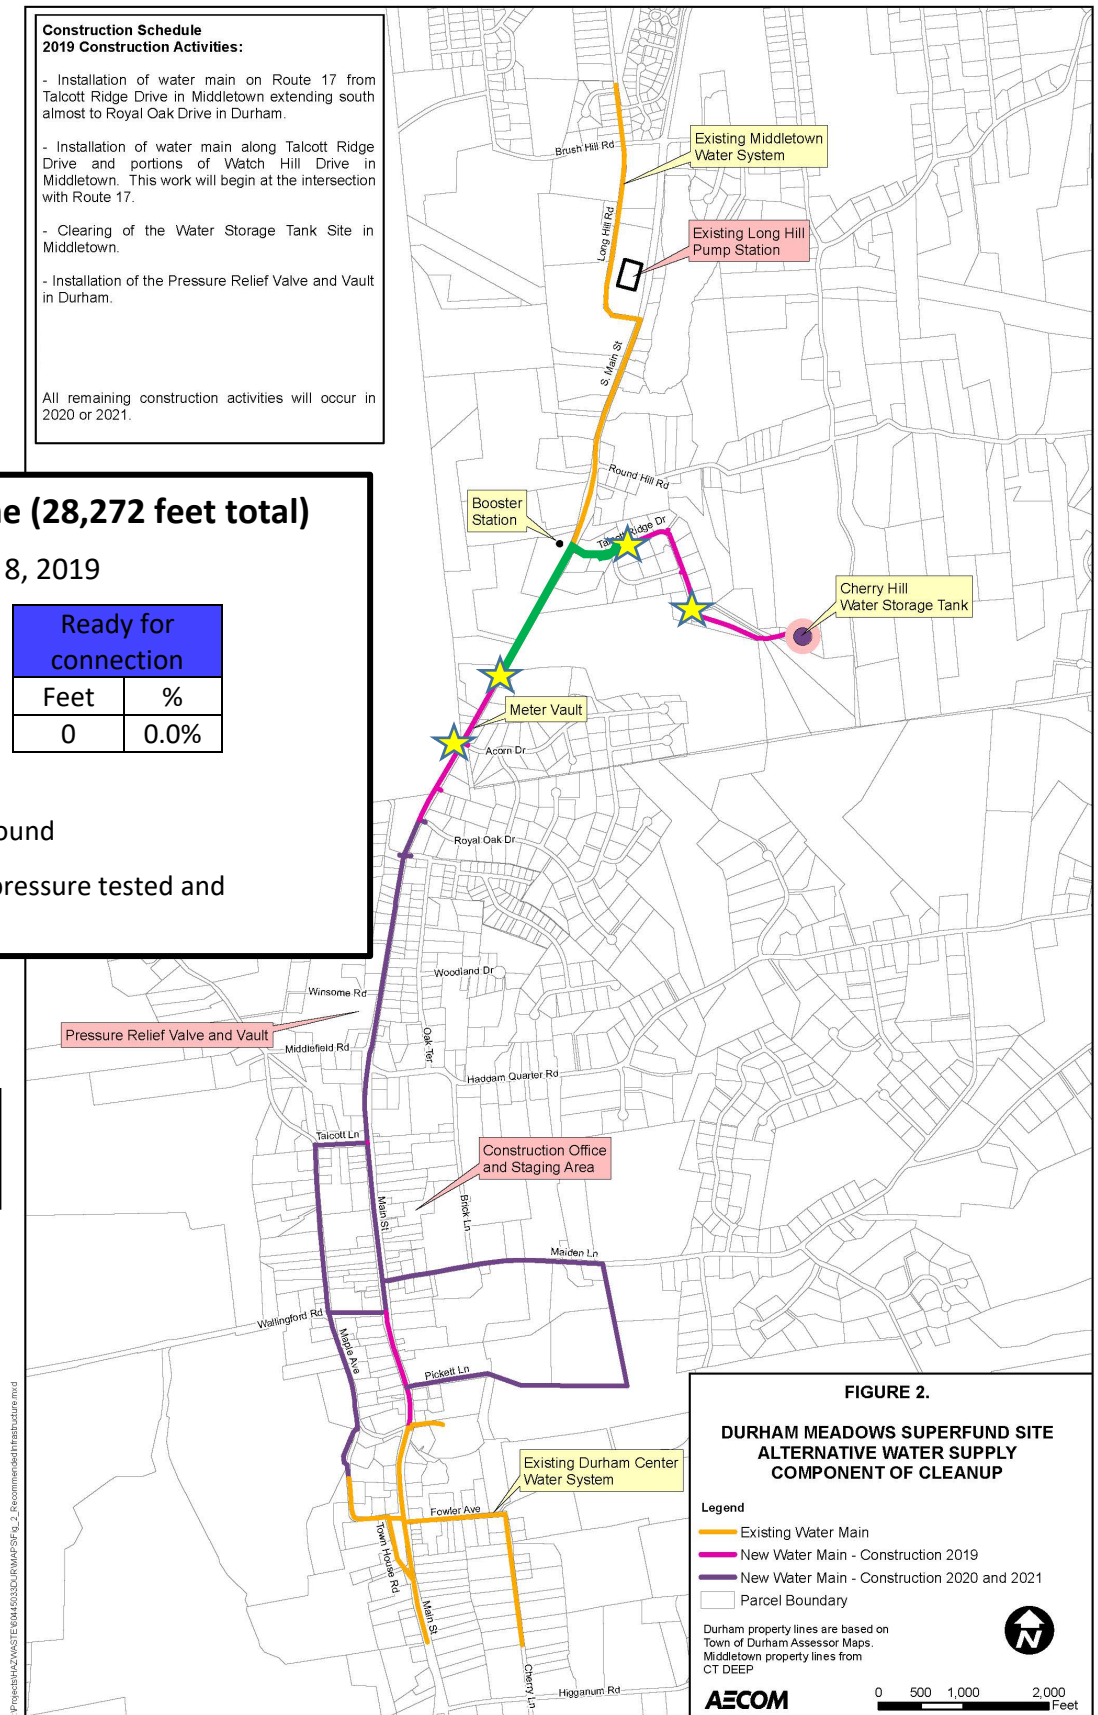



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

October 18, 2019


Curb Stops (211 total)

Start Date: August 24, 2020

Installed		Ready for connection	
Each	%	Each	%
0	0.0%	0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.



Homes Connected (115 total)


Start Date: October 27, 2020

Connected	
Homes	%
0	0.0%



Cherry Hill Tank Construction (72 feet)

Start Date: June 11, 2020

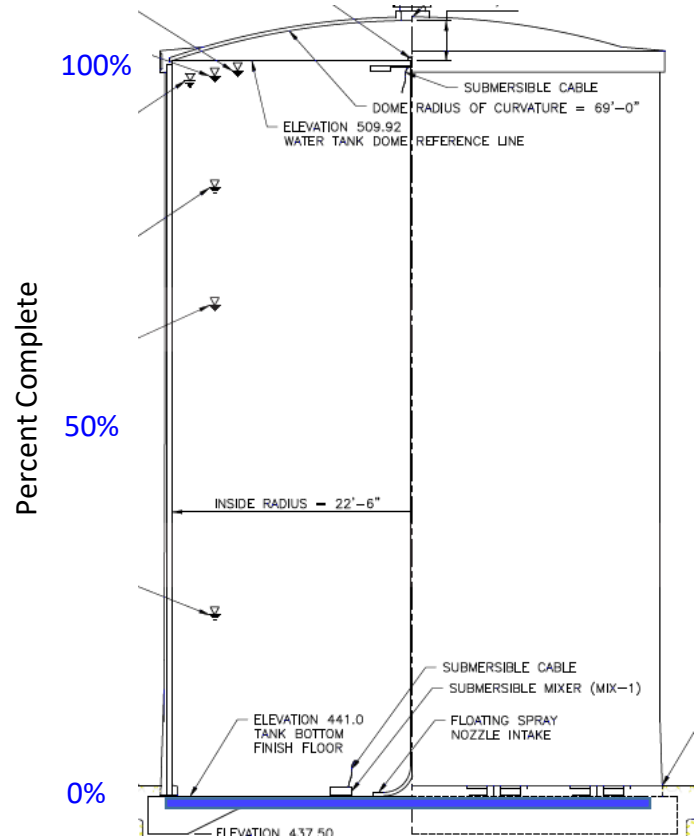




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

October 18, 2019

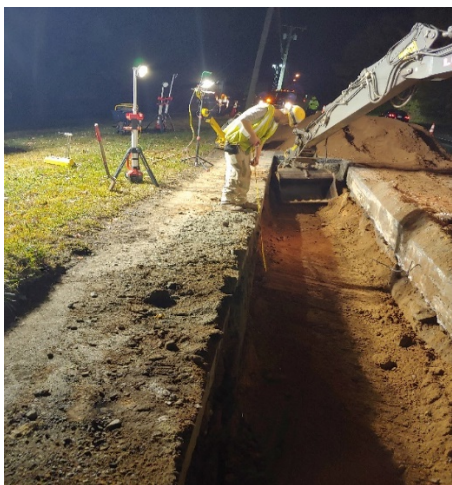

Backfilling pipe trench on South Main Street (Rt 17) in Middletown.



Installing 16" Ductile Iron Pipe on South Main Street (Rt 17) in Middletown.



Compaction Testing on South Main Street (Rt 17) in Middletown.
