



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

December 13, 2019

Work Accomplished Last Two Weeks

December 2, 2019 through December 6, 2019.

- ✓ Installed 24 LFT of 8" Ductile Iron Pipe (DIP) and Fire Hydrant on Parsons Lane, Durham.
- ✓ Installed 35 LFT of 8" DIP and Fire Hydrant on Little Lane, Durham.
- ✓ Installed Fire Hydrant at Station # 147+00 on Main Street, Durham.
- ✓ Started clearing the tank access road and tank site in Middletown.

December 9, 2019 through December 13, 2019.

- ✓ Pressure tested Talcott Ridge Drive, Middletown. Pressure test passed.

Work Planned for Next Week

December 16, 2019 through December 20, 2019.

- **No Excavation Activity – Winter Shut-Down.**
- Continue clearing tank access road and tank site.
- Start clearing Booster Station, Meter Vault and PRV Vault.
- Fill 16" DIP on Main Street (Rte. 17) in Middletown and Durham.

Work Accomplished During the 2019 Construction Season

- 16" DIP – Talcott Ridge Drive, Middletown: 2,016 LFT.
- 20" DIP – Talcott Ridge Drive, Middletown: 884 LFT.
- 16" DIP – South Main Street (Rte. 17), Middletown: 2,600 LFT.
- 8" DIP – Watch Hill Drive, Middletown: 648 LFT.
- 16" DIP – Main Street (Rte. 17), Durham: 3,408 LFT.
- Fire Hydrants installed – Middletown: 7
- Fire Hydrants installed – Durham: 5



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

December 13, 2019

Construction Schedule 2019 Construction Activities:

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south almost to Royal Oak Drive in Durham.
- Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown. This work will begin at the intersection with Route 17.
- Clearing of the Water Storage Tank Site in Middletown.
- Installation of the Pressure Relief Valve and Vault in Durham.

All remaining construction activities will occur in 2020 or 2021.


Mainline Water Line (28,272 feet total)

Start Date: September 8, 2019

Installed	
Feet	%
9,556	33.80

Ready for connection	
Feet	%
0	0.0%

Planned Work
Location/Limits

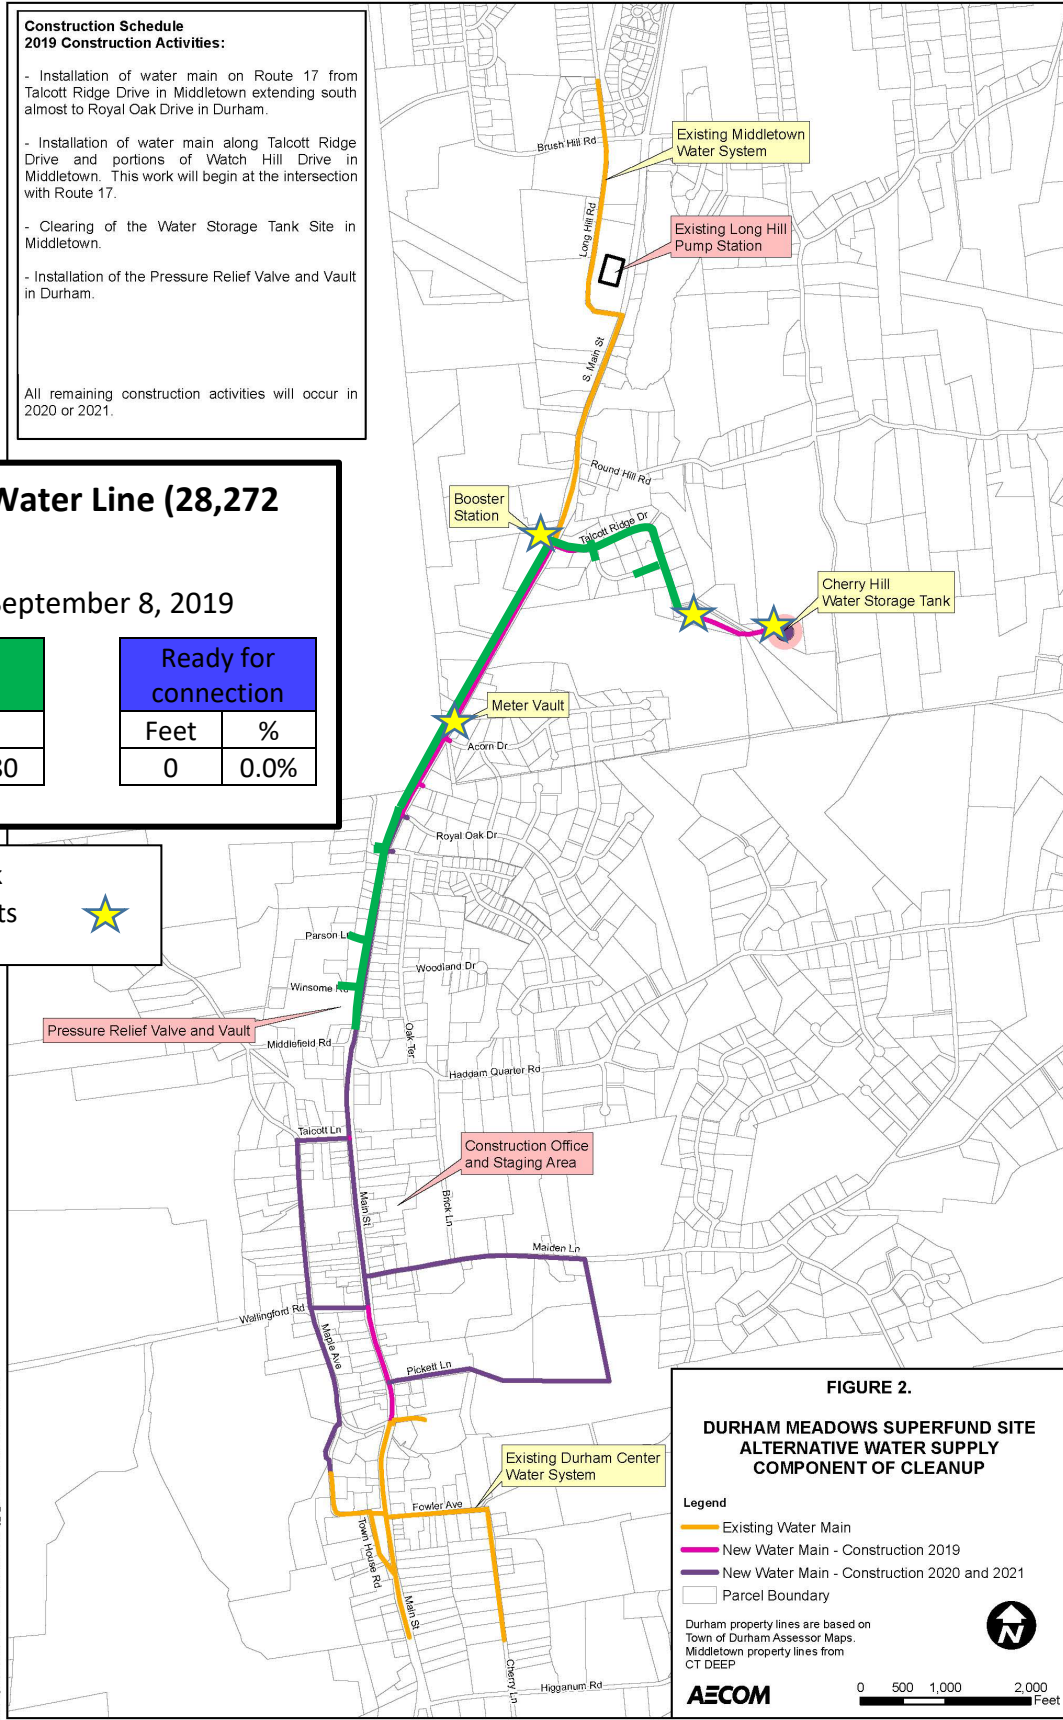



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

December 13, 2019


Curb Stops (211 total)

Start Date: August 24, 2020

Installed		Ready for connection	
Each	%	Each	%
0	0.0%	0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.



Homes Connected (115 total)


Start Date: October 27, 2020

Connected	
Homes	%
0	0.0%



Cherry Hill Tank Construction (72 feet)

Start Date: June 11, 2020

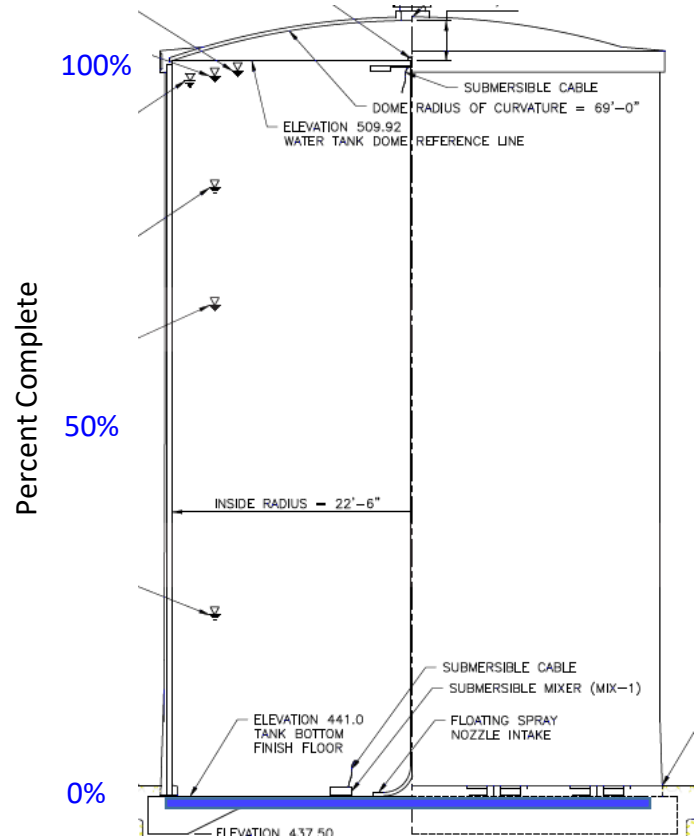



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

December 13, 2019



Installing 8" DI pipe Parsons Ln



Clearing Tank Site
