



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

July 31, 2020

Work Accomplished Last Two Weeks:

July 17, 2020 to July 31, 2020:

- Installed eighteen (18) water services main to curb stop on Main Street (Route 17) in Durham.
- Installed 178 LFT. of 12" Ductile Iron Pipe (DIP) in the stream crossing at Hersig Brook on Pickett Lane in Durham.
- Completed the installation of the stream crossing at Hersig Brook on Pickett Lane. Cleaned up and restored the stream slopes
- Installed 175 LFT. of 12" DIP on Pickett Lane between STA # 408+96.5 and STA # 410+71
- Installed 38 LFT. of 8" DIP on Brick Lane, Durham.
- Started the stream crossing on Maple Avenue in Durham and installed 62 LFT. of 12" DIP at the crossing.
- Replaced brick sidewalk at Allyn Brook on Pickett Lane in Durham.
- Pressure Tested 3,071 LFT. of 12" DIP from STA # 500+00 to STA # 530+71 on Pickett Lane in Durham.
- Pressure Tested 1,050 LFT. of 12" Dip from STA # 400+00 to STA # 410+50 on Maiden Lane in Durham.
- DN Tank began installation of the footing at the tank site in Middletown.

Work Planned for Next Two Weeks:

August 3, 2020 to August 7, 2020

- Continue installing water services on Main Street in Durham.
- Continue installing stream crossing on Maple Avenue in Durham.
- DN Tank to install footing at the tank site in Middletown.

August 10, 2020 to August 14, 2020

- Continue installing water services on Main Street in Durham.
- Begin installing 12" DIP on Maple Avenue in Durham.
- DN Tank to install flooring at the tank site in Middletown.




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

July 31, 2020

Figure 1: Water Main Installation Summary

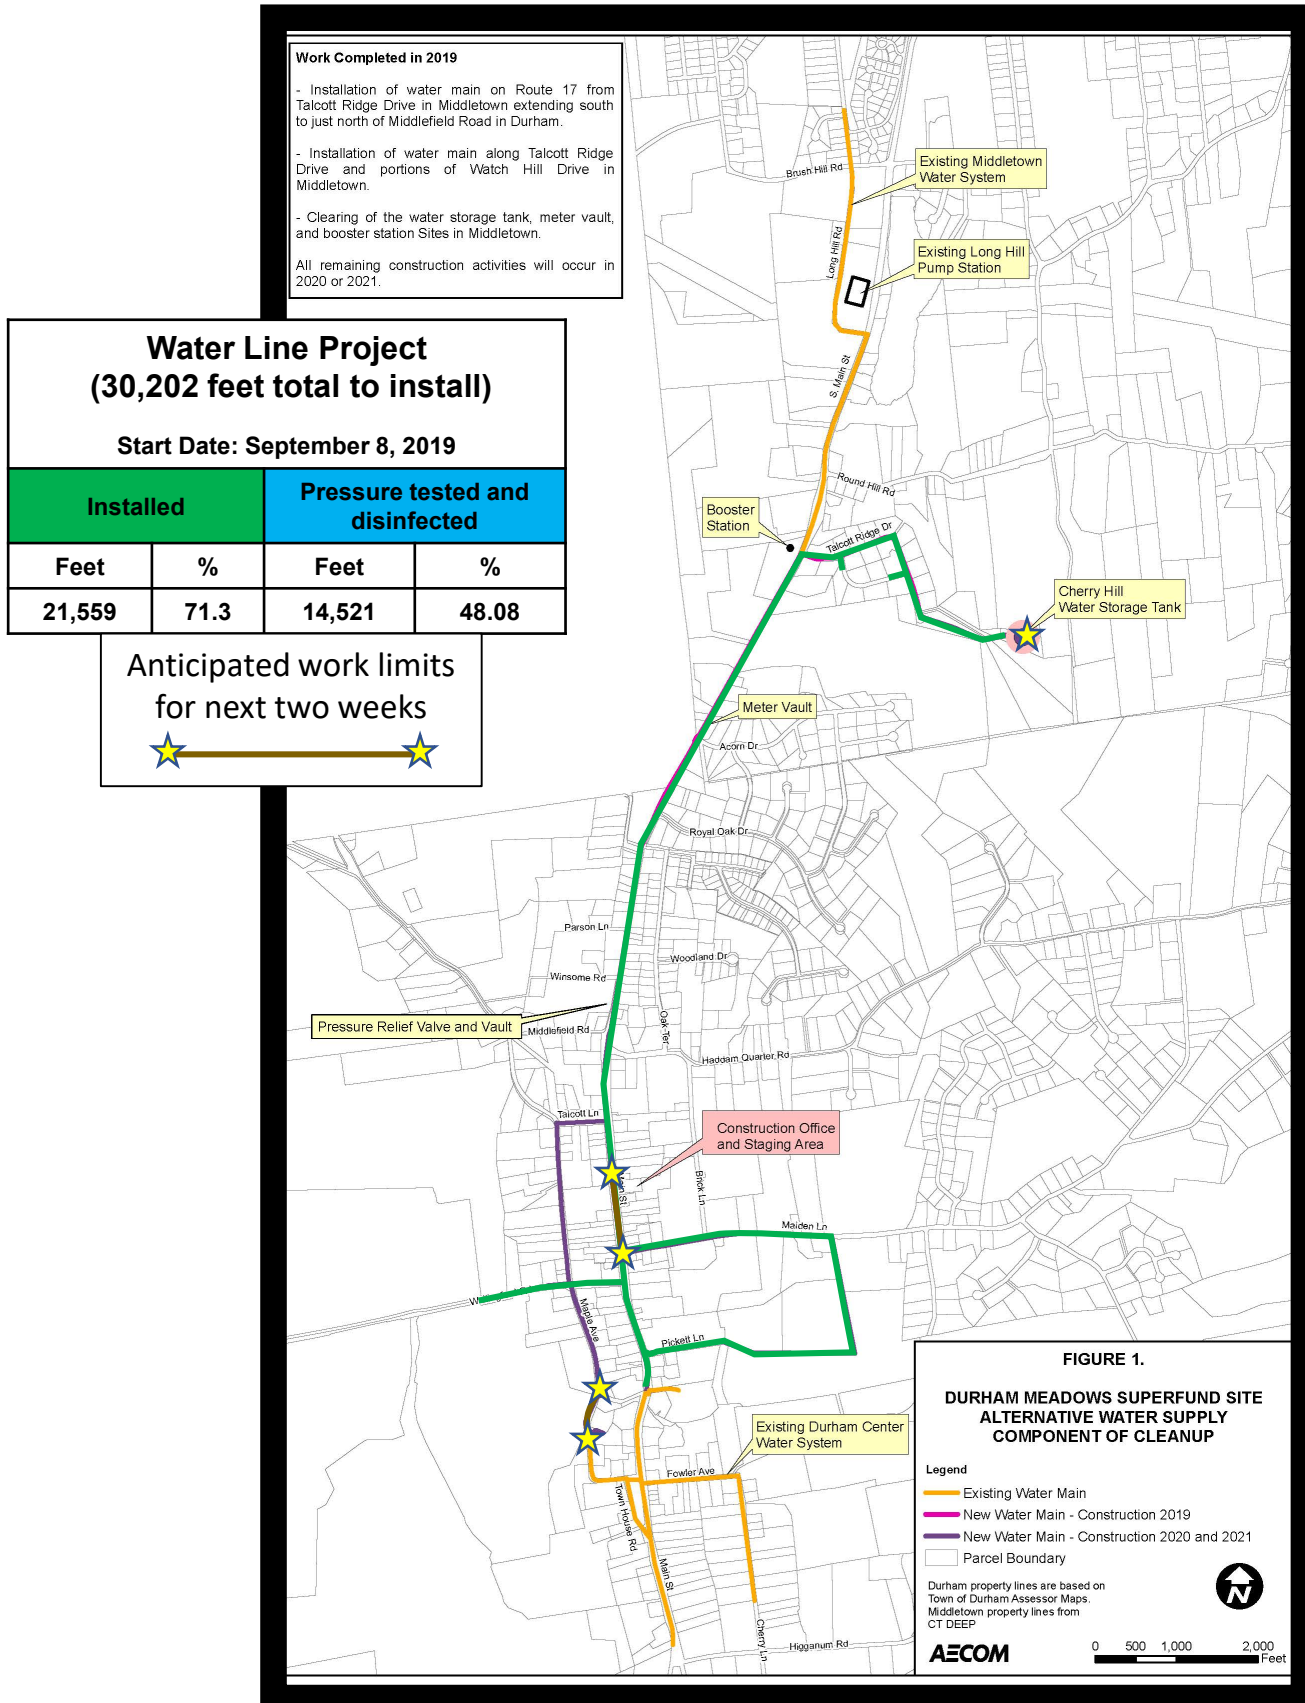



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

July 31, 2020


Figure 2: Curb Stop Installation Summary
Middletown

Curb Stops (17 total in Middletown)

Start Date: May 11, 2020

Installed		Pressure tested and disinfected	
Number	%	Number	%
17	100	0	0

Anticipated work limits
for next two weeks

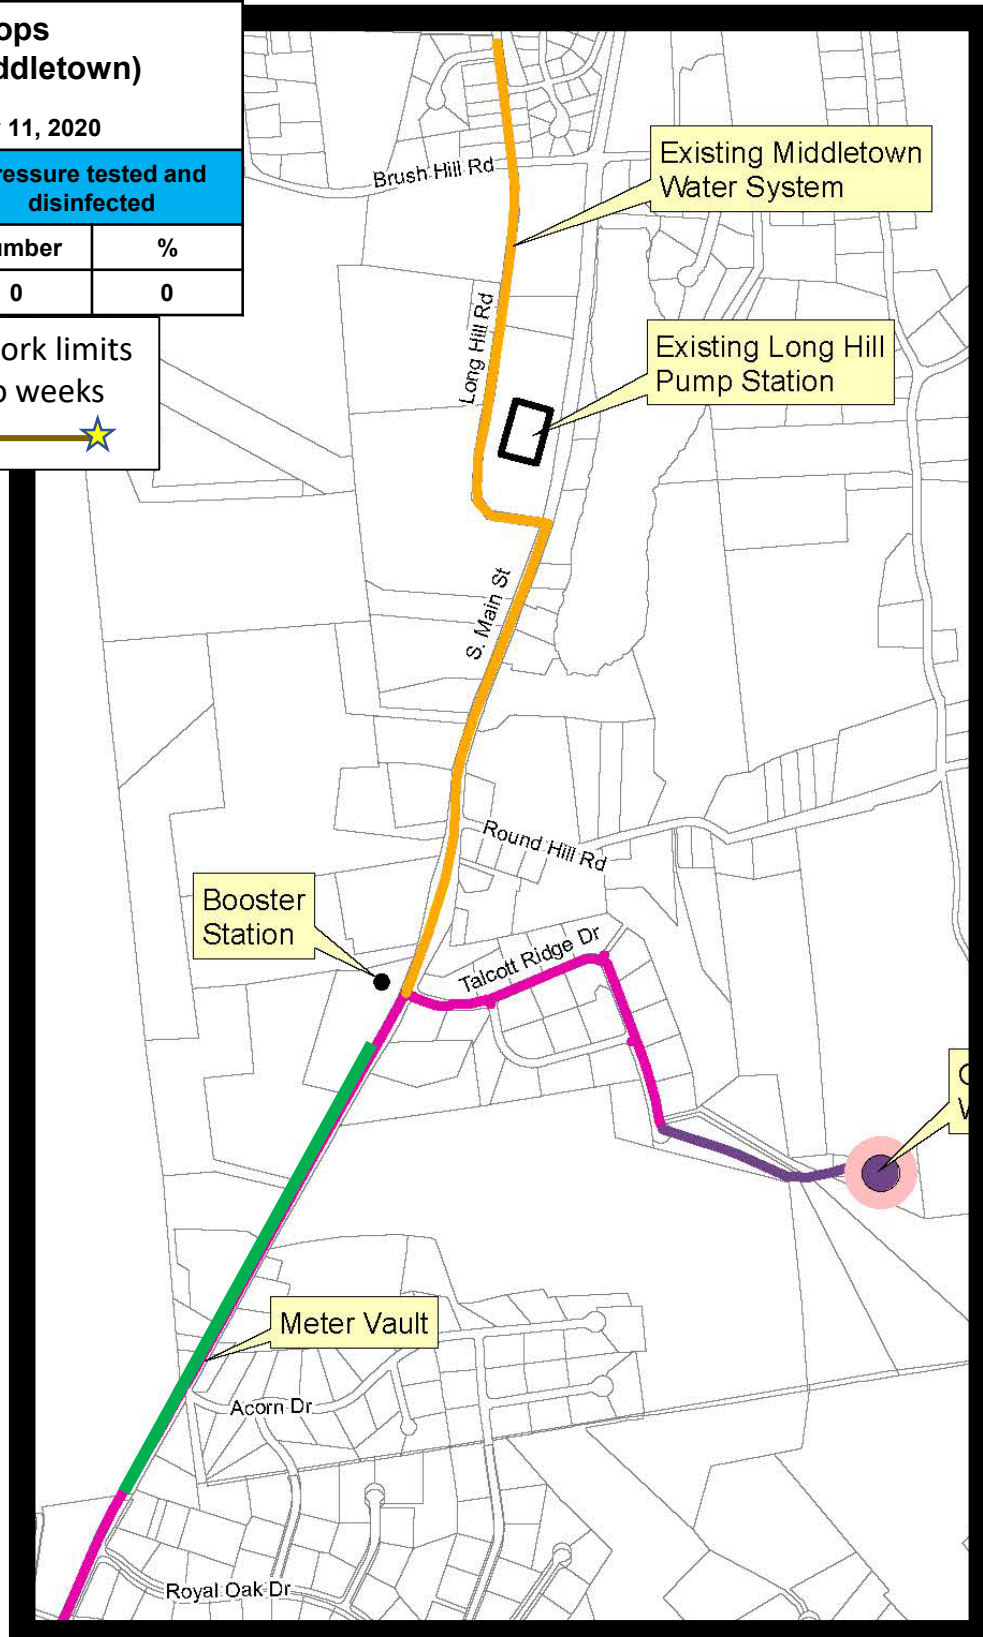




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

July 31, 2020

**Figure 3: Curb Stop Installation Summary
Durham**

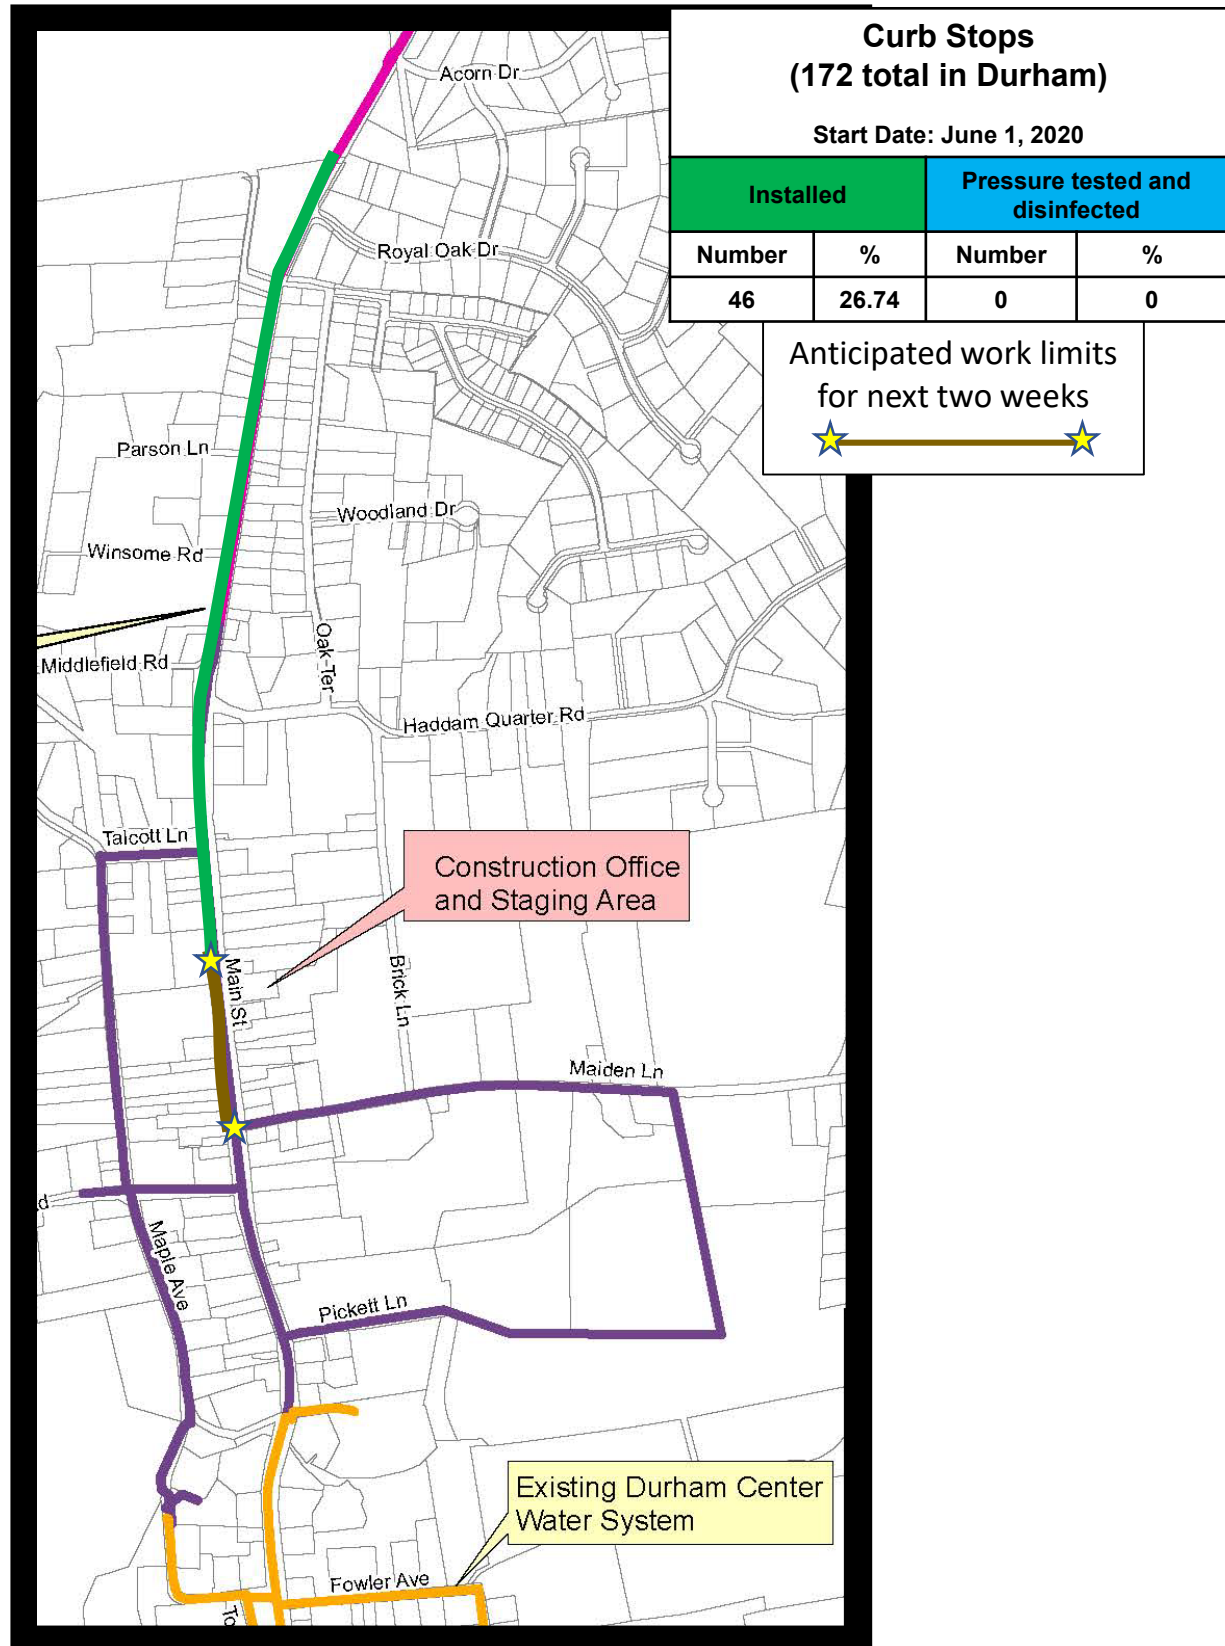




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

July 31, 2020

Figure 4: Full Service Connection Summary
Durham

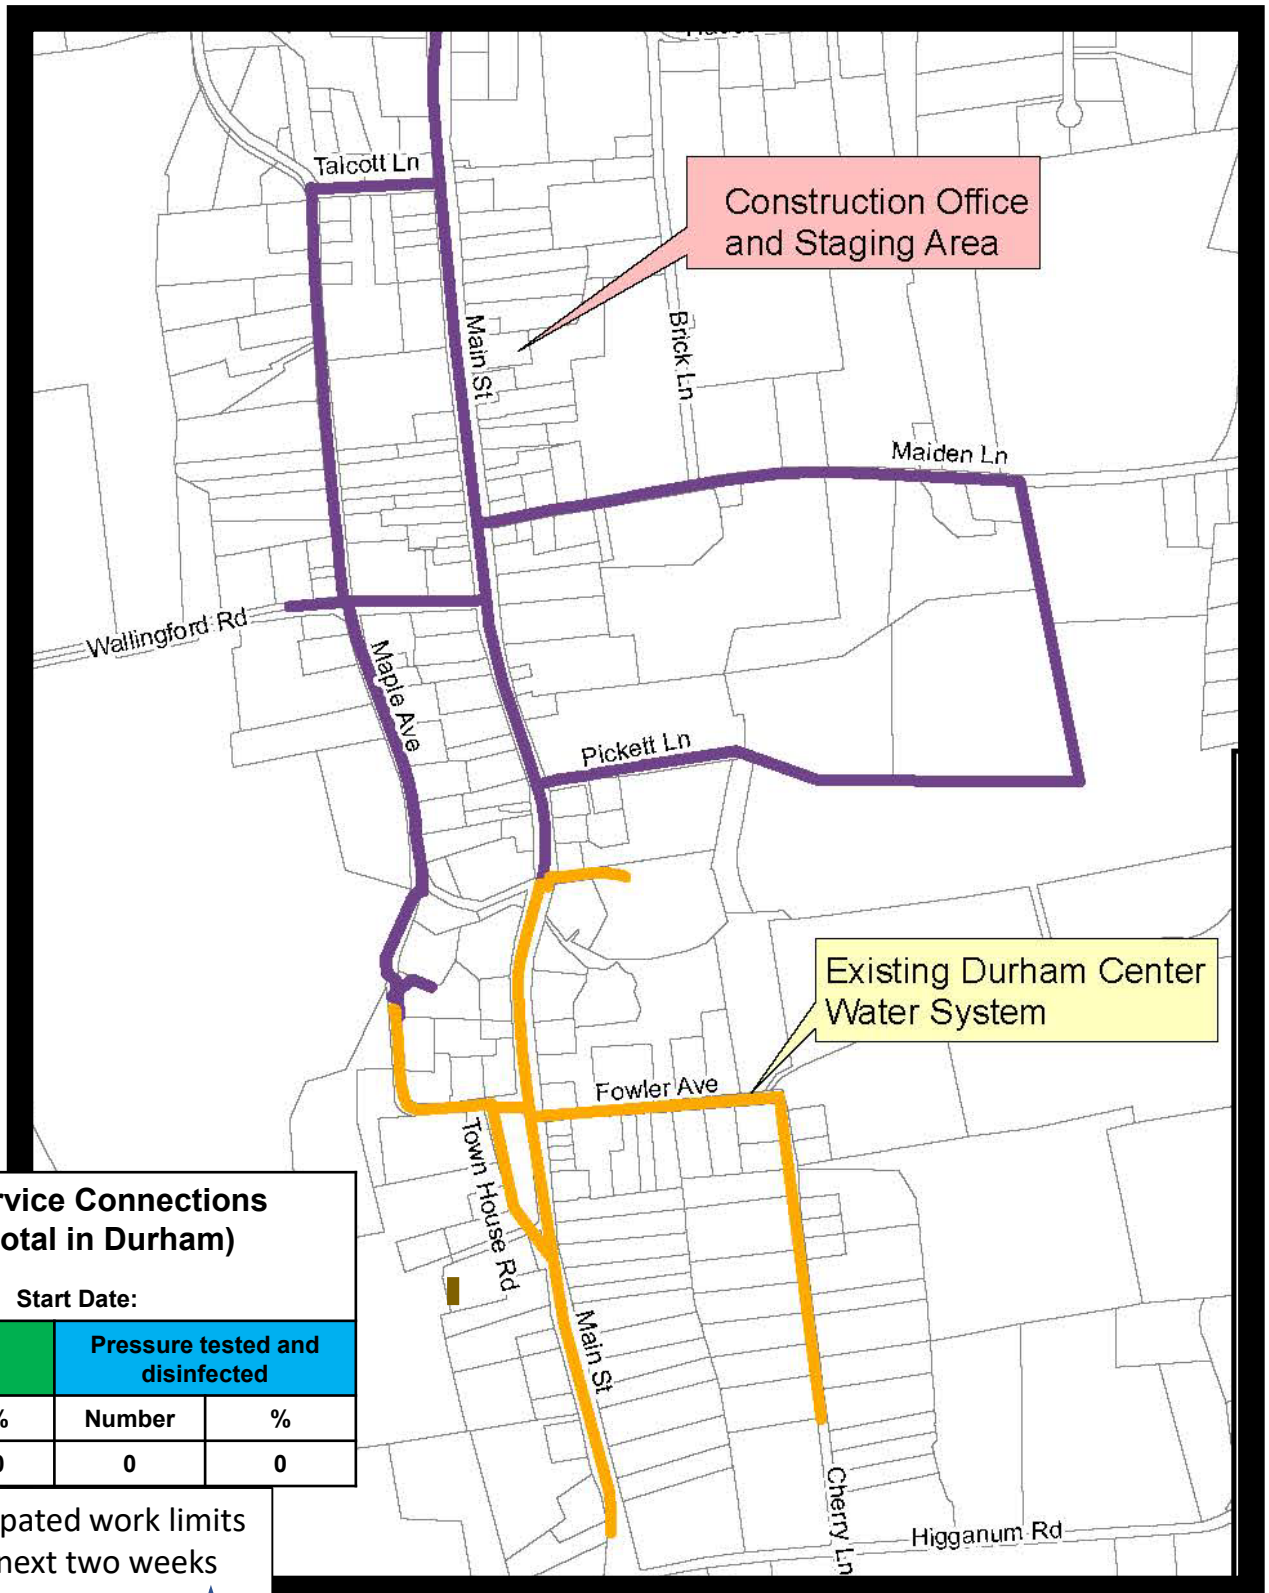



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

July 31, 2020

Water Tank Construction (72 Feet Height)

Start Date:

Installed

Feet of Tank Height
Completed

%

0


0

100%

Percent Complete

50%

0%

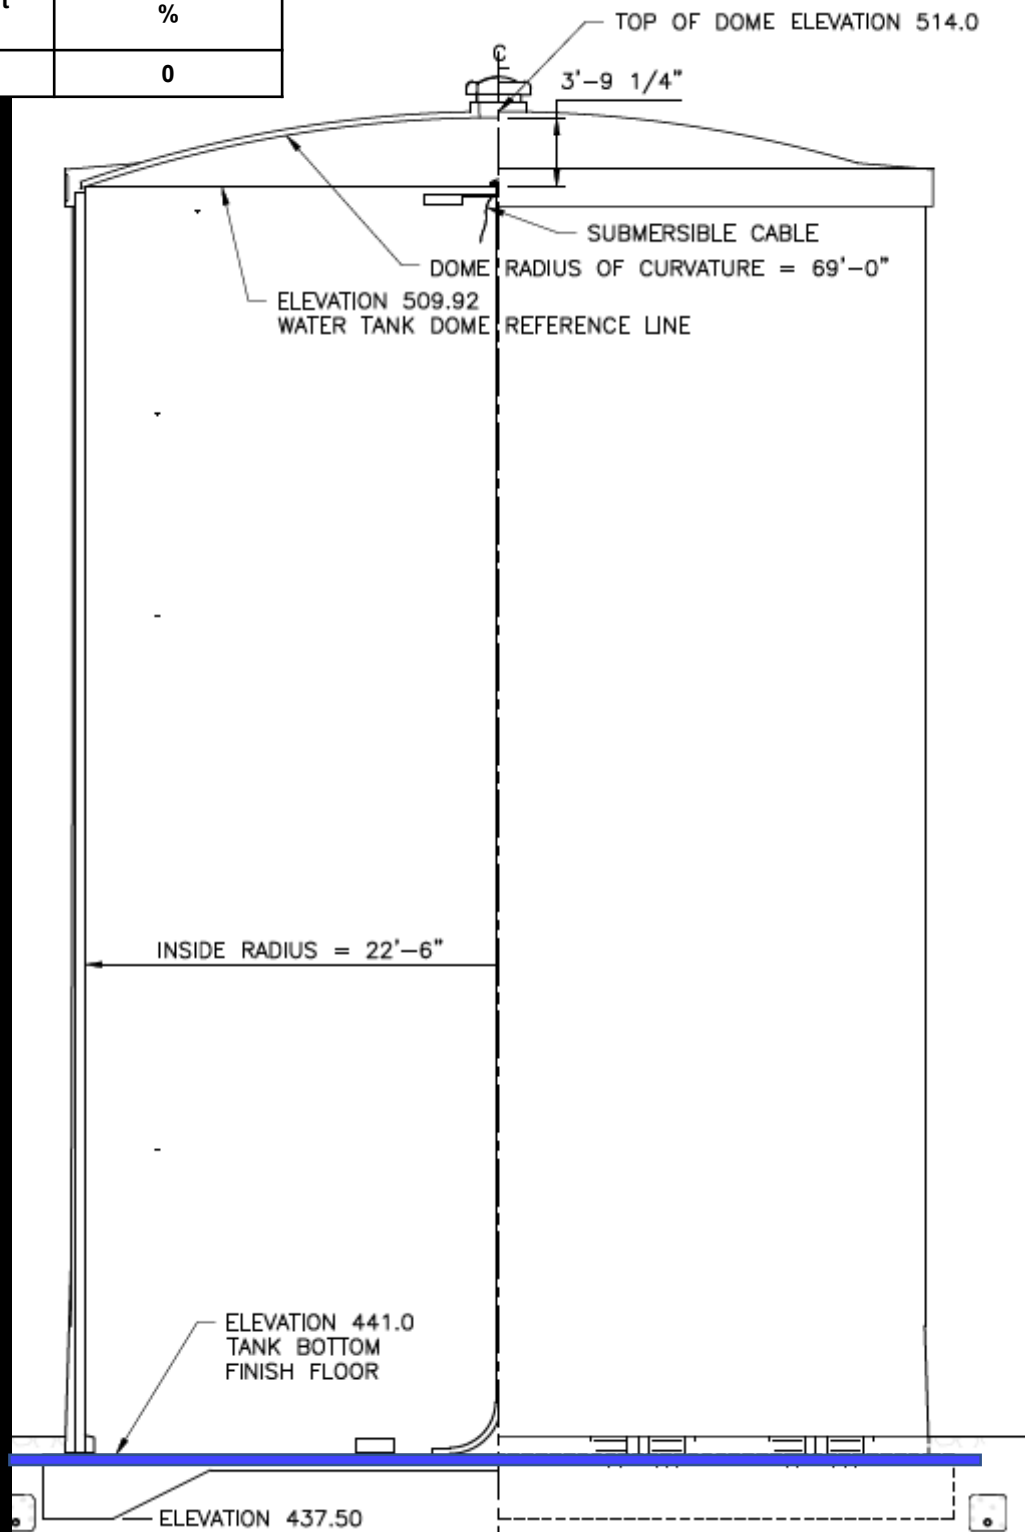



Bi-Weekly Progress Report
Durham Meadows Superfund Project, Durham & Middletown, CT
US Army Corps of Engineers Contract No. W912WJ19C0002
July 31, 2020



Maple Lane Stream Crossing



Tank Foundation
