



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

April 16, 2021

Work Accomplished to Date:

- Installed Altitude Vault at Tank Site
- Began Site Work at Booster Station
- Flushed and Chlorinated Water Main on Route 17 (Pending Lab Results)

Work Planned for Next Two Weeks:

April 19th, 2021- April 30th, 2021

- Connect Piping from Altitude Vault to Tank and 20" DIP (Ductile Iron Pipe) from Tank Access Road.
- Install Booster Footing and Foundation
- Flush and Chlorinate Maple Ave, Talcott Lane, and Wallingford Road (Route 68)



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

April 16, 2021

**Figure 1: Water Main Installation Summary
Middletown and Durham**

Water Line Project (30,202 feet total to install)

Start Date: September 8, 2019

Installed		Pressure tested and disinfected	
Feet	%	Feet	%
29,430	98	14,521	48

Completed Waterline




Remaining Waterline to be installed



Wells (128 total)

Start Date: TBD

Abandoned		Converted to Monitoring Well	
Number	%	Number	%
0/125	0	0/3	

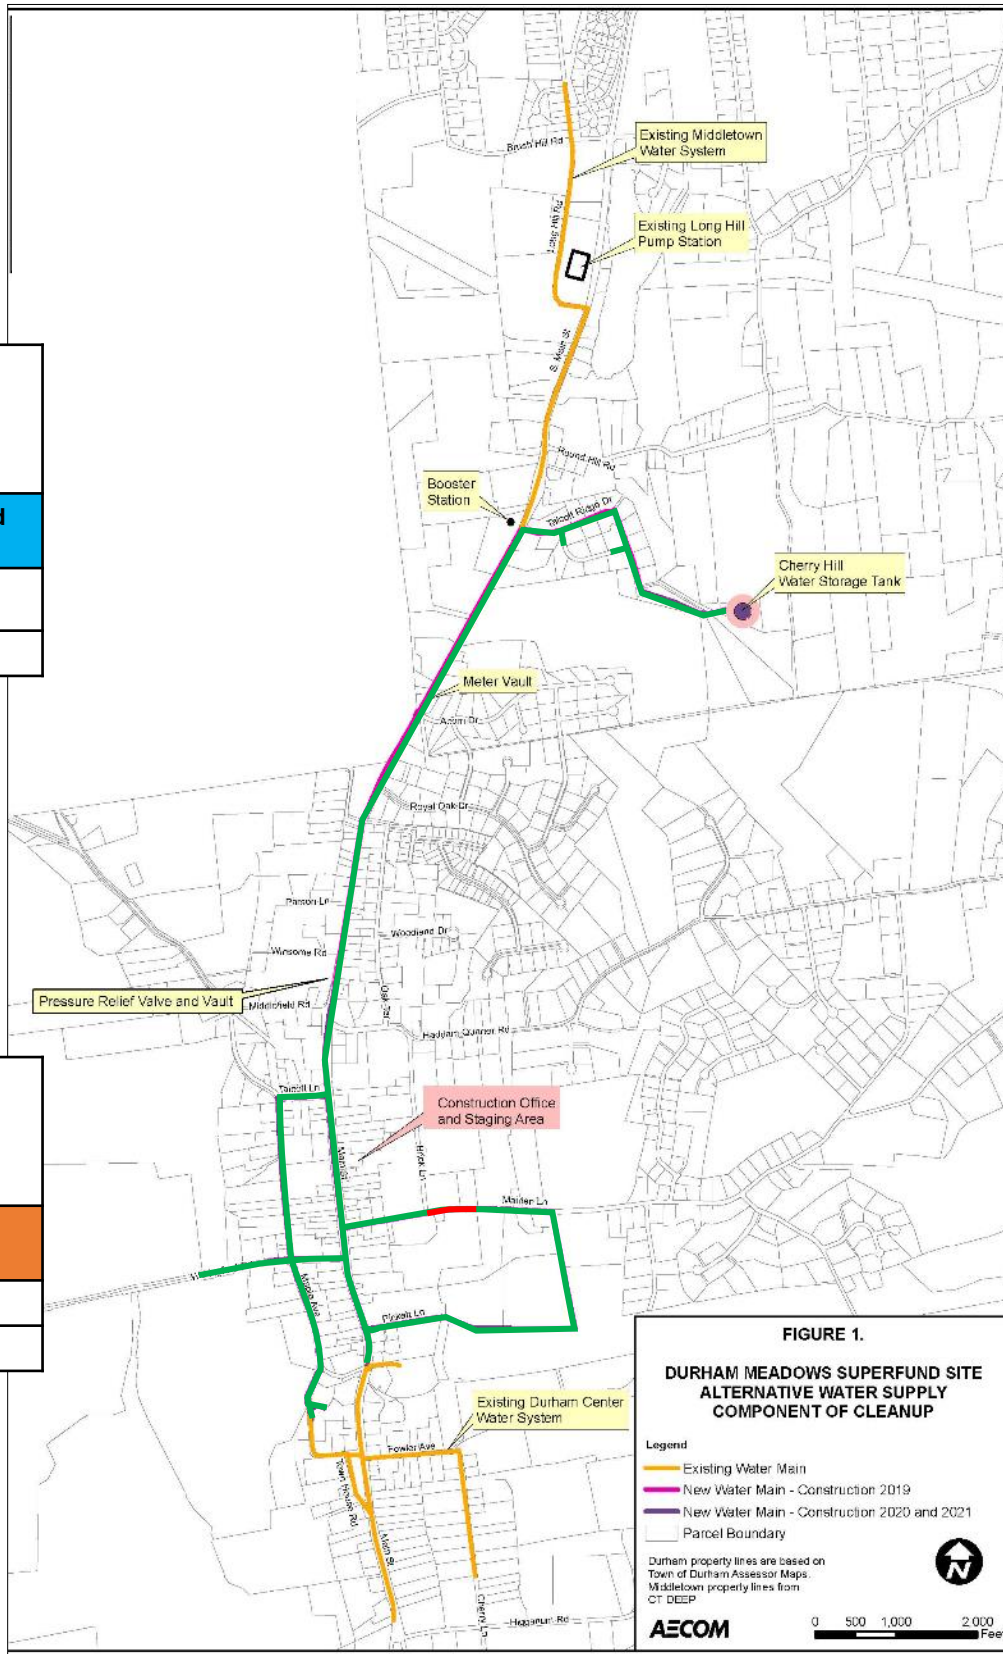




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

April 16, 2021

Figure 2: Full-Service Connection Summary
Durham

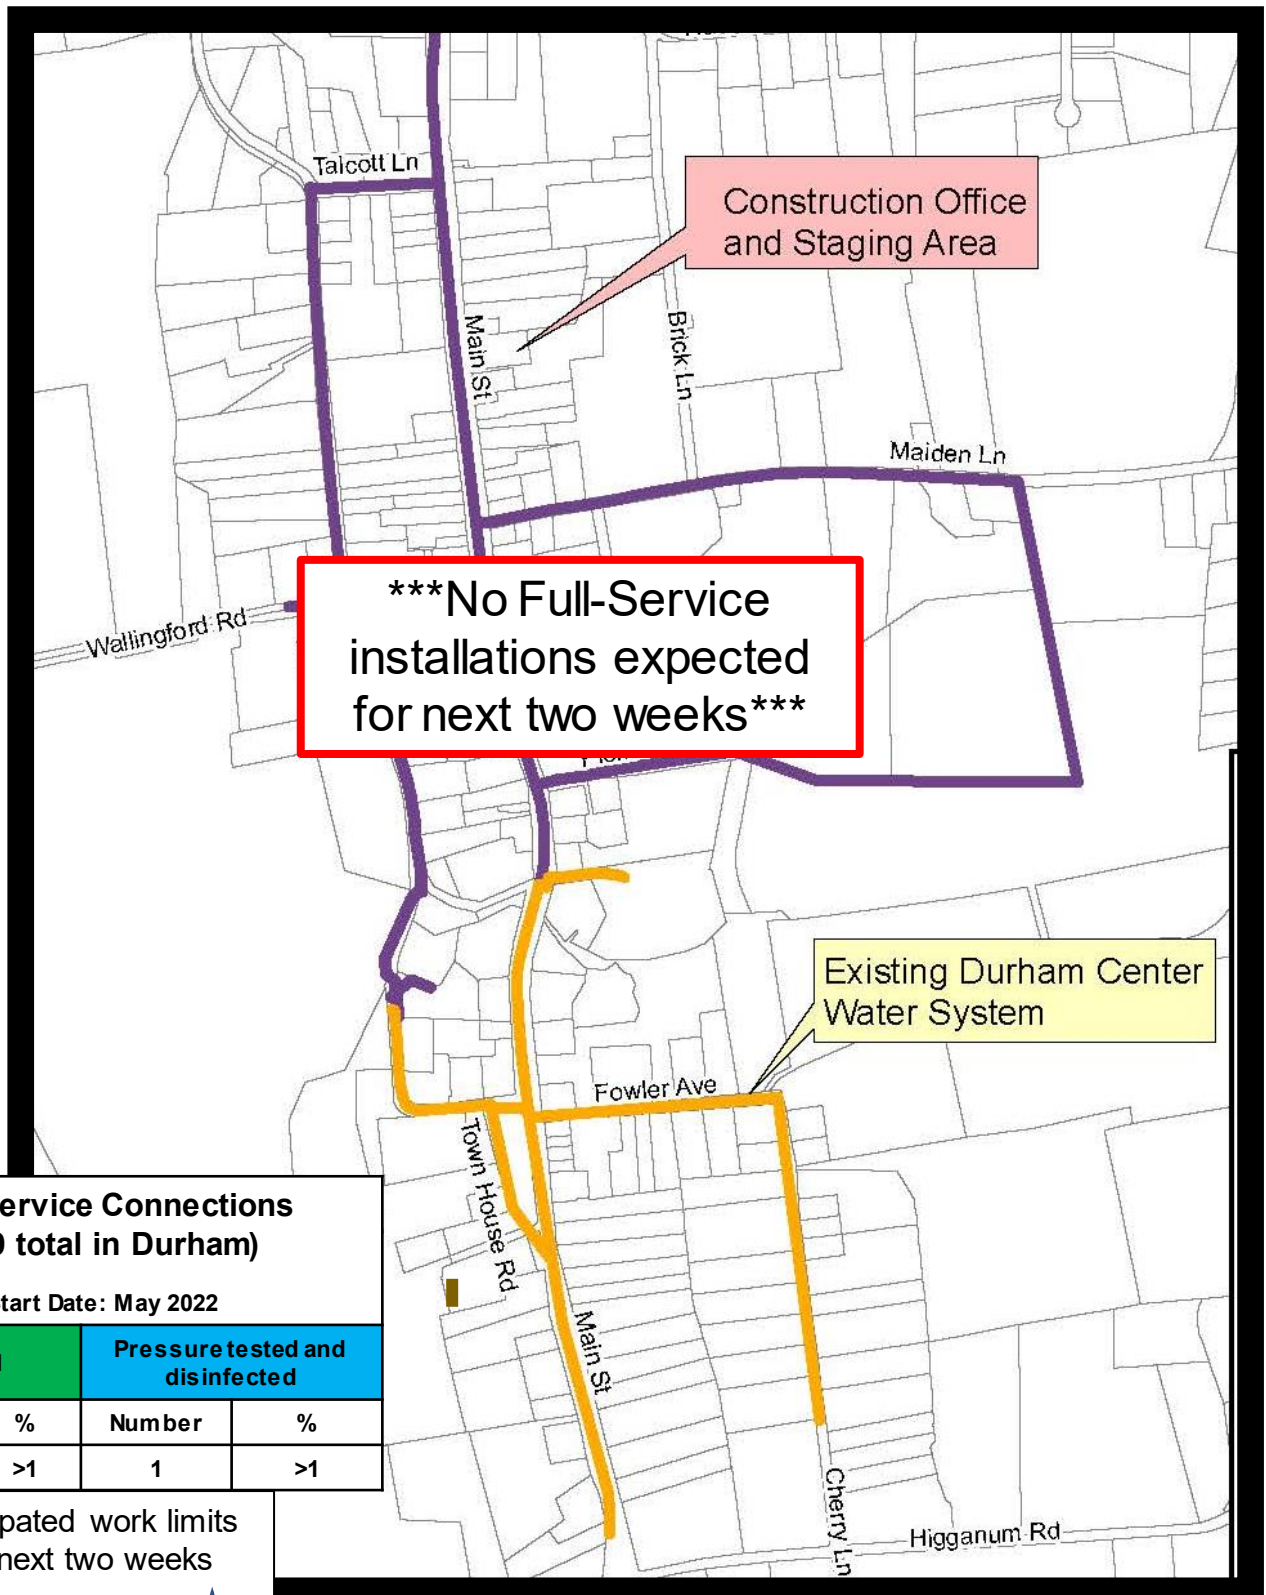

Full Service Connections (119 total in Durham)

Start Date: May 2022

Installed		Pressure tested and disinfected	
Number	%	Number	%
1	>1	1	>1




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

April 16, 2021

Figure 3: Main Structure Summary
Middletown and Durham

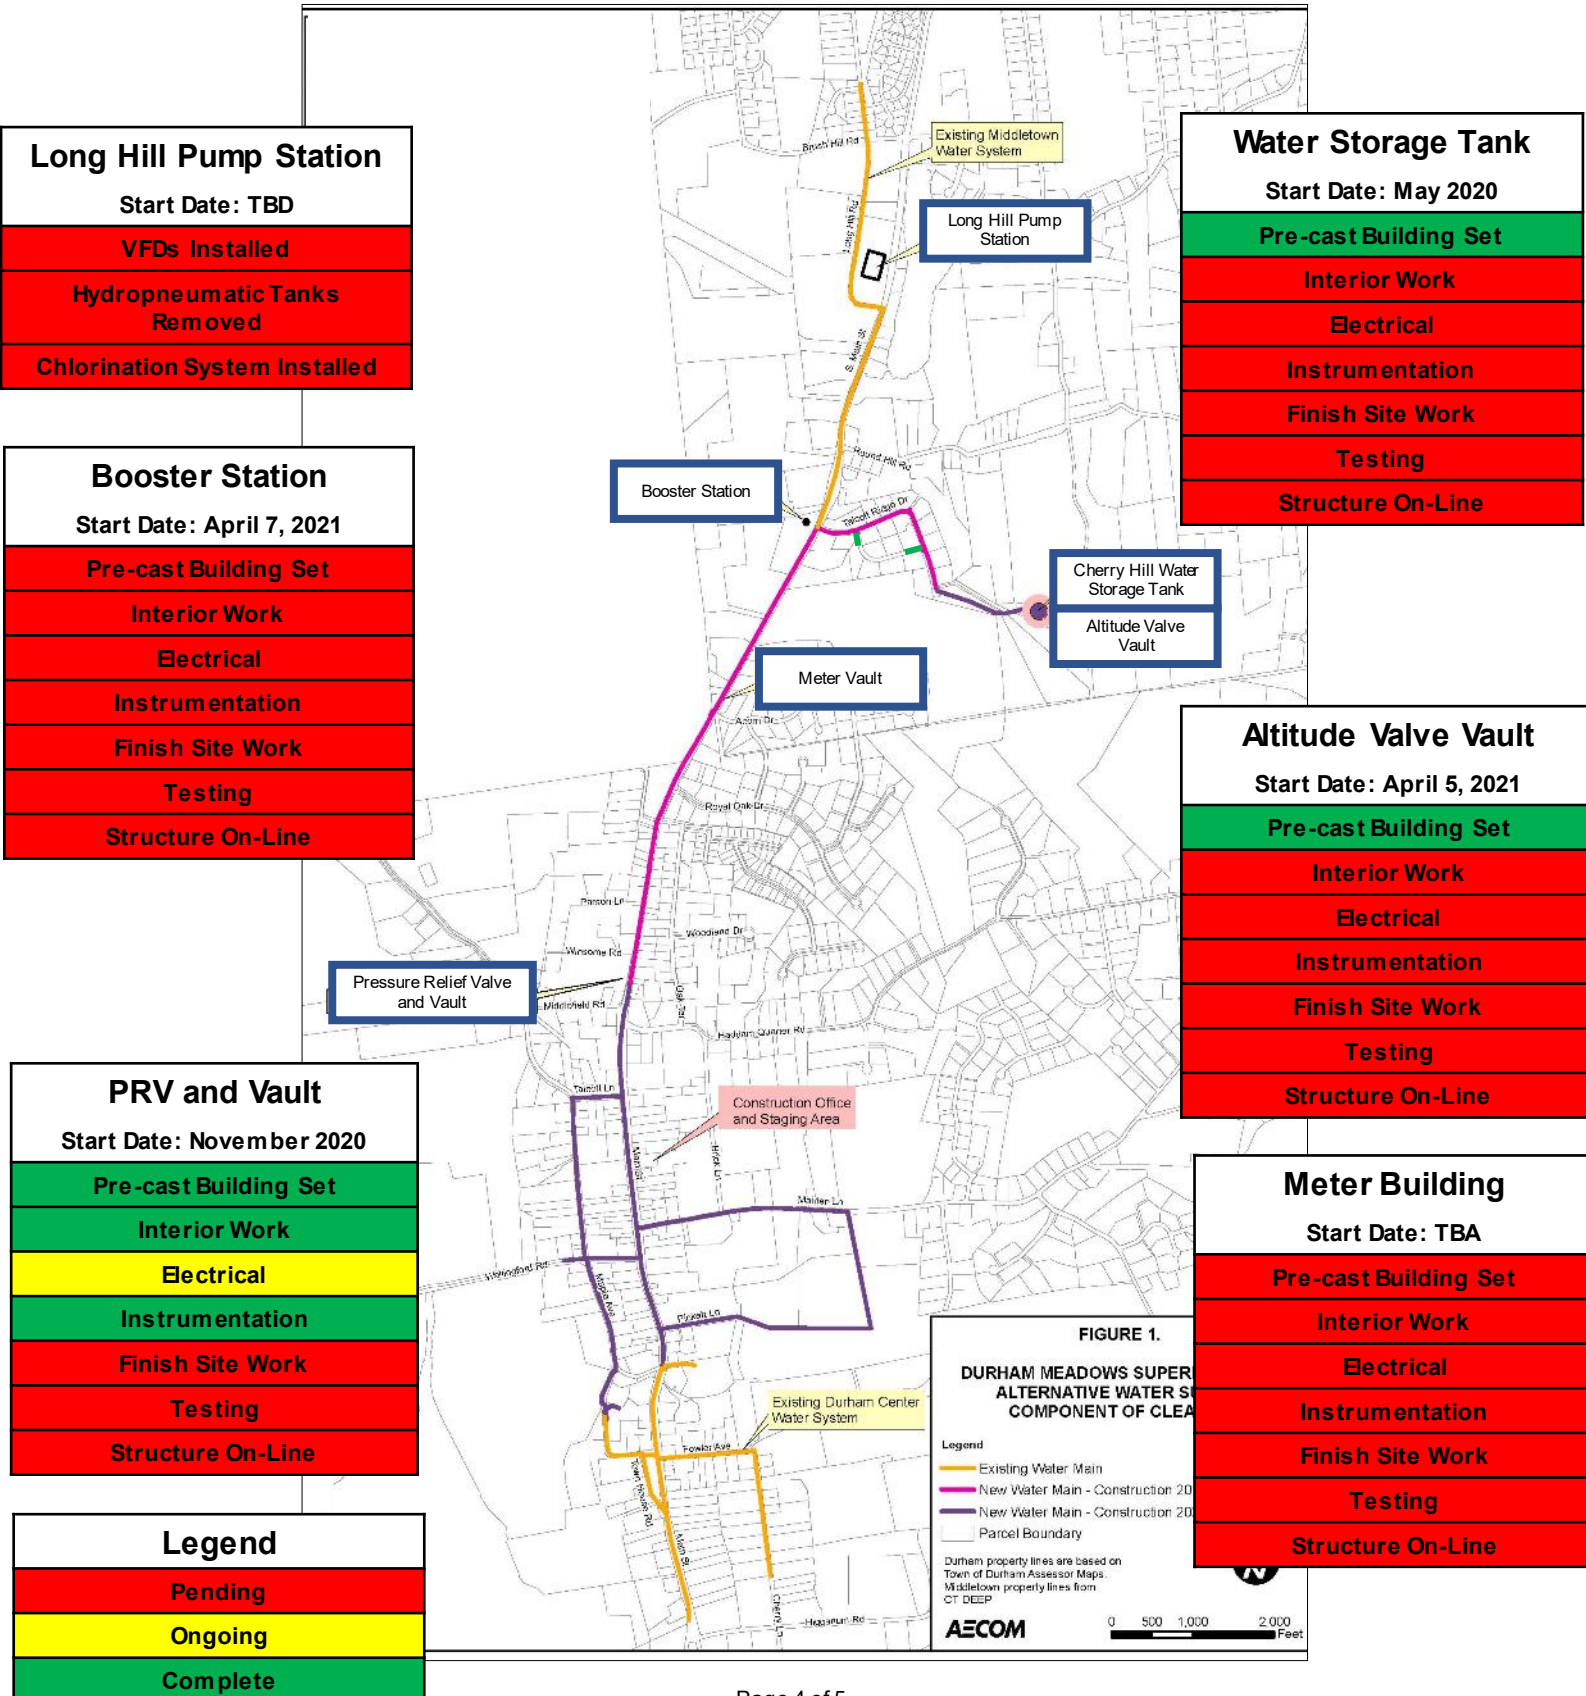



Bi-Weekly Progress Report
Durham Meadows Superfund Project, Durham & Middletown, CT
US Army Corps of Engineers Contract No. W912WJ19C0002
April 16, 2021



Altitude Vault Installation at Cherry Hill Water Storage Tank
