

Daily Report

Project:	Durham Meadows Pipeline Installation
Location:	South Main Street, Middletown CT
Project #:	AECOM: 60445033
Contractor:	Ludlow Construction

Date:	October 27, 2019
Day of Week:	Sunday
Report No:	18
Page:	1 of 8

Weather Conditions

Conditions:	Night			
Temperature (°F):	High	58°F	Low	50°F

[illegible]

Summary of Work

Visitors:

Notes:

- Starting from Sta. 131+35

1900 – on site

1915 – cones placed

1950 – trenching for first section

2025 – 1st section in

- Placing, compacting pipe bedding and laying warning tape

2100 – 2nd section in

- Placing, compacting pipe bedding and laying warning tape

2105 – support in place for 3rd section

2115 – compaction testing 1st lift over 1st section

2120 – 3rd section in

- Placing, compacting pipe bedding and laying warning tape

2125 – trenching for 4th section

- Placing 1st backfill lift over 3rd section

|2140 – 4th section in

- Placing, compacting pipe bedding and laying warning tape

- Placing 2nd backfill lift over sections 1-3

2200 – trenching for 5th, 6th sections

2225 – 5th section attached

- 15' section preceding 6" valve section (16" butterfly valve, Tee section with gate valve, 16" butterfly valve)
- Placing, compacting pipe bedding and laying warning tape

Res. Representative:

F. Grimberg

Date: 10/27/19

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 27, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Sunday
Project #:	AECOM: 60445033	Report No:	18
Contractor:	Ludlow Construction	Page:	2 of 8

2250 – valve section in trench, leveling
2255 – attaching valve section
2300 – leaving site

Payment Items:

Res. Representative:

F. Grimberg

Date: 10/27/19

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 27, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Sunday
Project #:	AECOM: 60445033	Report No:	18
Contractor:	Ludlow Construction	Page:	3 of 8



Figure 1 – Stone bedding pile at Sta. 135+50

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 27, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Sunday
Project #:	AECOM: 60445033	Report No:	18
Contractor:	Ludlow Construction	Page:	4 of 8



Figure 2 –Backfill pile at Sta. 131+35

Daily Report

Project: Durham Meadows Pipeline Installation
Location: South Main Street, Middletown CT
Project #: AECOM: 60445033
Contractor: Ludlow Construction

Date: October 27, 2019
Day of Week: Sunday
Report No: 18
Page: 5 of 8



Figure 3 – Compacting 2nd fill lift over sections 1-3

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 27, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Sunday
Project #:	AECOM: 60445033	Report No:	18
Contractor:	Ludlow Construction	Page:	6 of 8

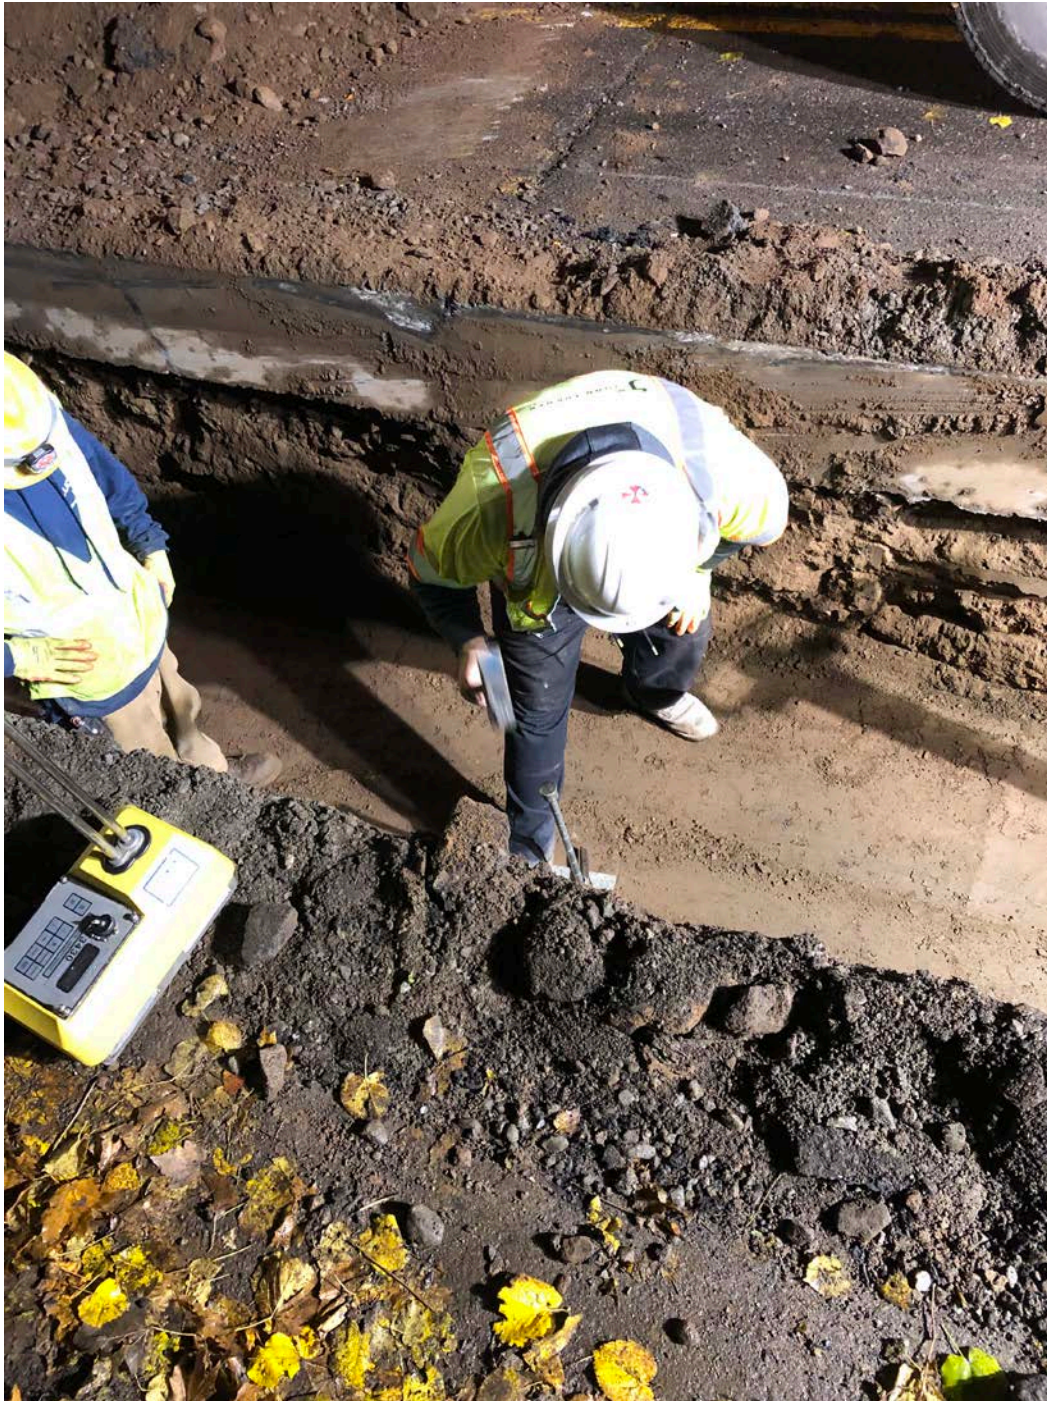


Figure 4 – Compaction testing 2nd fill lift over section 2

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 27, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Sunday
Project #:	AECOM: 60445033	Report No:	18
Contractor:	Ludlow Construction	Page:	7 of 8



Figure 5 – Valve section to be placed at Sta. 132+30

Daily Report

Project: Durham Meadows Pipeline Installation
Location: South Main Street, Middletown CT
Project #: AECOM: 60445033
Contractor: Ludlow Construction

Date: October 27, 2019
Day of Week: Sunday
Report No: 18
Page: 8 of 8

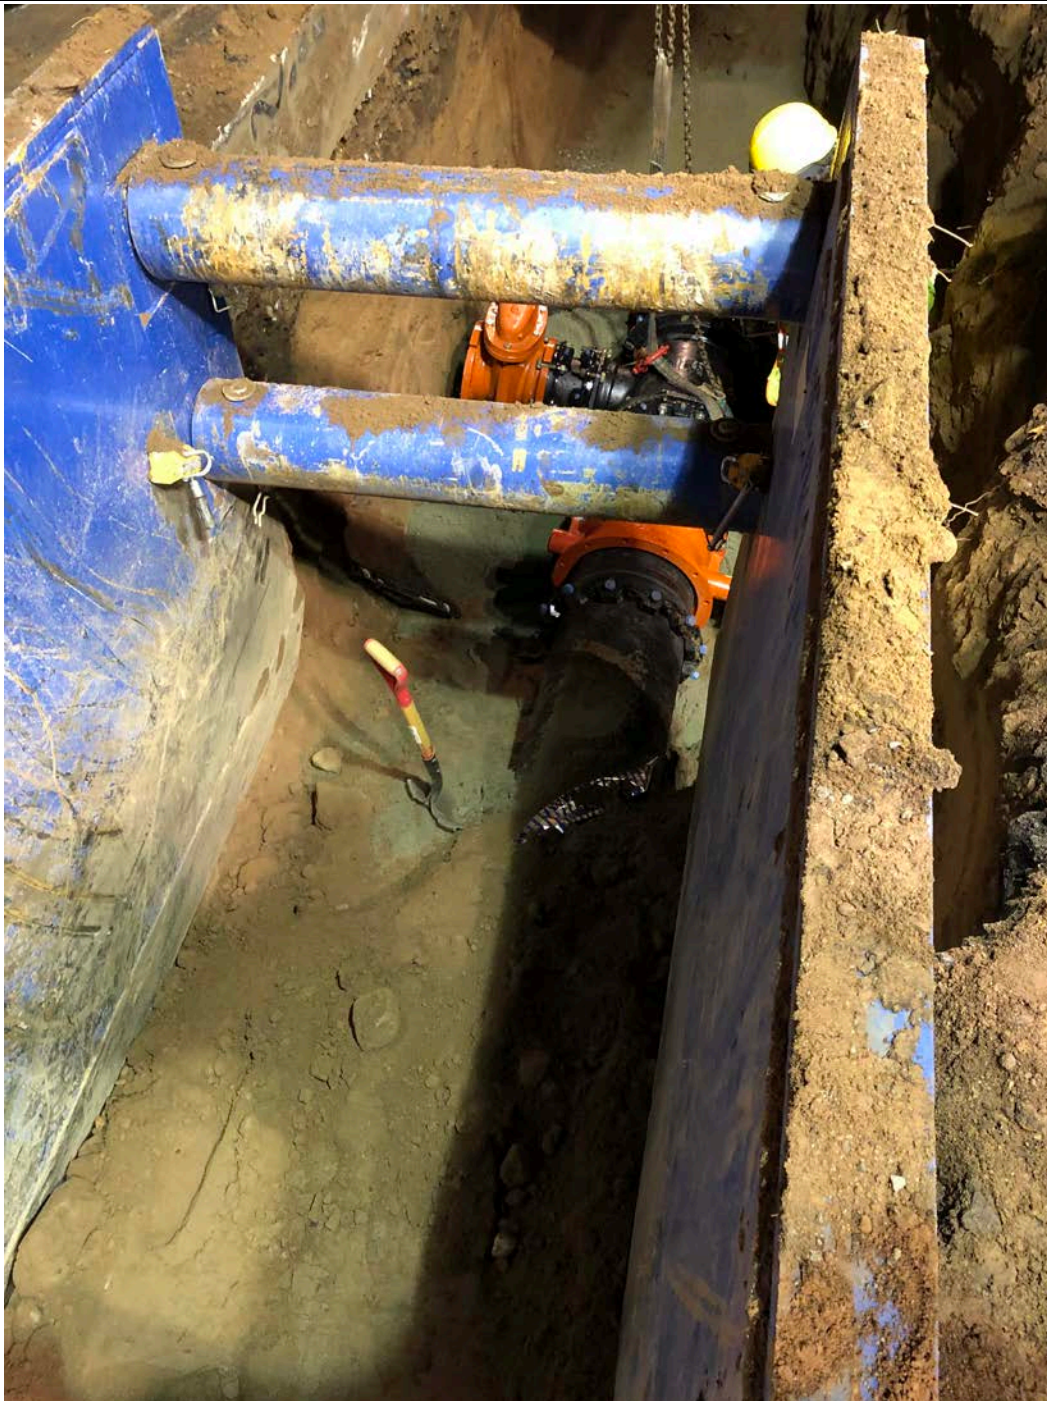


Figure 6 – Valve section in place at Sta. 132+30
