

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 7

### Weather Conditions

**Conditions:** Night  
**Temperature (°F):** High 40°F Low 32°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	x	hrs
				Ludlow Construction			
				Superintendent	1	x	8
				Safety Officer	1	x	8
HDR (representing USACE)				Dump truck Operator	3	x	8
Field Engineer	1	x	8	Excavator Operator	1	x	8
				Skid Steer Operator	1	x	8
				Laborers	4	x	8
				Sub-contractor			
				Dump truck Operator	1	x	8
				Flaggers	2	x	8
				Compression tester	1	x	8
				Middletown Police Dept.			
				Traffic officer			

### Summary of Work

**Visitors:**

**Notes:**

- Starting from Sta. 157+08
- Using graded backfill

1900 - on site  
 1920 - breaking ground  
 1945 - 1st pipe section installed  
 - Placing, compacting pipe bedding and laying warning tape  
 2000 - 2nd pipe section installed  
 - Placing, compacting pipe bedding and laying warning tape  
 2030 - Tee installed  
 - Attaching valve box sections to valve at tee  
 - Placing, compacting backfill  
 2100 - laying first backfill layer over pipe sections 1-2  
 2110 - 3rd pipe section installed  
 - Placing, compacting pipe bedding and laying warning tape  
 2130 - compacting backfill  
 2140 - 4th pipe section installed  
 - Placing, compacting pipe bedding and laying warning tape  
 2200 - placing 2nd backfill lift over tee section  
 2210 - 5th pipe section installed  
 - Placing, compacting pipe bedding and laying warning tape  
 2230 - 6th pipe section installed  
 - Placing, compacting pipe bedding and laying warning tape

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 7

2245 - 7th pipe section installed  
- Placing, compacting pipe bedding and laying warning tape  
2300 – break time  
- Leaving site now

**Payment Items:**

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 7



Figure 1 – Pile of graded backfill at Sta. 157+08

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 7



Figure 2 – Tee section in trench, attached to water main

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 7



Figure 3 – Compacting backfill lift

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 7



Figure 4 – Backfill pile

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 20, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	32
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	7 of 7

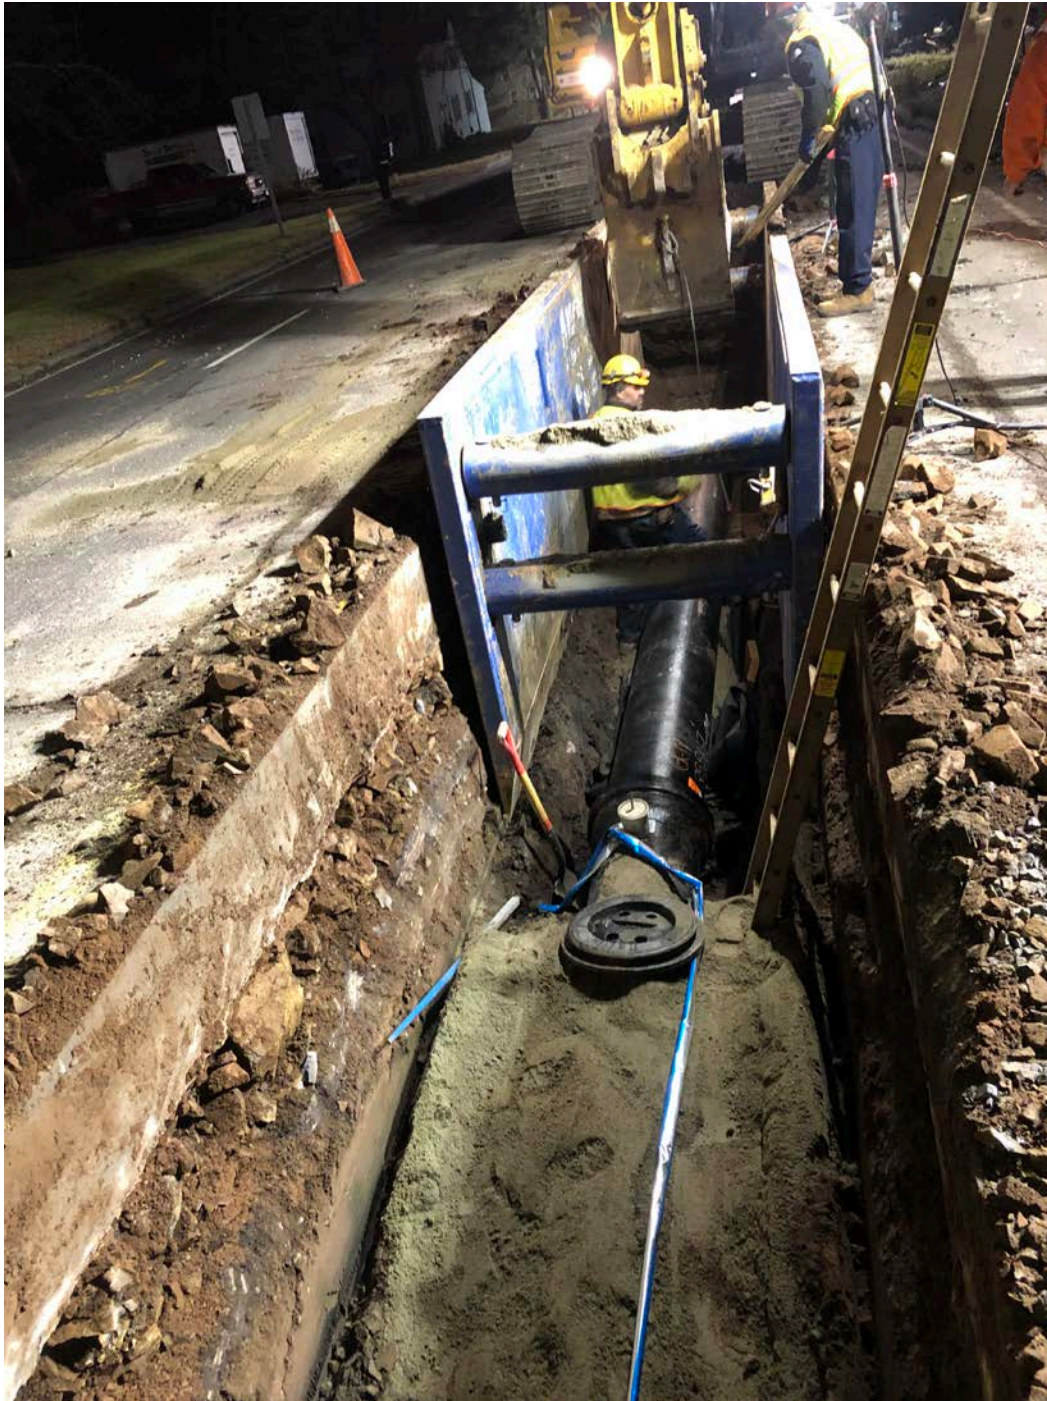


Figure 5 – Placing 5<sup>th</sup> pipe section
