

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 7

### Weather Conditions

**Conditions:** Night  
**Temperature (°F):** High 55°F Low 45°F

### Contractors & Subcontractors Workforce

Trade	#	x	hrs
Ludlow Construction			
Superintendent	1	x	8
Safety Officer	1	x	8
Dump truck Operator	3	x	8
Excavator Operator	1	x	8
Skid Steer Operator	1	x	8
Laborers	4	x	8
Sub-contractor			
Dump truck Operator	1	x	8
Flaggers	2	x	8
Compaction tester	1	x	8
Middletown Police Dept.			
Traffic officer			

### Equipment in Use

Type	#	x	hrs
Dump truck	4	x	8
Excavator	1	x	8
Skid Steer Loader	1	x	8
Plate Compactor	1	x	8
Jumping Jack Compactor	1	x	8
Light Tower	3	x	8
Mid-size Excavator	1	x	8

### Summary of Work

#### Visitors:

#### Notes:

- Starting from Sta. 139+52
  - Using 3 minus backfill again
- 1900 – on site  
 1930 – breaking ground  
 1950 – 1<sup>st</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 2010 – 2<sup>nd</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 2030 – 3<sup>rd</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 2045 – 4<sup>th</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 - Laying first fill lift over 1-3  
 2105 – 5<sup>th</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 2120 – compacting 2<sup>nd</sup> backfill lift over pipe lengths 1-4  
 2126 – 6<sup>th</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 2210 – stone bedding laid under 7<sup>th</sup> section  
 2215 – 7<sup>th</sup> section in  
 - Placing, compacting pipe bedding and laying warning tape  
 2240 – cutting 8<sup>th</sup> section

**Res. Representative:**

F. Grimberg

**Date:** 11/4/19

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 7

2250 – 8<sup>th</sup> section in  
- Lunch time  
- Leaving site

**Payment Items:**

**Res. Representative:**

F. Grimberg

**Date:** 11/4/19

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 7

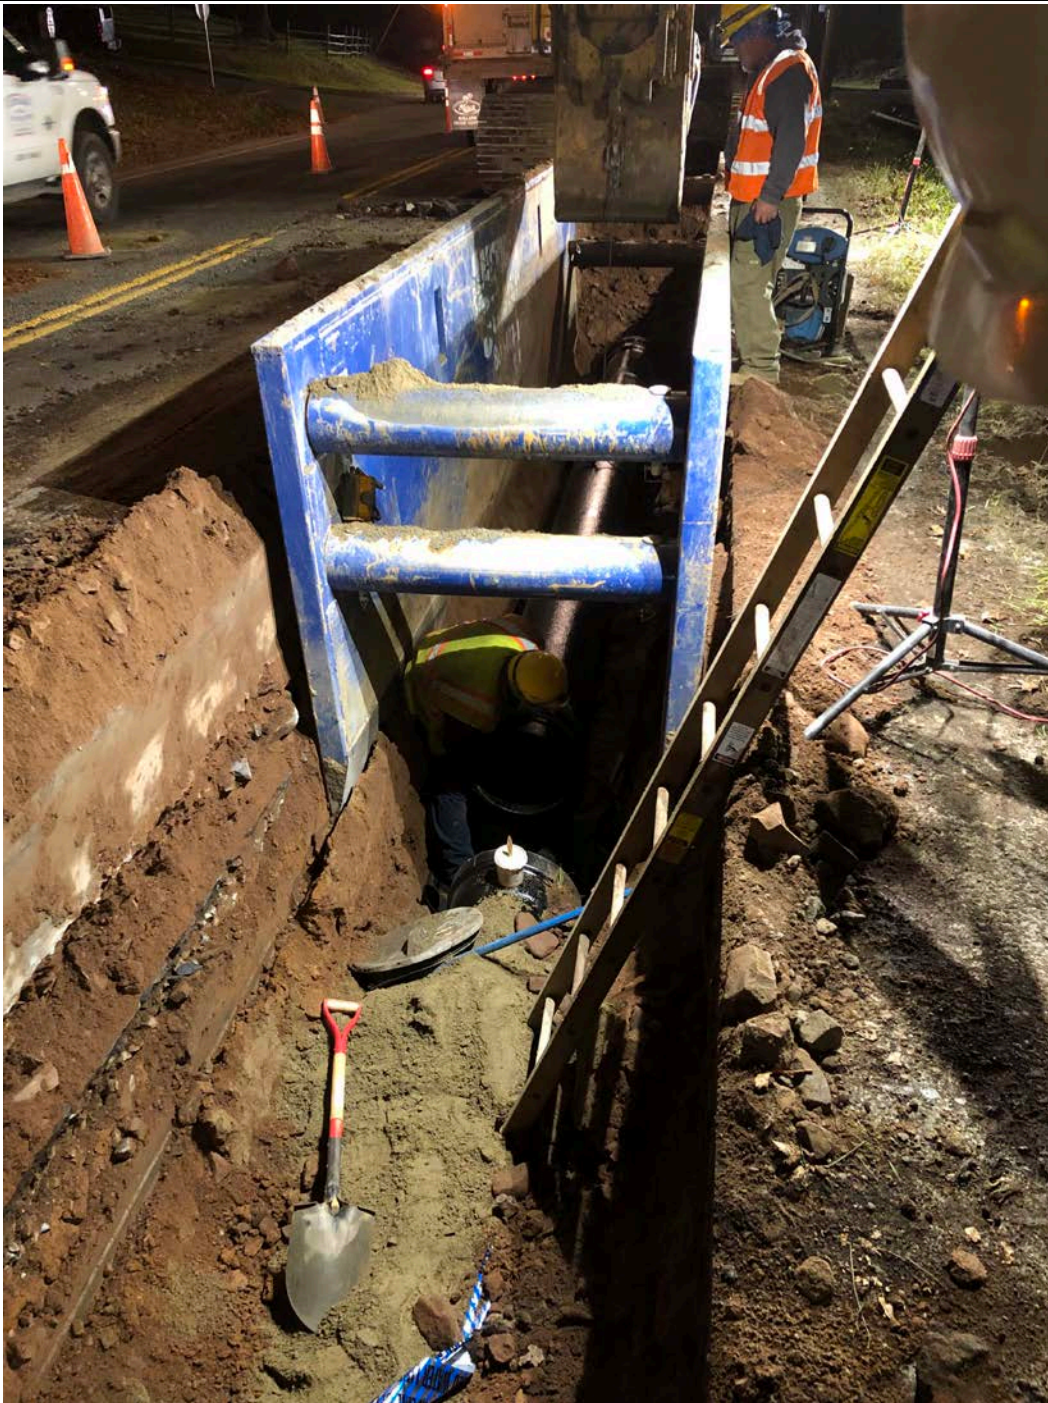


Figure 1 – Placing 3<sup>rd</sup> pipe section



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 7



Figure 2 –Backfill pile at Sta. 139+52



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 7



Figure 3 – Compacting 1<sup>st</sup> fill lift over 1<sup>st</sup>-2<sup>nd</sup> pipe sections



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 7



Figure 4 – Compacted top backfill layer



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	November 4, 2019
<b>Location:</b>	South Main Street, Middletown CT	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 60445033	<b>Report No:</b>	21
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	7 of 7

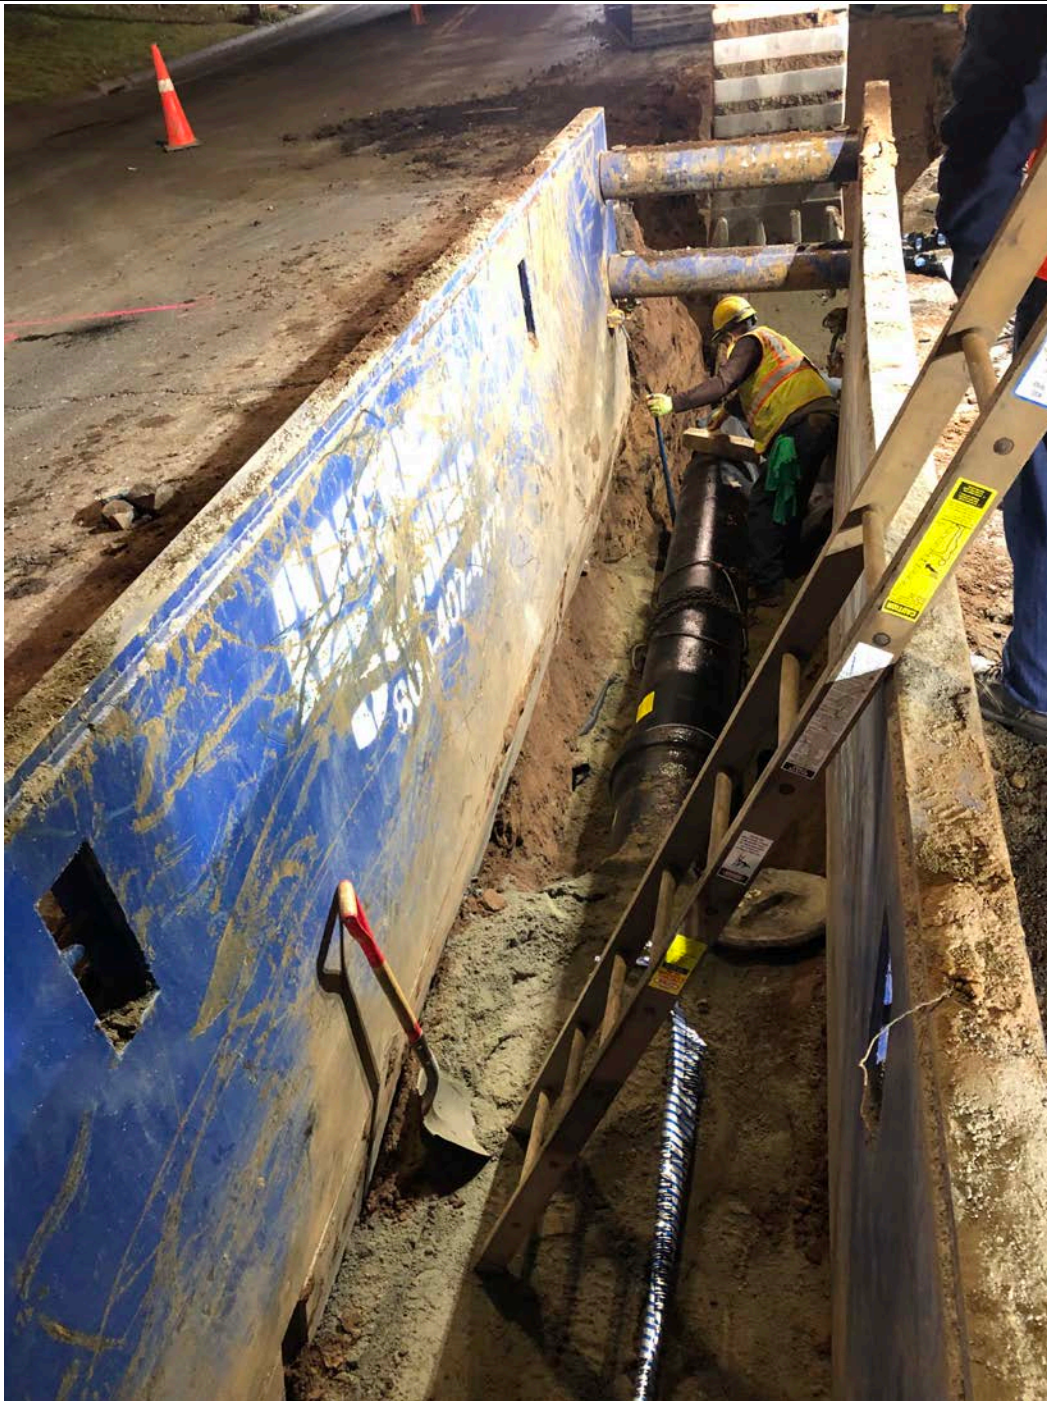


Figure 5 – Placing 8<sup>th</sup> pipe section
