

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 10

Weather Conditions

Conditions: Daylight hours: Cloudy. Winds variable 0-4 mph.  
 Temperature (°F): High 57°F Low 48°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	x	Hrs
USACE				Ludlow Construction			
Field Engineer	2	x	8	Superintendent	1	x	8
				Safety Officer	1	x	8
				Foreman	0	x	8
				Dump truck Operator	1	x	8
				Excavator Operator	1	x	8
				Skid Steer/ Bucket Loader	1	x	8
				Laborers	3	x	8
				Note that some persons			
Barnhart	0	x	8	Multiple pieces equipment.			
United Concrete	0	x	8				
JMS	0	x	8	Sub-contractor	0	x	8
CT Traffic Control	0	x	8	Municipal Police Detail	0	x	8
				State Police Detail	0	x	8

Visitors: None.

### Pipe Connections, Installations, and Other Work

Ludlow continued work at the booster station work zone located at Station 750+63 on South Main Street in Middletown.

### Daily Activities – Booster Station, South Main Street, Middletown

Ludlow continued work at the booster station work zone located at Station 750+63 on South Main Street in Middletown.

0725: Ludlow is working at the booster station located at Station 750+63 as they begin to remove the wooden forms from the sides of the footings that were cast on Monday, May 3, 2021.

0851: Ludlow has removed all wood from the exterior of the footing forms at the booster station located at Station 750+63 in Middletown.

0944: Ludlow has begun to secure horizontal pieces of rebar to the upright pieces of rebar that they previously placed for the frost wall associated with the booster station that will be installed at Station 750+63, Middletown.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	05/05/21
-----------------------------	------------	--------------	----------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 10

1049: Ludlow continues to secure horizontal pieces of rebar to the upright pieces of rebar that they previously placed for the frost wall associated with the booster station that will be installed at Station 750+63, Middletown.

1147: Ludlow has almost finished securing horizontal pieces of rebar to the upright pieces of rebar that they previously placed for the frost wall associated with the booster station that will be installed at Station 750+63, Middletown.

1248: Ludlow has begun to erect steel concrete forms on top of the booster station footing for the frost wall associated with the booster station that will be installed at Station 750+63, Middletown.

1347: Ludlow continues to erect steel concrete forms on top of the booster station footing for the frost wall associated with the booster station that will be installed at Station 750+63, Middletown.

1415: Ludlow continues to erect steel concrete forms on top of the booster station footing for the frost wall associated with the booster station that will be installed at Station 750+63, Middletown.

<b>Res. Representative:</b>	<u>J. Meunier</u>	<b>Date:</b>	<u>05/05/21</u>
-----------------------------	-------------------	--------------	-----------------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 10



Picture 1: View of the booster station footings with vertical dowels cast in place for the frost wall. Wood forms have just been removed from the sides of the footings. Station 750+63 South Main Street in Middletown. View to the southeast.

Res. Representative:

J. Meunier

Date: 05/05/21



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 10



Picture 2: View of the booster station footings with vertical dowels cast in place for the frost wall. Wood forms have just been removed from the sides of the footings. Station 750+63 in Middletown.


Res. Representative:

J. Meunier

Date: 05/05/21

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 10

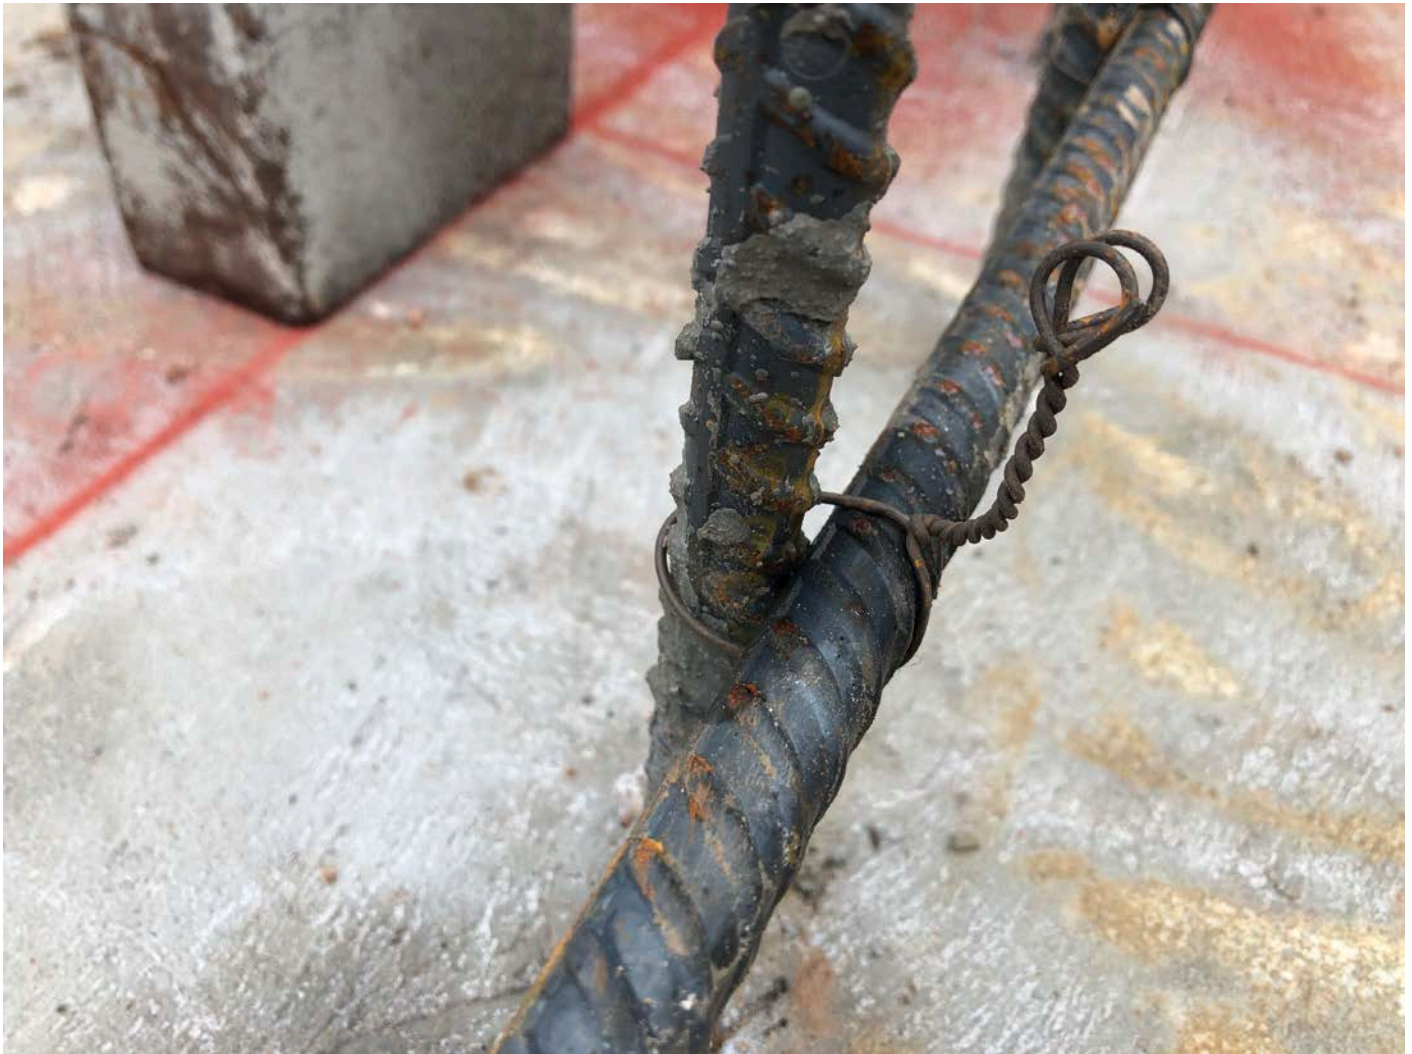

**Picture 3: Closeup of intersecting rebar for the frost wall that has been secured with wire ties at the booster station located at Station 750+63 in Middletown.**

**Res. Representative:**

J. Meunier

**Date:** 05/05/21



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 10



**Picture 4: View of the booster station footprint with footings cast in place and the majority of the frost wall rebar installed and secured with wire ties at the booster station located Station 750+63, Middletown. View to the southeast.**



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	7 of 10



Picture 5: Rebar that has been placed as part of the construction of the frost wall for the booster station located at Station 750+63 in Middletown.

Res. Representative:

J. Meunier

Date: 05/05/21



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	8 of 10



Picture 6: Ludlow in the process of erecting concrete forms at the booster station footprint located at Station 750+63, Middletown. View to the east.

Res. Representative:

J. Meunier

Date: 05/05/21



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	9 of 10



Picture 7: Ludlow in the process of erecting concrete forms at the booster station footprint located at Station 750+63, Middletown. View to the northwest.

Res. Representative:

J. Meunier

Date: 05/05/21



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	May 5, 2021
<b>Location:</b>	South Main Street, Middletown	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	236
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	10 of 10



Picture 8: Ludlow in the process of erecting concrete forms at the booster station footprint located at Station 750+63, Middletown. View to the southeast.
