

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	June 9, 2021
Location:	S. Main Street and the Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	260
Contractor:	Ludlow Construction	Page:	2 of 7

1050: Ludlow done with grading the new catch basin. DN Tank appears to be on the dome and inside the tank working. No one was available to speak to about the progress as all persons were either on top or inside the tank.

1430: DN Tanks is nearly completed with power washing the inside of the water tank. Speaking with Andrew (DN Tanks) they are planning on arriving at 0600 tomorrow to start the first coat (primer) on the water tank top and Tammscoat on the walls. Friday plan on doing the second coat of Tammscoat on the entire outside of the tank. Inside work will resume on Monday.

Daily Activities –Booster station work zone, Main Street, Middletown

0715: Ludlow trenching at the booster station today for conduits. Building concrete trench/rebar for conduit. Building pad for generator. Spoke with Billy (Ludlow), United still to come back and complete stone face along bottom of building. Missing stones related to grappling locations. United also sealed floor hole (interior booster station trench) which had been seeping into the trench.

0945: Trench half dug out coming from building. Ludlow currently grading the generator pad area.

1100: Booster station work continuing. Sumps are running again today to keep the water table down while doing conduit trenches.

1440: Booster station conduit trench work was completed along with generator pad area. Prepped for electrical work tomorrow. Billy (Ludlow) said they will continue at the booster station and depending on traffic may continue with grading work on the water tank site.


Res. Representative:	<u>W. Abrahams-Dematte</u>	Date:	<u>06/09/21</u>
-----------------------------	----------------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	June 9, 2021
Location:	S. Main Street and the Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	260
Contractor:	Ludlow Construction	Page:	3 of 7



Picture 1: Facing southeast. Conduits exit through booster station wall at this location. Start of excavation

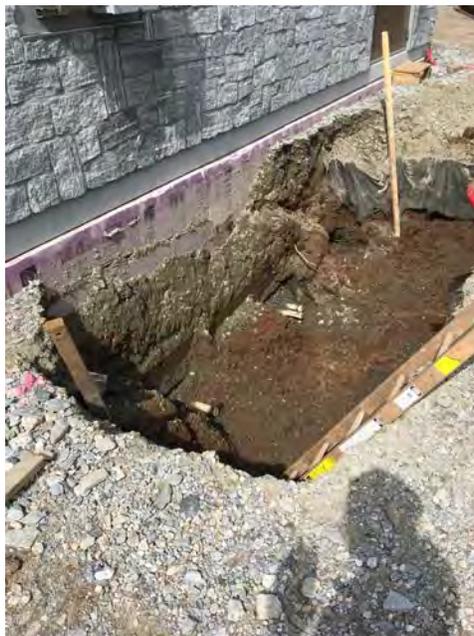

Picture 2: View into pit of conduits through wall.

Res. Representative:

W. Abrahams-Dematte

Date: 06/09/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	June 9, 2021
Location:	S. Main Street and the Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	260
Contractor:	Ludlow Construction	Page:	4 of 7



Picture 3: Facing south, behind booster station. Mark out for generator foundation.



Picture 4: Facing west. Conduit mark out line.

Res. Representative:	<u>W. Abrahams-Dematte</u>	Date:	<u>06/09/21</u>
-----------------------------	----------------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	June 9, 2021
Location:	S. Main Street and the Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	260
Contractor:	Ludlow Construction	Page:	5 of 7



Picture 5: Same view as previous picture, end of day.



Picture 6: Same view as Picture 3. Facing south behind booster station. Generator foundation excavation at top of photo.

Res. Representative:	<u>W. Abrahams-Dematte</u>	Date:	<u>06/09/21</u>
-----------------------------	----------------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	June 9, 2021
Location:	S. Main Street and the Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	260
Contractor:	Ludlow Construction	Page:	6 of 7



Picture 7: View east. Generator foundation to the right of photo. Conduit trench to Route 17 and new pole location.



Picture 8: Conduits sealed through vault up at water tank. Electrical enclosure to right in foreground. Two to be connected by United's electrician.

Res. Representative:	<u>W. Abrahams-Dematte</u>	Date:	<u>06/09/21</u>
-----------------------------	----------------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	June 9, 2021
Location:	S. Main Street and the Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	260
Contractor:	Ludlow Construction	Page:	7 of 7



Picture 7: View south. New catch basin installed. Finalized catchment grading around basin.



Picture 8: View southwest of new catch basin.

Res. Representative:	<u>W. Abrahams-Dematte</u>	Date:	<u>06/09/21</u>
-----------------------------	----------------------------	--------------	-----------------
