

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	1 of 14

Weather Conditions

Conditions: Daylight hours: Overcast. Winds variable 0-7 mph.
 Temperature (°F): High 73°F Low 55°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	x	Hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	1	X	8
				Safety Officer	1	X	8
				Foreman	1	X	8
				Dump truck Operator	2	X	8
				Excavator Operator	1	X	8
				Skid Steer/Bucket Loader	1	X	8
				Laborers	4	X	8
Barnhart	0	x	8	Note that some persons operate			
Fazzino Plumbing	2	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
CT Traffic Control	0	x	8	Sub-contractor	4	X	8
A&R Electrical	2	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Pipe Connections, Installations, and Other Work

Ludlow resumed construction of a retaining wall located between Stations 10+83 and 11+34. Ludlow performed earth work on the southeast and southwest sides of the water tank. A&R Electrical pulled wire through various conduits associated with the water tank, and also installed three light poles on the west and north side of the water tank. Fazzino Plumbing installed final water service components at the residences located at 29 and 35 Maiden Lane.

Daily Activities – water tank work zone, Shared Access Road, Middletown

Ludlow resumed construction of a retaining wall located between Stations 10+83 and 11+34. Ludlow performed earth work on the southeast and southwest sides of the water tank. A&R Electrical pulled wire through various conduits associated with the water tank, and also installed three light poles on the west and north side of the water tank.

0709: Ludlow is mobilizing to the water tank work zone to resume work on the retaining wall located between Stations 10+83 and 11+34. Ludlow is currently disassembling the wall so they spin the geogrid fabric they placed on October 6, 2021 90°, which will orient the fabric for maximum strength.

Res. Representative:	J. Meunier	Date:	10/08/21
----------------------	------------	-------	----------

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	2 of 14

0719: Ludlow continues to excavate soil on the slopes located east and south east side of the water tank, live-loading the fill into dump trucks for offsite removal.

0722: Two electricians from A&R Electrical arrive at the water tank work zone. A&R Electrical is pulling wires through various conduits associated with the water tank. A&R Electrical will also be installing light poles on the west and north side of the water tank.

0821: Ludlow is performing earthwork on the southwest side of the water tank, shaping the slope and removing fill that is being live-loaded into dump trucks and removed off-site.

0847: Ludlow continues earth work on the southwest side of the water tank.

0849: A&R Electrical are erecting light poles on the west and north side of the water tank and wiring them.

0902: Ludlow continues construction of the retaining wall located between Stations 10+83 and 11+34 on the south side of the Shared Access Road.

0923: A&R Electrical continues to work on erecting and wiring light poles on the west and north side of the water tank.

0952: Ludlow continues the construction of a retaining wall between Stations 10+83 and 11+34 on the south side of the Shared Access Road.

0955: Ludlow continues excavating fill and live-loading it into dump trucks for offsite removal on the southeast side of the water tank as they continue to shape the slope.

1024: Ludlow continues to excavate fill as they shape the slope on the southeast side of the water tank.

1035: Ludlow continues construction of the retaining wall located between Stations 10+83 and 11+34 on the south side of the Shared Access Road.

1041: A&R Electrical continues to install and wire light poles on the west side of the water tank.

1220: A&R Electrical is pulling wire through the 1" conduits located on the north side of the water tank.

1251: A&R Electrical continues to pull wires through the 1" conduits located on the northeast side of the water tank.

1313: Ludlow is using a dozer to shape the slope on the southeast side of the water tank. Ludlow is also placing and grading 1.5"-minus gravel on the northeast side of the water tank.

1321: A&R Electrical continues to work on the wire they have pulled through the 1" conduits located on the northeast side of the water tank.

1402: A&R Electrical has finished work for the day and departs the water tank work zone.

Res. Representative:	J. Meunier	Date:	10/08/21
----------------------	------------	-------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	3 of 14

Daily Activities – full water service installation activities, Maiden Lane, Durham

Fazzino Plumbing installed final water service components at the residences located at 29 and 35 Maiden Lane.

0931: Fazzino Plumbing is working at the 29 Maiden Lane residence for the installation of final water service components.

1010: Fazzino Plumbing continues to install final water service components at the 29 Maiden Lane residence.

1103: Fazzino Plumbing has mobilized to 35 Maiden Lane for the installation of final water service components.

1338: Fazzino Plumbing just finished with the installation of a 1" copper water service line at the 35 Maiden Lane residence.



Picture 1: Ludlow shaping the slope to the southeast of the water tank located east of the Shared Access Road in Middletown. View to west.

Res. Representative:	J. Meunier	Date:	10/08/21
----------------------	------------	-------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	4 of 14



Picture 2: A&R Electrical working inside of the electrical enclosure located on the north side of the altitude vault at the water tank work zone. View to the north.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	5 of 14



Picture 3: A&R Electrical working on a light pole they just installed on the west side of the water tank. View to the north.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	6 of 14



Picture 4: Ludlow shaping the slope to the southwest of the water tank located east of the Shared Access Road in Middletown. View to east.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	7 of 14



Picture 5: A&R Electrical wiring a light pole they just installed on the west side of the water tank. View to the southeast.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	8 of 14



Picture 6: Geogrid that Ludlow placed on the south side of the retaining wall they are constructing between Stations 10+83 and 11+34 on the south side of the Shared Access Road. View to the east.

Daily Report


Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	9 of 14



Picture 7: Ludlow constructing a retaining wall between Stations 10+83 and 11+34 on the south side of the Shared Access Road. View to the west.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	10 of 14

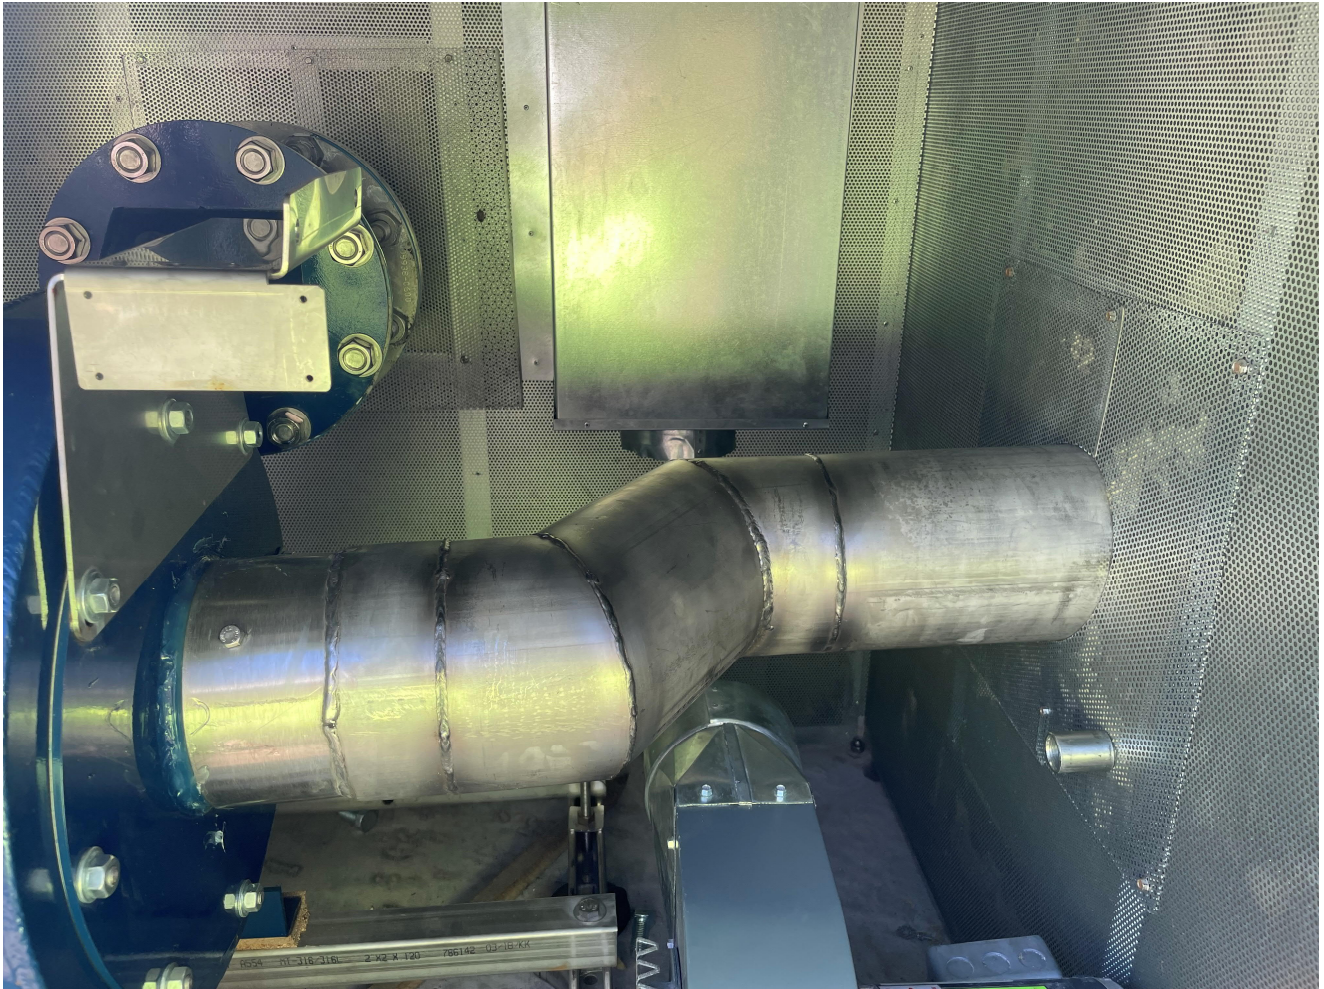

Picture 8: Stainless steel duct that Ludlow's subcontractor fabricated for placement on the blower located inside of the blower cabinet on the northeast side of the water tank. View to the south.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	11 of 14



Picture 9: Ludlow shaping the slope to the southeast of the water tank located east of the Shared Access Road in Middletown. View to west.

Daily Report


Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	12 of 14



Picture 10: Ludlow grading 1.5'-minus gravel on the northeast side of the water tank. View to the west.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	13 of 14

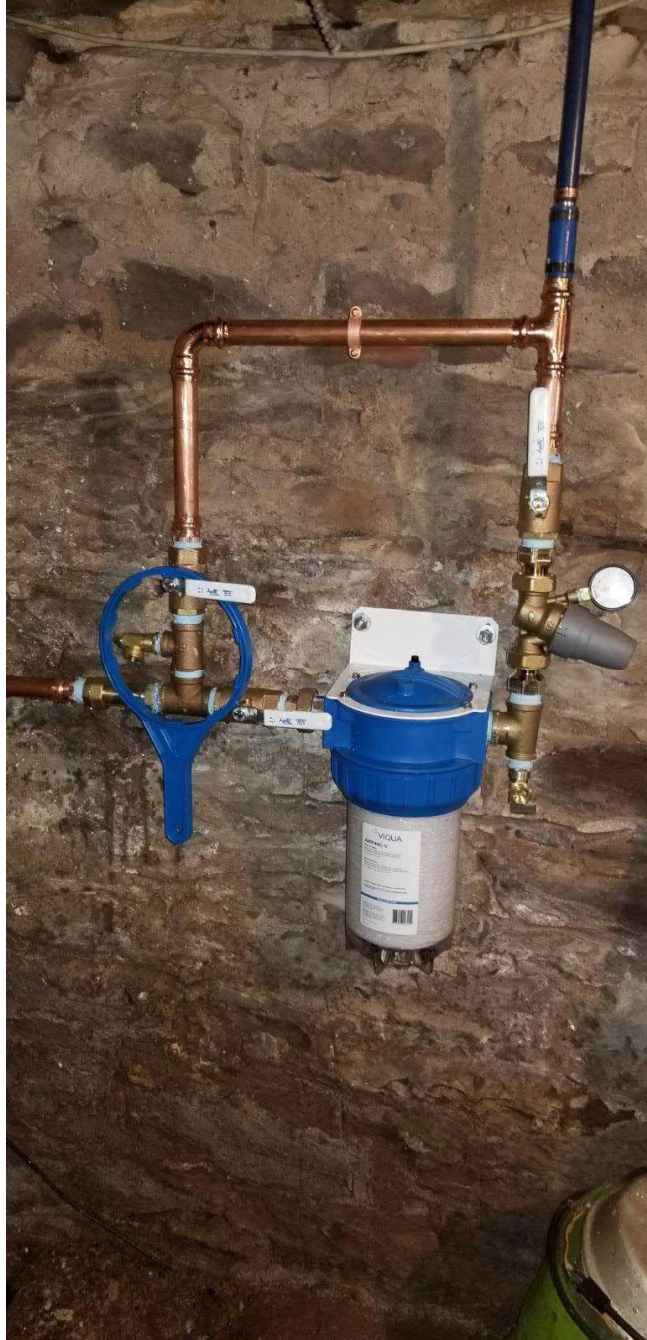

Picture 11: Final water service components that Fazzino Plumbing installed at the 29 Maiden Lane, Durham, residence.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 8, 2021
Location:	Maiden Lane, Durham; Shared Access Road, Middletown	Day of Week:	Friday
Project #:	AECOM: 6061487	Report No:	339
Contractor:	Ludlow Construction	Page:	14 of 14



Picture 12: Final water service components that Fazzino Plumbing installed at the 35 Maiden Lane, Durham, residence.

Res. Representative:	J. Meunier	Date:	10/08/21
----------------------	------------	-------	----------
