

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	1 of 12

Weather Conditions

Conditions: Daylight hours: Partly cloudy. Winds variable 0-4 mph.
 Temperature (°F): High 52°F Low 25°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	x	hrs
USACE				Ludlow Construction			
Field Engineer	2	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
				Foreman	1	X	8
				Dump truck Operator	0	X	8
				Excavator Operator	0	X	8
Eagle Fence	2	X	8	Skid Steer/ Bucket Loader	0	X	8
Fazzino Plumbing	1	X	8	Laborers	1	X	8
United Concrete	0	X	8	Note that some persons operate			
Frontier	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
CT Traffic Control	0	x	8	Sub-contractor	3	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Pipe Connections, Installations, and Other Work

Fazzino Plumbing worked on replacing brass tees on the final water system components they previously installed at the 119 and 95R Maple Avenue properties; 10 Johns Way; and 177R, 202, 261, 308, and 322 Main Street, Durham. Eagle Fence and Guardrail continued installing a permanent fence around the water tank work zone located east of the Shared Access Driveway in Middletown.

Daily Activities – Fence installation, Shared Access Driveway, Middletown

Eagle Fence and Guardrail continued installing a permanent fence around the water tank work zone located east of the Shared Access Driveway in Middletown.

0753: Eagle Fence and Guardrail has returned to the water tank work zone where they have drilled approximately 75% of the holes they will need to install permanent fencing around the tank and the altitude valve vault.

1026: Eagle Fence and Guardrail is cleaning out the holes they drilled yesterday at the water tank work zone with post hole diggers.

Res. Representative:	J. Meunier	Date:	12/15/21
-----------------------------	------------	--------------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	2 of 12

1251: Eagle Fence and Guardrail continues to work on excavating the holes they will need to install fence posts as part of the permanent fencing that will surround the water tank and the altitude valve vault.

Daily Activities – Replacement of brass tees, Maple Avenue and Main Street, Durham

Fazzino Plumbing worked on replacing brass tees on the final water system components they previously installed at the 119 and 95R Maple Avenue properties; 10 Johns Way; and 177R, 202, 261, 308, and 322 Main Street, Durham.

0738: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 202 Main Street, Durham, residence.

0831: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 308 Main Street, Durham, residence.

0851: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 261 Main Street, Durham, residence.

0933: Fazzino Plumbing continues changing out the brass tees on the final water system components they previously installed at the 261 Main Street, Durham, residence.

0955: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 119 Maple Avenue, Durham, residence.

1018: Fazzino Plumbing continues changing out the brass tees on the final water system components they previously installed at the 119 Maple Avenue residence.

1104: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 177R Main Street, Durham, residence.

1123: Fazzino has just arrived at the 297 Main Street residence to change out the brass tees on the final water system components they previously installed at the residence.

1206: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 268 Main Street residence.

1311: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 10 Johns Way, Durham, residence.

1348: Fazzino Plumbing continues working on changing out the brass tees on the final water system components they previously installed at the 10 Johns way residence.

1420: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 95R Maple Avenue, Durham, residence.

Res. Representative:	J. Meunier	Date:	12/15/21
-----------------------------	------------	--------------	----------

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	3 of 12

1534: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 322 Main Street, Durham, residence.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>12/15/21</u>
-----------------------------	-------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	4 of 12



Picture 1: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 202 Main Street, Durham, residence.


Res. Representative:

J. Meunier

Date: 12/15/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	5 of 12

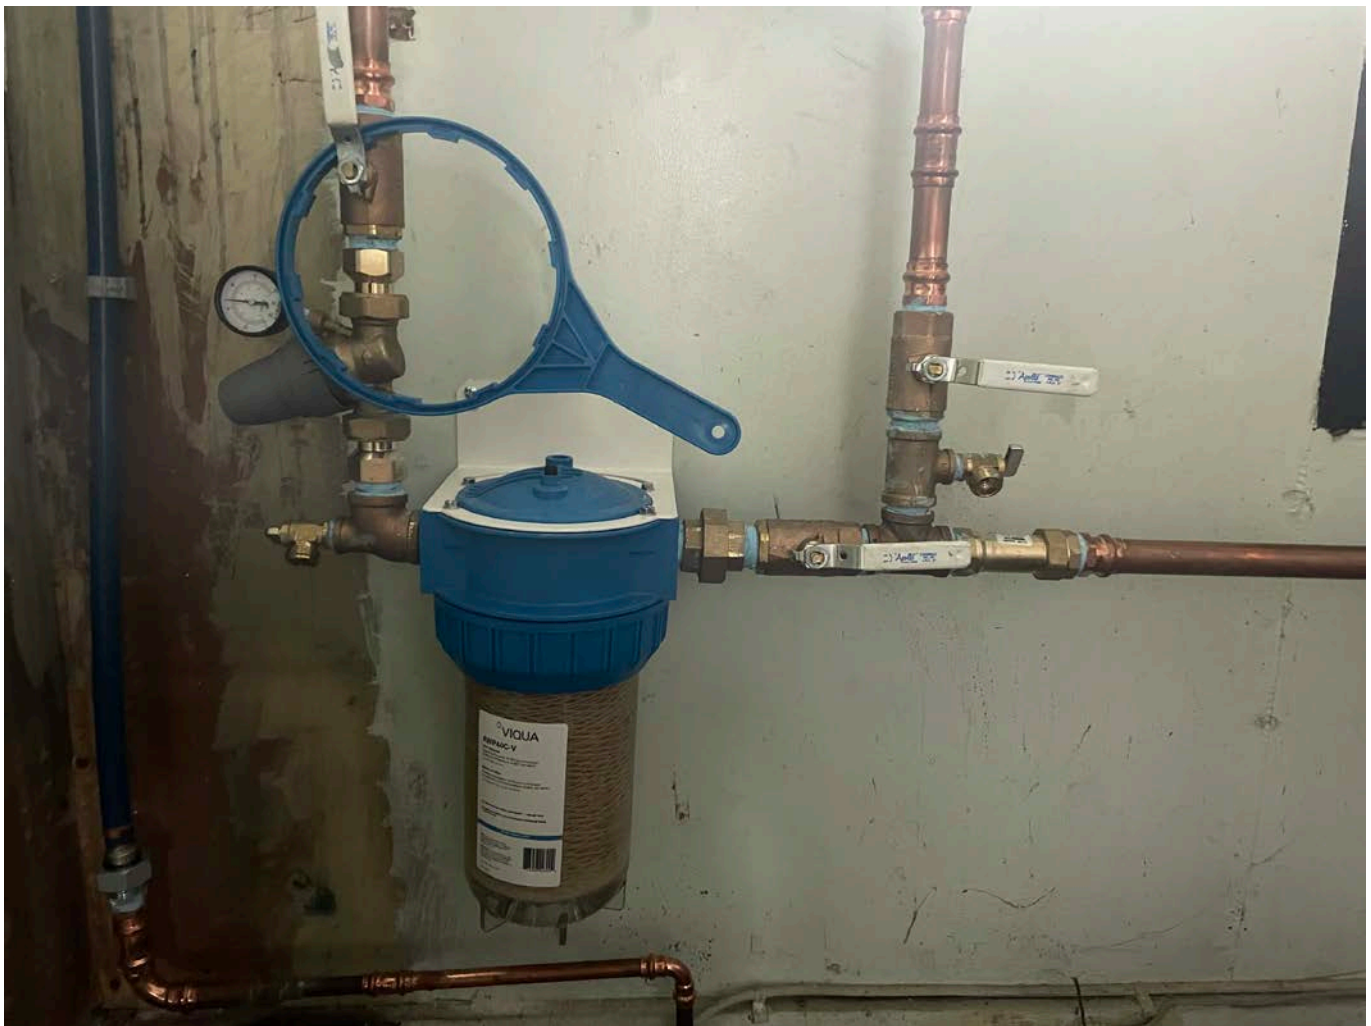

Picture 2: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 261 Main Street, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/15/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	6 of 12



Picture 3: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 119 Maple Avenue, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/15/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	7 of 12



Picture 4: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 177R Main Street, Durham, residence.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	8 of 12



Picture 5: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 297 Main Street, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/15/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	9 of 12



Picture 6: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 268 Main Street, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/15/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	10 of 12



Picture 7: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 10 Johns Way, Durham, residence.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>12/15/21</u>
-----------------------------	-------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	11 of 12



Picture 8: Eagle Fence and Guardrail working to clear a hole they augured yesterday on the north side of the Shared Access Driveway in Middletown with a breaker bar and a pole hole digger. View to the north.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>12/15/21</u>
-----------------------------	-------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 15, 2021
Location:	Main Street, Johns Way, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Wednesday
Project #:	AECOM: 6061487	Report No:	383
Contractor:	Ludlow Construction	Page:	12 of 12



Picture 9: Eagle Fence and Guardrail clearing a hole they augured yesterday on the west side of the altitude valve vault at the water tank work zone with a pole hole digger. View to the south.
