

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	1 of 9

Weather Conditions

Conditions: Daylight hours: Overcast/rainy. Wind variable 0-9 mph.
 Temperature (°F): High 53°F Low 35°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
				Foreman	1	X	8
				Dump truck Operator	0	X	8
				Excavator Operator	0	X	8
Knapp Engineering	0	X	8	Skid Steer/Bucket Loader	0	X	8
Fazzino Plumbing	0	X	8	Laborers	0	X	8
United Concrete	0	X	8	Note that some persons operate			
Frontier	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	2	x	8				
CT Traffic Control	0	x	8	Sub-contractor	2	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Pipe Connections, Installations, and Other Work

Apuzzo Electric disconnected the existing pump control boxes, feed wires back to the main electrical panel, disconnected wires from the panel, and installed new copper bonding wires from the main electrical panel to the new water services at 172, 175, and 224 Maple Avenue; 78, 93R, and 110 Maiden Lane; and 14 Talcott Lane, Durham.

Daily Activities – Installation of new bonding wire, Durham

Apuzzo Electric disconnected the existing pump control boxes, feed wires back to the main electrical panel, disconnected wires from the panel, and installed new copper bonding wires from the main electrical panel to the new water services at 172, 175, and 224 Maple Avenue; 78, 93R, and 110 Maiden Lane; and 14 Talcott Lane, Durham.

0741: AECOM arrives at the 175 Maple Avenue, Durham, residence where two electricians from Apuzzo Electric are installing ground wires to the recently installed final water system components.

0824: Apuzzo Electric is finishing up installation activities at the 175 Maple Avenue residence.

0830: Apuzzo Electric arrives at the 244 Maple Avenue, Durham, residence to install ground wires to the recently installed final water system components.

Res. Representative:	J. Meunier	Date:	3/24/22
-----------------------------	------------	--------------	---------

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	2 of 9

0903: Apuzzo Electric has finished installation activities at the 244 Maple Avenue residence.

0913: Apuzzo Electric arrives at the 93R Maiden Lane, Durham, residence to install ground wires to the recently installed final water system components.

0952: Apuzzo Electric departs the 93R Maiden Lane residence after completing installation activities.

0959: Apuzzo Electric arrives at the 78 Maiden Lane, Durham, residence to install ground wires to the recently installed final water system components.

1026: Apuzzo Electric departs 93R Maiden Lane residence after completing installation activities.

1033: Apuzzo Electric arrives at the 110 Maiden Lane, Durham, residence to install ground wires to the recently installed final water system components.

1056: Apuzzo Electric departs the 110 Maiden Lane residence after completing installation activities.

1107: Apuzzo Electric arrives at the 14 Talcott Lane, Durham, residence. However, they were unable to make contact with the home owner and are preparing to mobilize to the 172 Maple Avenue, Durham, residence.

1114: Apuzzo Electric has mobilized to the 172 Maple Avenue residence to install ground wires to the recently installed final water system components.

1139: Work has paused at the 172 Maple Avenue residence as one of the Apuzzo Electric electricians leaves the site to purchase additional copper wire to complete installation activities.

1159: Apuzzo Electric departs the 172 Maple Avenue residence after completing installation activities.

1206: Apuzzo Electric has mobilized to the 14 Talcott Lane residence to install ground wires to the recently installed final water system components after having made contact with the home owner.

1228: Apuzzo Electric departs the 14 Talcott Lane residence after completing installation activities.

1236: Apuzzo Electric arrives at the 133 Maple Avenue, Durham, residence to install ground wires to the recently installed final water system components. Unfortunately, the electricians were unable to gain access to the home and were unable to make contact with the home owner.

1300: Apuzzo Electric is departing the residence at 133 Maple Avenue after they were unable to gain access to the home and were unable to make contact with the home owner. Work at this address will need to be rescheduled for a later date.

Additional Information

Fazzino Plumbing finished the installation of final water service components at the 230 Maple Avenue, Durham, residence yesterday.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>3/24/22</u>
-----------------------------	-------------------	--------------	----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	3 of 9



Picture 1: Apuzzo Electric installing a ground line to the final water service components at the 175 Maple Avenue, Durham, residence.

Res. Representative:

J. Meunier

Date: 3/24/22

Daily Report


Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	4 of 9



Picture 2: Apuzzo Electric installing a ground line to the final water service components at the 244 Maple Avenue, Durham, residence.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	5 of 9

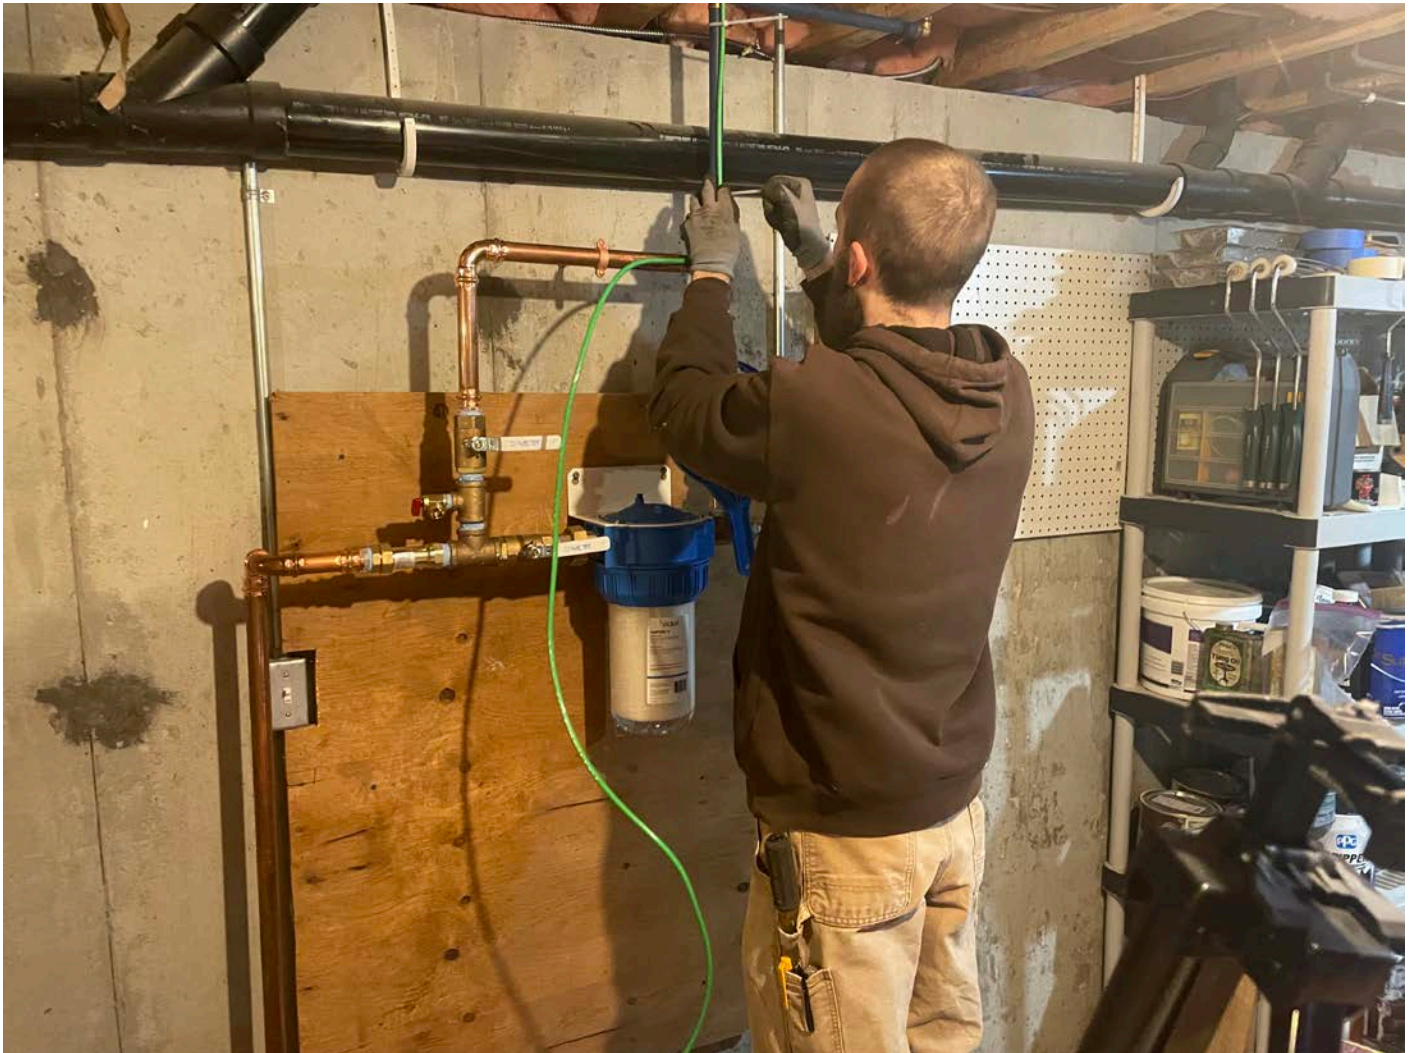

Picture 3: Apuzzo Electric installing a ground line to the final water service components at the 93R Maiden Lane, Durham, residence.


Res. Representative:

J. Meunier

Date: 3/24/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	6 of 9

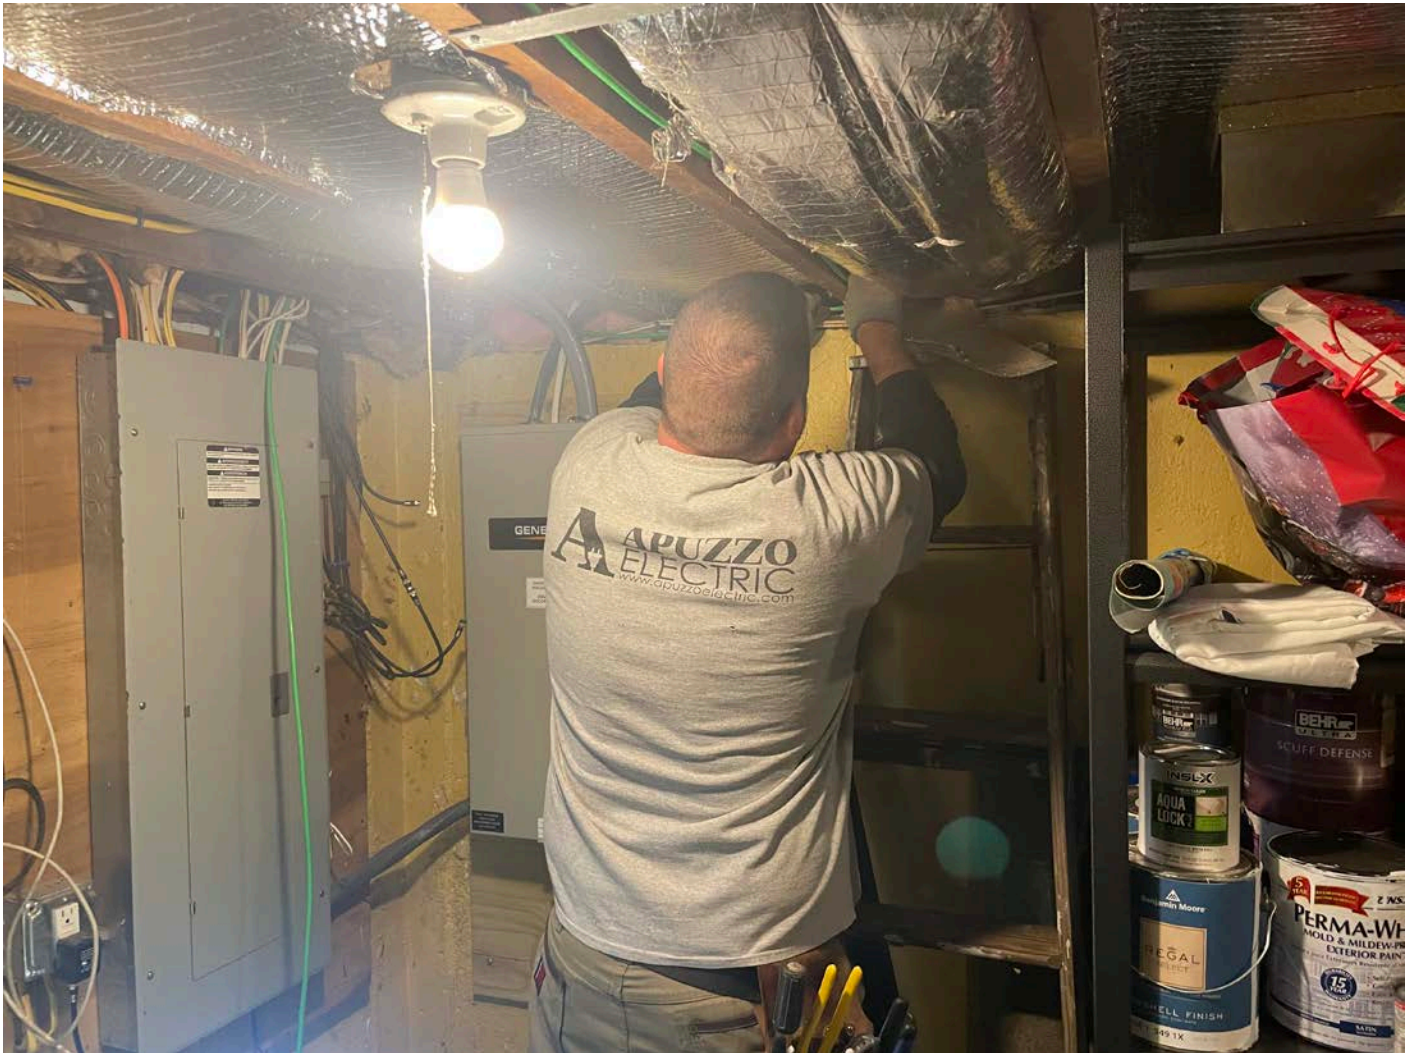

Picture 4: Apuzzo Electric installing a ground line to the final water service components at the 78 Maiden Lane, Durham, residence.

Res. Representative:

J. Meunier

Date: 3/24/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	7 of 9



Picture 5: Apuzzo Electric installing a ground line to the final water service components at the 110 Maiden Lane, Durham, residence.

Res. Representative:

J. Meunier

Date: 3/24/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	8 of 9



Picture 6: Apuzzo Electric installing a ground line to the final water service components at the 172 Maple Avenue, Durham, residence.

Res. Representative:

J. Meunier

Date: 3/24/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 24, 2022
Location:	Maple Avenue, Maiden Lane, and Talcott Lane, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	398
Contractor:	Ludlow Construction	Page:	9 of 9



Picture 7: Apuzzo Electric installing a ground line to the final water service components at the 14 Talcott Lane, Durham, residence.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>3/24/22</u>
-----------------------------	-------------------	--------------	----------------
