

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	1 of 8

Weather Conditions			
Conditions:	Daylight hours: Partly cloudy. Wind variable 0-10 mph.		
Temperature (°F):	High 94°F	Low	71°F

Contractors & Subcontractors Workfor57				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	1	X	8
Flow Tech	0	X	8	Foreman	1	X	8
Matt Chlor	0	X	8	Dump truck Operator	1	X	8
A&J Construction	0	X	8	Excavator Operator	1	X	8
Grela Well Drilling	0	X	8	Skid Steer/Bucket Loader	1	X	8
Fazzino Plumbing	0	X	8	Laborers	3	X	8
United Concrete	0	X	8	Note that some persons operate			
Knapp Engineering	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Alarm Systems, Inc.	0	x	8	Sub-contractor	0	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: High School Maintenance Supervisor.

Daily Activities – Miscellaneous Activities, Durham

0749: Ludlow Construction is excavating the area that is east of the Francis E. Korn Center. They are excavating using an excavator and manual hand digging to access the underground water main.

0813: Ludlow Construction continues to excavate the area that is east of the Francis E. Korn Center.

0912: Ludlow Construction continues to excavate the area that is east of the Francis E. Korn Center.

1038: Ludlow Construction continues to excavate the area that is east of the Francis E. Korn Center. The fire service and domestic water service pipes have been exposed.

1126: Ludlow Construction is finishing up the connection of the domestic water service to the water valve. Ludlow Construction uses an excavator to hold the pipe while installing it into the valve. The other side of the existing water service was capped.

1217: Ludlow Construction is finishing up the connection of the domestic water service to the valve.

Res. Representative:	A. Mora	Date:	8/9/22
-----------------------------	---------	--------------	--------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	2 of 8

1231: Ludlow Construction is installing silt fence to prevent erosion from occurring at the bottom of the slope is west of District 13 regional superintendent building's parking lot.

1246: Ludlow Construction has backfilled the domestic water service side of the excavated trench with sand. Ludlow Construction has cut into the existing fire service connection.

1317: Ludlow Construction has attached the fire service valve and is finishing up installing the rest of the fire service piping.

1411: Ludlow Construction has backfilled both sides of the trench and now is using manual hand digging and a compactor to compact the soil and sand to prep for the second half of backfilling.

1444: Ludlow Construction has completely backfilled the trench that was excavated to access the domestic and fire service pipelines. Ludlow Construction is using a compactor to fully compact the backfilled area and a sweeper to push all the soil on the road into the backfilled area to be compacted.

Res. Representative:	A. Mora	Date:	8/9/22
-----------------------------	---------	--------------	--------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	3 of 8



Photo 1: Ludlow Construction begins to excavate on Pickett Lane to access the fire service and domestic water service connections to the former Korn School.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	4 of 8

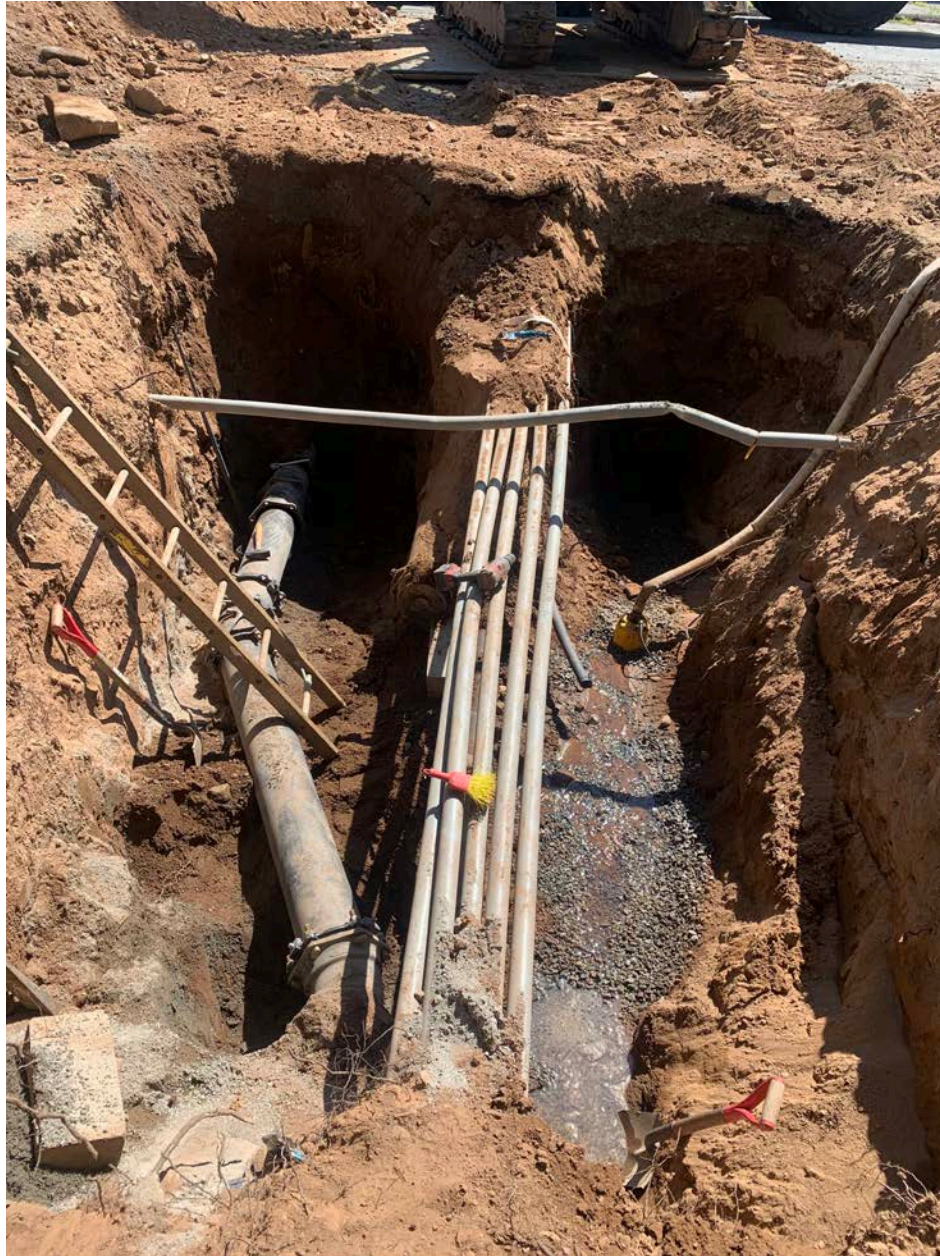


Photo 2: Ludlow Construction connecting the fire service at the former Korn School.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	5 of 8



Photo 3: Ludlow Construction is connecting the 4" domestic water service at the former Korn School.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	6 of 8

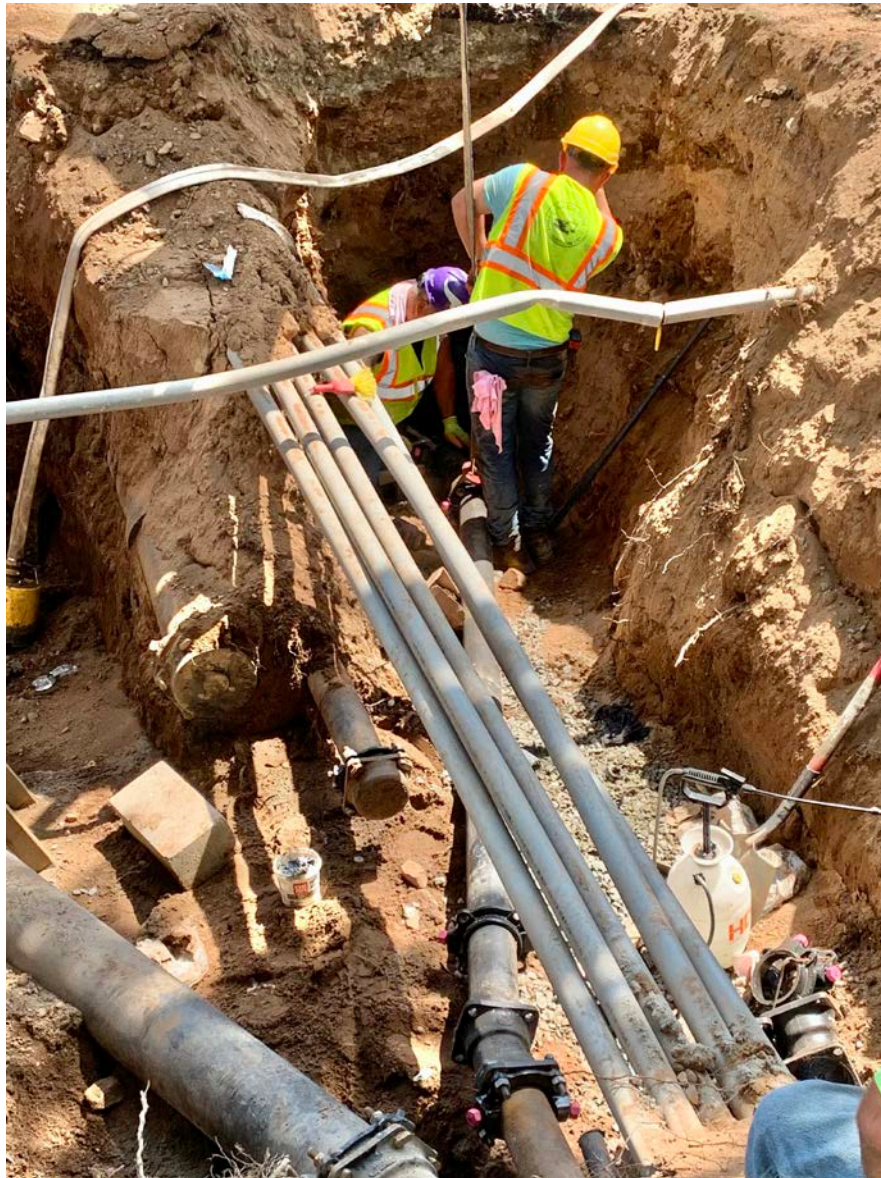


Photo 4: Ludlow Construction capping the former domestic water service at Korn School.

Res. Representative:	<u>A. Mora</u>	Date:	<u>8/9/22</u>
-----------------------------	----------------	--------------	---------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	7 of 8

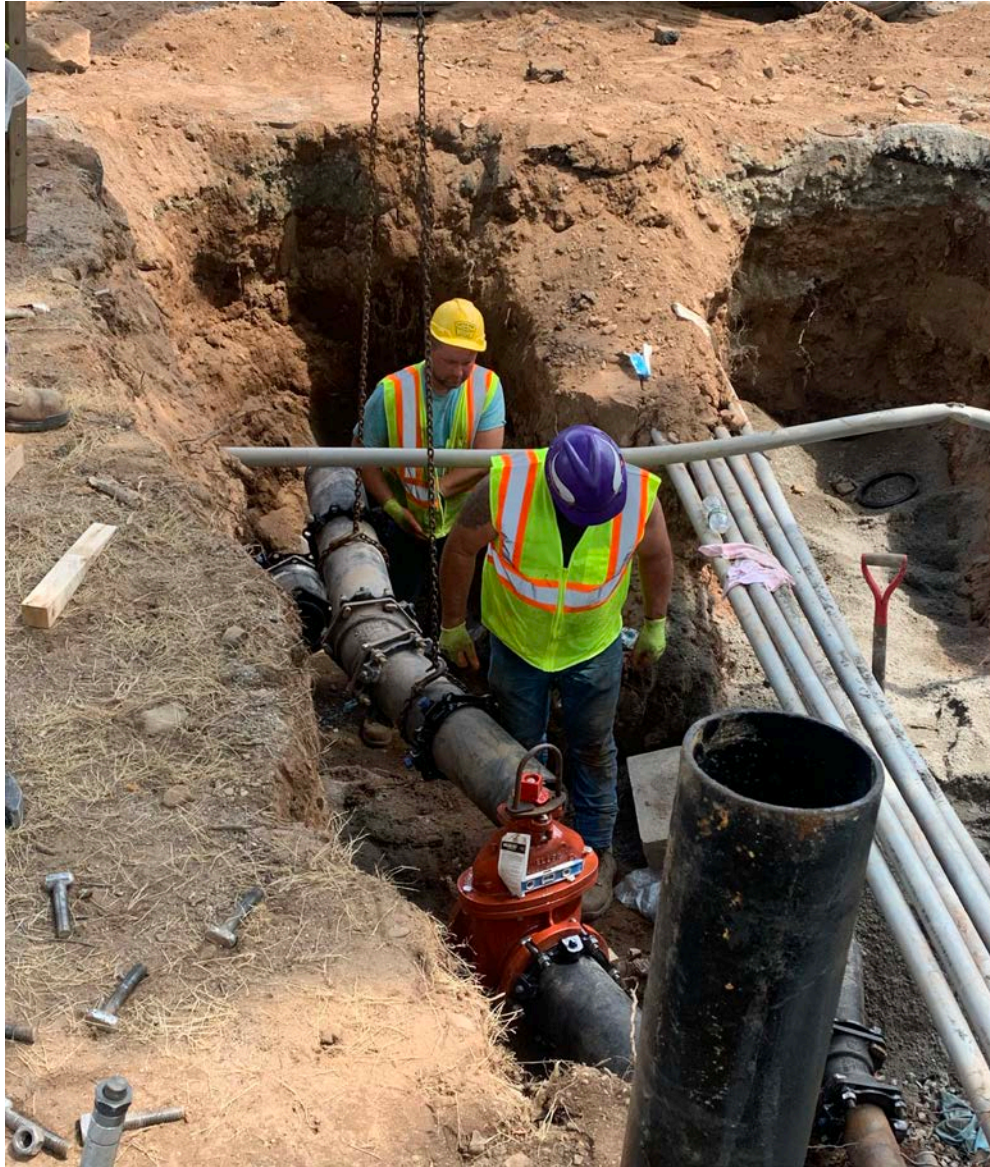


Photo 5: Ludlow Construction is working on tying in the 8-inch fire service.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 9, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Tuesday
Project #:	AECOM: 60614871	Report No:	485
Contractor:	Ludlow Construction	Page:	8 of 8



Photo 6: Ludlow Construction finishes the backfilling of the excavated trench at the former Korn School by compacting the ground with a compactor and prepping it for loam.
