

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	1 of 10

Weather Conditions			
Conditions:	Daylight hours: Sunny. Wind variable 0-7 mph.		
Temperature (°F):	High	80°F	Low 56°F

Contractors & Subcontractors Workforce					Equipment in Use				
Trade	#	x	hrs		Trade	#	X	hrs	
USACE					Ludlow Construction				
Field Engineer	1	x	8		Superintendent	0	X	8	
					Safety Officer	1	X	8	
United Concrete	0	x	8		Foreman	1	X	8	
West State Mechanical	0	x	8		Dump truck Operator	1	X	8	
Northeast Rigging	0	x	8		Excavator Operator	1	X	8	
Grela Well Drilling	0	X	8		Skid Steer/ Bucket Loader	1	X	8	
Fazzino Plumbing	0	X	8		Laborers	2	X	8	
United Concrete	0	x	8		Note that some persons operate				
Knapp Engineering	0	x	8		Multiple pieces equipment.				
Apuzzo Electric	0	x	8						
Alarm Systems, Inc.	0	x	8		Sub-contractor	0	X	8	
A&R Electrical	0	x	8		Municipal Police Detail	0	X	8	
					State Police Detail	0	X	8	

Visitors: None.

Daily Activities – Preparation of sections of sidewalks for concrete placement on Pickett Lane & Main Street, asphalt and loam placement on Maple Avenue

0805: Ludlow Construction fills in potholes with cement on Pickett Lane.

0832: Ludlow Construction installs wire mesh reinforcement at the backflow preventer enclosure base at the south side of Pickett Lane.

0850: Ludlow Construction begins to remove a piece of the sidewalk at 215 Main Street and excavates the ground below the section of removed sidewalk using an excavator to prep the area for concrete placement.

0907: Ludlow Construction begins to remove a piece of sidewalk located at Durham Fitness and begins to excavate the ground that is below it to prep the area for concrete placement.

0935: Ludlow Construction is excavating a section of sidewalk on 289 Main Street to prep the area for concrete placement.

0939: Ludlow Construction is cutting a piece of sidewalk on 293 Main Street to remove the sidewalk with an excavator afterwards.

Res. Representative:	A.Mora	Date:	9/08/22
-----------------------------	--------	--------------	---------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	2 of 10

1029: Ludlow Construction is on 289 Main Street continuing to prep a section of removed sidewalk for concrete placement by installing wire mesh reinforcement.

1058: Ludlow Construction is at Durham auto parts to remove a section of the sidewalk using an excavator. Ludlow Construction forms the sidewalk and places wire mesh reinforcing to prep the section of sidewalk for concrete placement.

1211: Ludlow Construction preps an area for asphalt laying on 126 Maple Avenue.

1242: Ludlow Construction lays the first asphalt driveway course at 126 Maple Avenue.

1255: Ludlow Construction uses a roller to flatten the recently laid asphalt on 126 Maple Avenue

1431: Ludlow Construction lays a second layer of asphalt on 126 Maple Avenue.

1456: Ludlow Construction lays loam and seeds around the freshly laid asphalt to restore the area at 126 Maple Avenue.

Res. Representative:	<u>A.Mora</u>	Date:	<u>9/08/22</u>
-----------------------------	---------------	--------------	----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	3 of 10



Picture 1: Ludlow Construction is at the backflow preventer enclosure base on Pickett Lane installing wire mesh reinforcement in the completed forms.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	4 of 10



Picture 2: Ludlow Construction is excavating with an excavator to prepare the sidewalk area for concrete sidewalk restoration located at 215 Main Street.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	5 of 10



Picture 3: Ludlow Construction is excavating with an excavator to prepare the area for concrete sidewalk restoration located at 289 Main Street.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	6 of 10



Picture 4: Ludlow Construction is saw-cutting a section of sidewalk to remove the sidewalk for restoration located at 297 Main Street.

Daily Report


Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	7 of 10



Picture 5: Ludlow construction has fully prepped a section of sidewalk for concrete placement at 289 Main Street.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	8 of 10

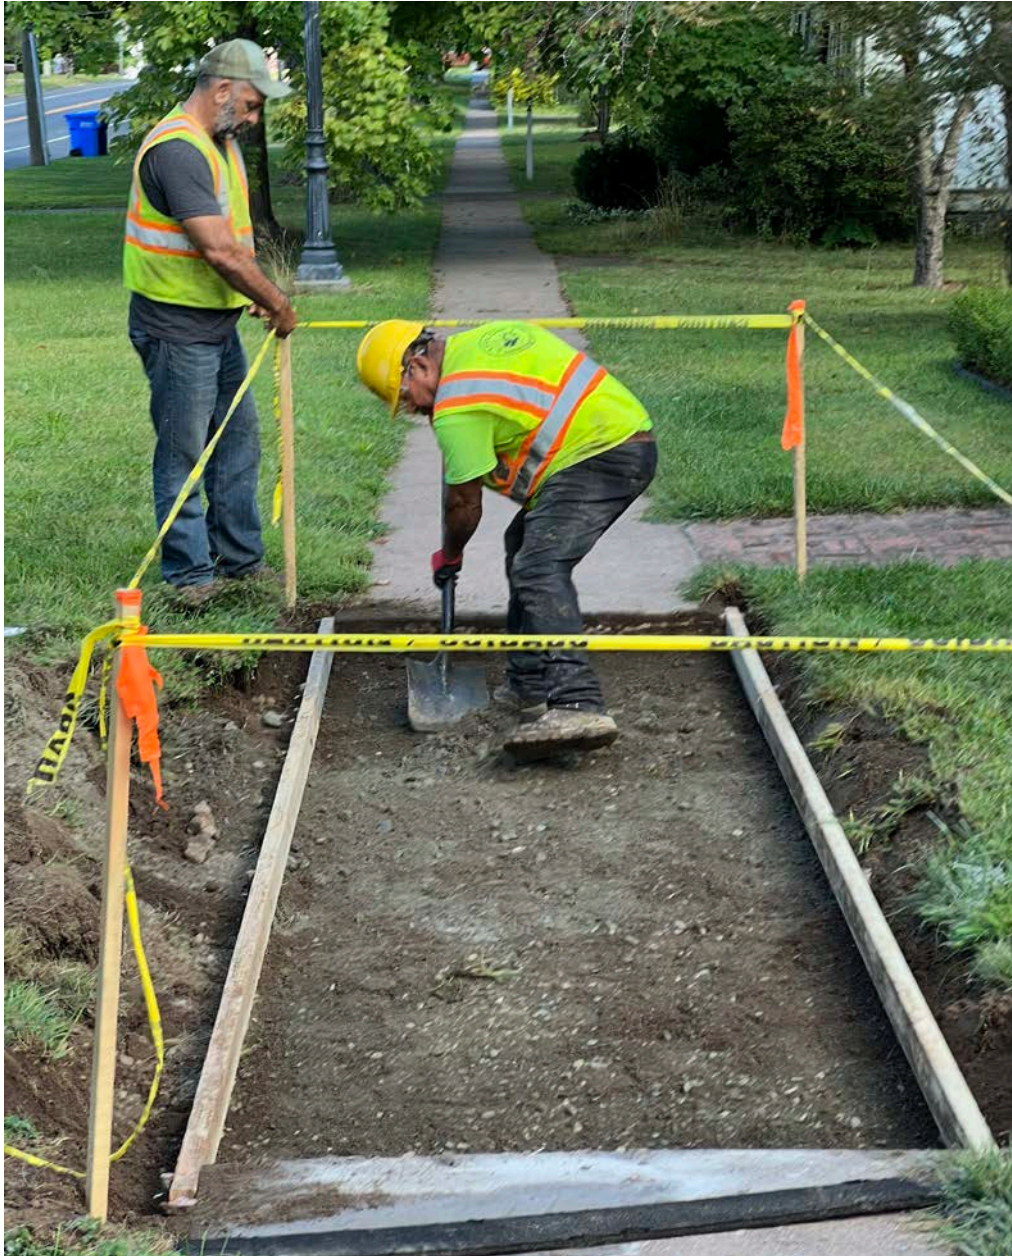

Picture 6: Ludlow Construction is excavating an area of removed sidewalk to prepare for sidewalk restoration at 297 Main Street.

Res. Representative:	<u>A.Mora</u>	Date:	<u>9/08/22</u>
-----------------------------	---------------	--------------	----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	9 of 10



Picture 7: Ludlow Construction is laying the first layer of asphalt at 126 Maple Avenue using excavator and Ludlow personnel.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	September 8, 2022
Location:	Pickett Lane, Main Street, and Maple Avenue, Durham	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	505
Contractor:	Ludlow Construction	Page:	10 of 10



Picture 8: Ludlow Construction is laying a second layer of asphalt at 126 Maple Avenue.
