

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	October 28, 2022
<b>Location:</b>	Main Street, Durham; Shared Access Driveway, Middletown	<b>Day of Week:</b>	Friday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	539
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 6

### Weather Conditions

Conditions: Daylight hours: Partly sunny. Wind variable 0-5 mph.  
 Temperature (°F): High 68°F Low 36°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	1	X	8
United Concrete	0	X	8	Foreman	1	X	8
West State Mechanical	0	X	8	Dump truck Operator	1	X	8
JTC	0	X	8	Excavator Operator	1	X	8
Grela Well Drilling	2	X	8	Skid Steer/ Bucket Loader	1	X	8
Fazzino Plumbing	0	X	8	Laborers	3	X	8
United Concrete	0	X	8	Note that some persons operate			
Knapp Engineering	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Geophysical Applications	0	x	8	Sub-contractor	2	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

### Pipe Connections, Installations, and Other Work

Ludlow performed miscellaneous activities at the Booster Station and the water tank work zone located east of the Shared Access Driveway in Middletown. Grela decommissioned the well located at the 127 Main Street, Durham, residence.

### Daily Activities – Miscellaneous activities, Middletown

Ludlow performed miscellaneous activities at the Booster Station and the water tank work zone located east of the Shared Access Driveway in Middletown.

0724: Ludlow has mobilized to the Booster Station located on S. Main Street, Middletown.

0744: Ludlow is drilling into the pavement at the Booster Station to install a stop post for the two leaves of the gate on the east side of the fence that surrounds the station.

1015: Ludlow mobilizes to the water tank work zone on the Shared Access Driveway in Middletown.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	10/28/22
-----------------------------	------------	--------------	----------

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	October 28, 2022
<b>Location:</b>	Main Street, Durham; Shared Access Driveway, Middletown	<b>Day of Week:</b>	Friday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	539
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 6

1026: Ludlow continues to work at the water tank work zone where they are currently removing silt fence located east of the water tank.

1036: Ludlow is cutting brush on the north side of the security fence that surrounds the water tank that is located east of the Shared Access Driveway. Ludlow has finished removing the silt fence that was located to the east of the water tank.

1138: Ludlow continues to clear brush at the water tank work zone.

1222: Ludlow is pressure washing the sidewalk that surrounds the water tank.

1345: Ludlow has finished pressure washing the sidewalk that surrounds the water tank.

### Daily Activities – Well decommissioning activities, Durham

Grela decommissioned the well located at the 127 Main Street, Durham, residence.

1156: Grela has mobilized to the 127 Maple Avenue, Durham, residence to decommission the well located on the west side of the house.

1236: Grela has finished decommissioning the well located inside of the 127 Main Street residence.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	10/28/22
-----------------------------	------------	--------------	----------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	October 28, 2022
<b>Location:</b>	Main Street, Durham; Shared Access Driveway, Middletown	<b>Day of Week:</b>	Friday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	539
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 6



Picture 1: Ludlow drilling a hole in the pavement at the entrance to the Booster Station in order to install a stop post. View to the northwest.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	10/28/22
-----------------------------	------------	--------------	----------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	October 28, 2022
<b>Location:</b>	Main Street, Durham; Shared Access Driveway, Middletown	<b>Day of Week:</b>	Friday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	539
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 6




Picture 2: Ludlow clearing brush on the north side of the Shared Access Road in Middletown. View to the northeast.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	10/28/22
-----------------------------	------------	--------------	----------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	October 28, 2022
<b>Location:</b>	Main Street, Durham; Shared Access Driveway, Middletown	<b>Day of Week:</b>	Friday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	539
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 6

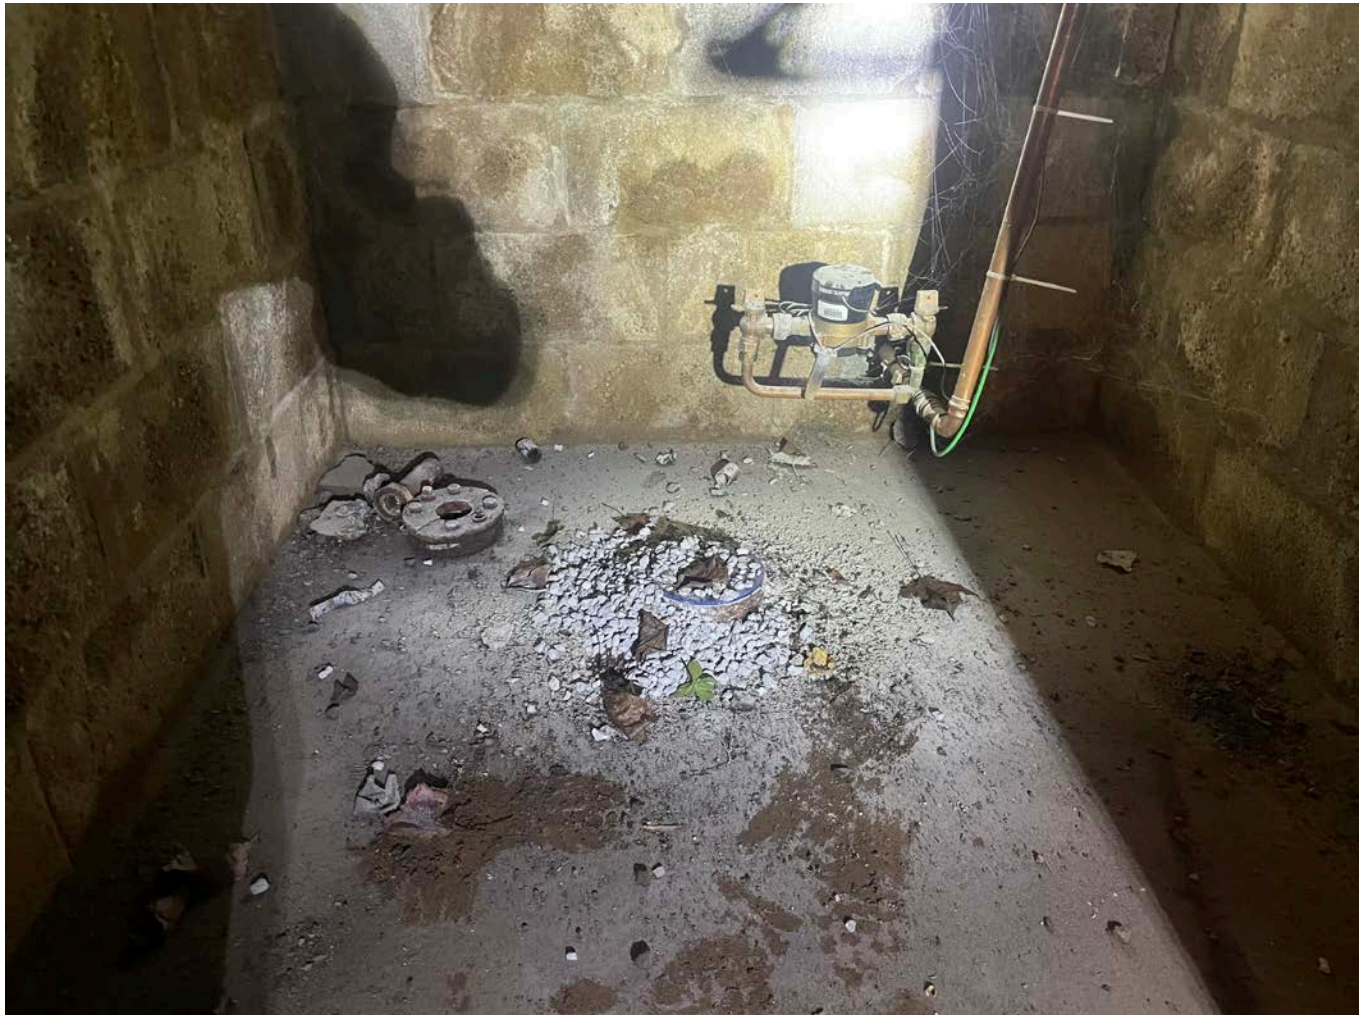

Picture 3: The well located in the basement of the 127 Main Street, Durham, residence on the west side of the foundation after Grela filled the well with bentonite chips and placed an expansion plug on the steel casing as part of well decommissioning activities. View to the west.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	10/28/22
-----------------------------	------------	--------------	----------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	October 28, 2022
<b>Location:</b>	Main Street, Durham; Shared Access Driveway, Middletown	<b>Day of Week:</b>	Friday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	539
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 6



Picture 4: Ludlow pressure washing the concrete sidewalk that surrounds the water tank located east of the Shared Access Road in Middletown. View to the south.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	10/28/22
-----------------------------	------------	--------------	----------
