



## Bi-Weekly Progress Report

### Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

May 22, 2020

#### Work Accomplished Last Two Weeks

May 8, 2020 through May 22, 2020

- Graded and paved the shared access road from Station # 20+50 to Station # 16+00. Raised catch basins at Station # 14+00, 14+37, 13+70 and 13+00 to match finish grade.
- Graded the hillside on the tank site and stabilized the area. Paved the new access road to the water tank.
- Cut open water main trench, added new material and installed new pavement on 1,976 LFT of trench on Talcott Ridge Drive and Watch Hill Drive in Middletown.
- Installed 1,306 LFT of 16" Ductile Iron Pipe (DIP) water main from Station # 184+23 to Station # 197+36 on Main Street (Rte. 17) in Durham.
- Installed 2,855 LFT of 12" DIP from Station # 501+00 to 529+55 on Pickett Lane in Durham.

#### Work Planned for Next Two Weeks:

- **May 25, 2020 to May 29, 2020:**
  - **Crew # 1** will start installing water services main to curb stop on South Main Street (Rte.17) in Middletown.
  - **Crew # 2** will continue installation of the 16" DIP on Main Street (Rte.17) in Durham during the day.
  - **Crew # 3** will continue installation of the 12" DIP on Pickett Lane in Durham.
- **June 1, 2020 to June 5, 2020**
  - **Crew # 1** will continue installing water services main to curb stop on South Main Street (Rte.17) Middletown.
  - **Crew # 2** will continue work on installing 16" DIP on Main Street (Rte.17) Durham during the day.
  - **Crew # 3** will continue the installation 12" DIP on Pickett Lane, Durham.
- Fill and Test 16" Water Main on Main Street (Rte. 17) Durham.



## Bi-Weekly Progress Report

# Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

May 22, 2020

### Construction Schedule 2019 Construction Activities:

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south almost to Royal Oak Drive in Durham.
- Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown. This work will begin at the intersection with Route 17.
- Clearing of the Water Storage Tank Site in Middletown.
- Installation of the Pressure Relief Valve and Vault

On Route 17 from  
Old Cemetery Road in Durham to Wallingford Road  
(Route 68) in Durham.

All remaining construction activities will occur in  
2020 or 2021.


## Mainline Water Line (28,272 feet total)

Start Date: September 8, 2019

Installed	
Feet	%
16,525	58.45

Ready for connection	
Feet	%
0	0.0%

Planned Work  
Location/Limits

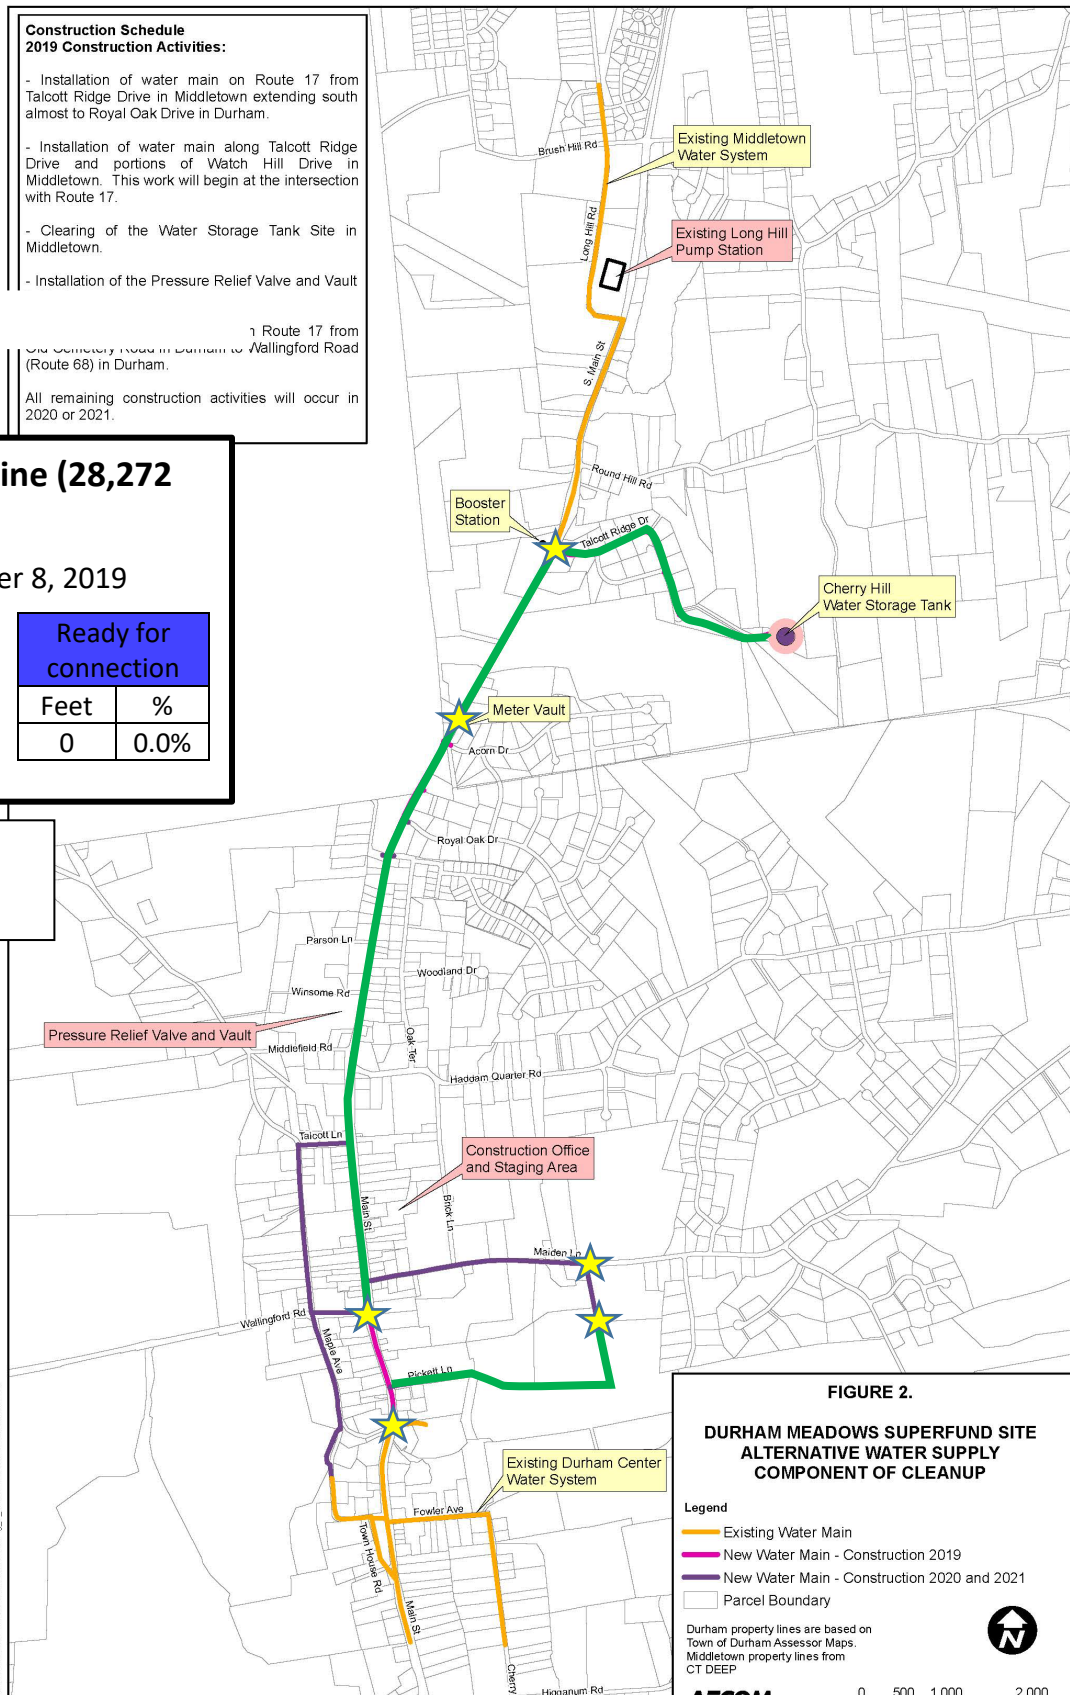



# Bi-Weekly Progress Report

## Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

May 22, 2020


### Curb Stops (211 total)

Start Date: August 24, 2020

Installed		Ready for connection	
Each	%	Each	%
0	0.0%	0	0.0%

Installed = Pipe in the ground

Ready for connection = pressure tested and chlorinated/disinfected.



### Homes Connected (115 total)


Start Date: October 27, 2020

Connected	
Homes	%
0	0.0%



### Cherry Hill Tank Construction (72 feet)

Start Date: June 11, 2020

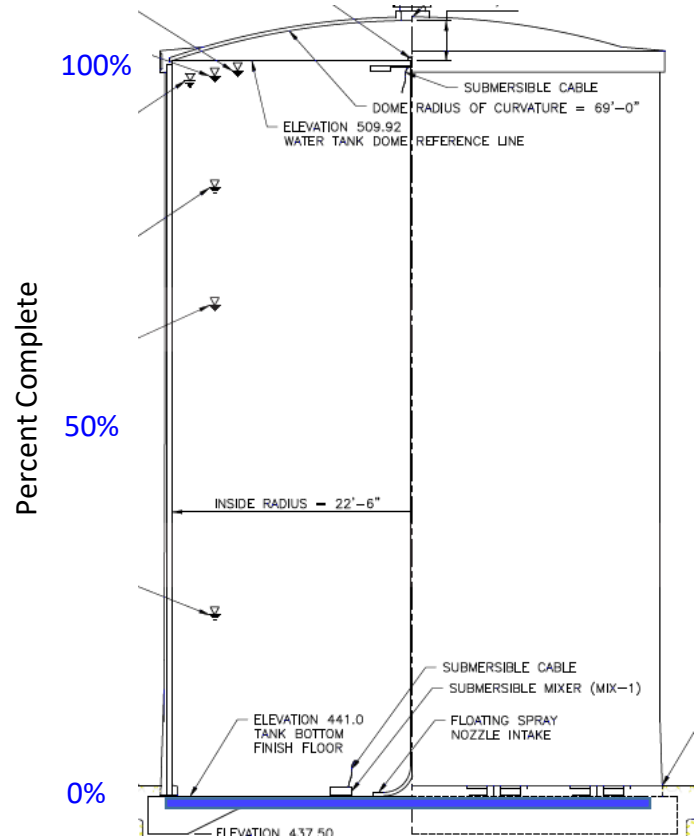



# Bi-Weekly Progress Report

## Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

May 22, 2020



Talcott Ridge Trench Pavement



Picket Lane Water Main Installation
