



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

June 19, 2020

Work Accomplished Last Two Weeks:

June 8, 2020 through June 19, 2020:

- Installed twenty (20) 1" water service main to curb stop on South Main Street (Rte.17) in Middletown.
- Installed 378 LFT. of 16" Ductile Iron Pipe (DIP) from Station # 205+47 to Station # 209+25 on Main Street (Rte. 17) in Durham.
- Installed 5 Fire Hydrants at Station #'s 194+49, 187+44, 183+57.5, 200+00 and 203+63 in Durham.
- Installed 2 Fire Hydrants at Station #'s 503+93 and 509+05 on Pickett Lane in Durham
- Installed 222 LFT. of 8" DIP on Middlefield Road (Rte. 147), Haddam Quarter Road and Talcott Lane in Durham.
- Installed 953 LFT. of 12" DIP on from Station # 600+00 to Station # 609+53 on Wallingford Road (Rte. 68) in Durham.
- Installed 40 LFT. of 4" DIP water service for the School field and 60 LFT. of 4" DIP for the High School at Station # 529+65 on Pickett Lane in Durham.

Work Planned for Next Two Weeks:

June 22, 2020 through June 26, 2020:

- Crew #1 will conduct tank site preparation in anticipation of the tank subcontractor mobilizing.
- Crew #2 will install water line crossings on Wallingford Road (Rte. 68) on Maple Avenue in Durham.
- Crew #3 will install 12" DIP on Maiden Lane, Durham

June 29, 2020 to July 3, 2020:

- Crew #1 will conduct tank site preparation in anticipation of the tank subcontractor mobilizing and will continue installing water services to curb stop on South Main Street (Rte.17) in Durham.
- Crew #2 will be installing the Stream Crossings on Pickett Lane in Durham.
- Crew #3 will install 12" DIP on Maiden Lane, Durham.



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

June 19, 2020

Figure 1: Water Main Installation Summary

Work Completed in 2019

- Installation of water main on Route 17 from Talcott Ridge Drive in Middletown extending south to just north of Middlefield Road in Durham.

- Installation of water main along Talcott Ridge Drive and portions of Watch Hill Drive in Middletown.

- Clearing of the water storage tank, meter vault, and booster station Sites in Middletown.


All remaining construction activities will occur in 2020 or 2021.

Water Line Project (28,272 feet total to install)

Start Date: September 8, 2019

Installed		Pressure tested and disinfected	
Feet	%	Feet	%
19,223	68	0	0

Anticipated work limits
for next two weeks

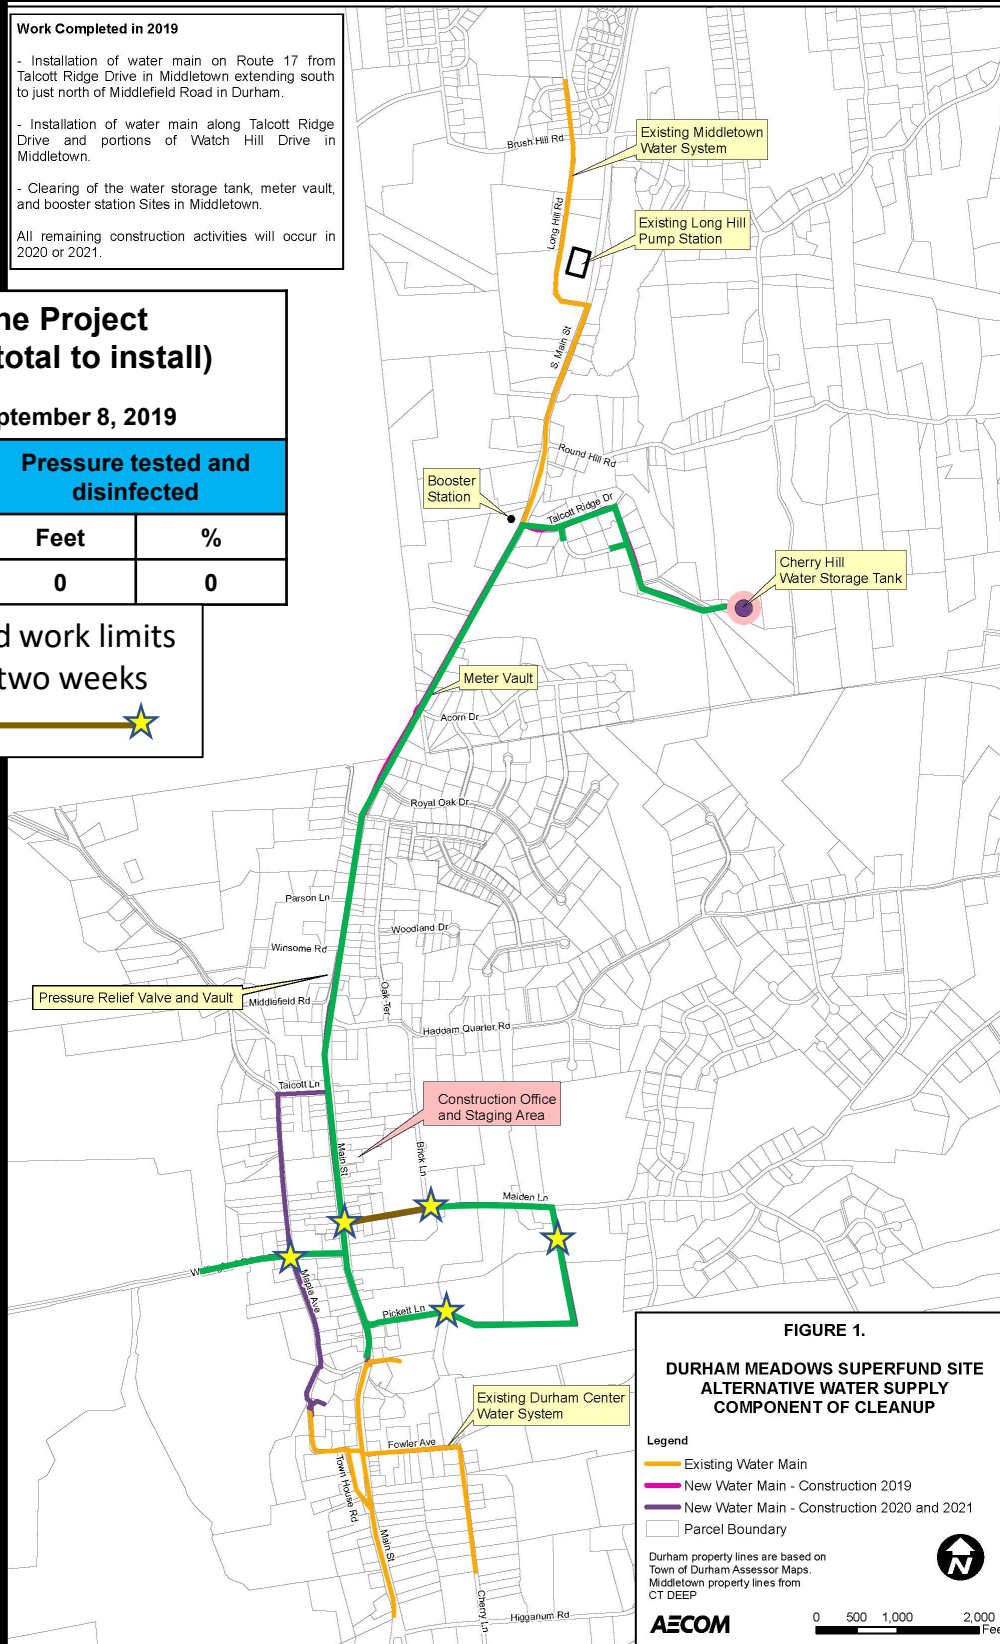



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

June 19, 2020


Figure 2: Curb Stop Installation Summary
Middletown

Curb Stops (17 total in Middletown)

Start Date: May 11, 2020

Installed		Pressure tested and disinfected	
Number	%	Number	%
17	100	0	0

Anticipated work limits
for next two weeks

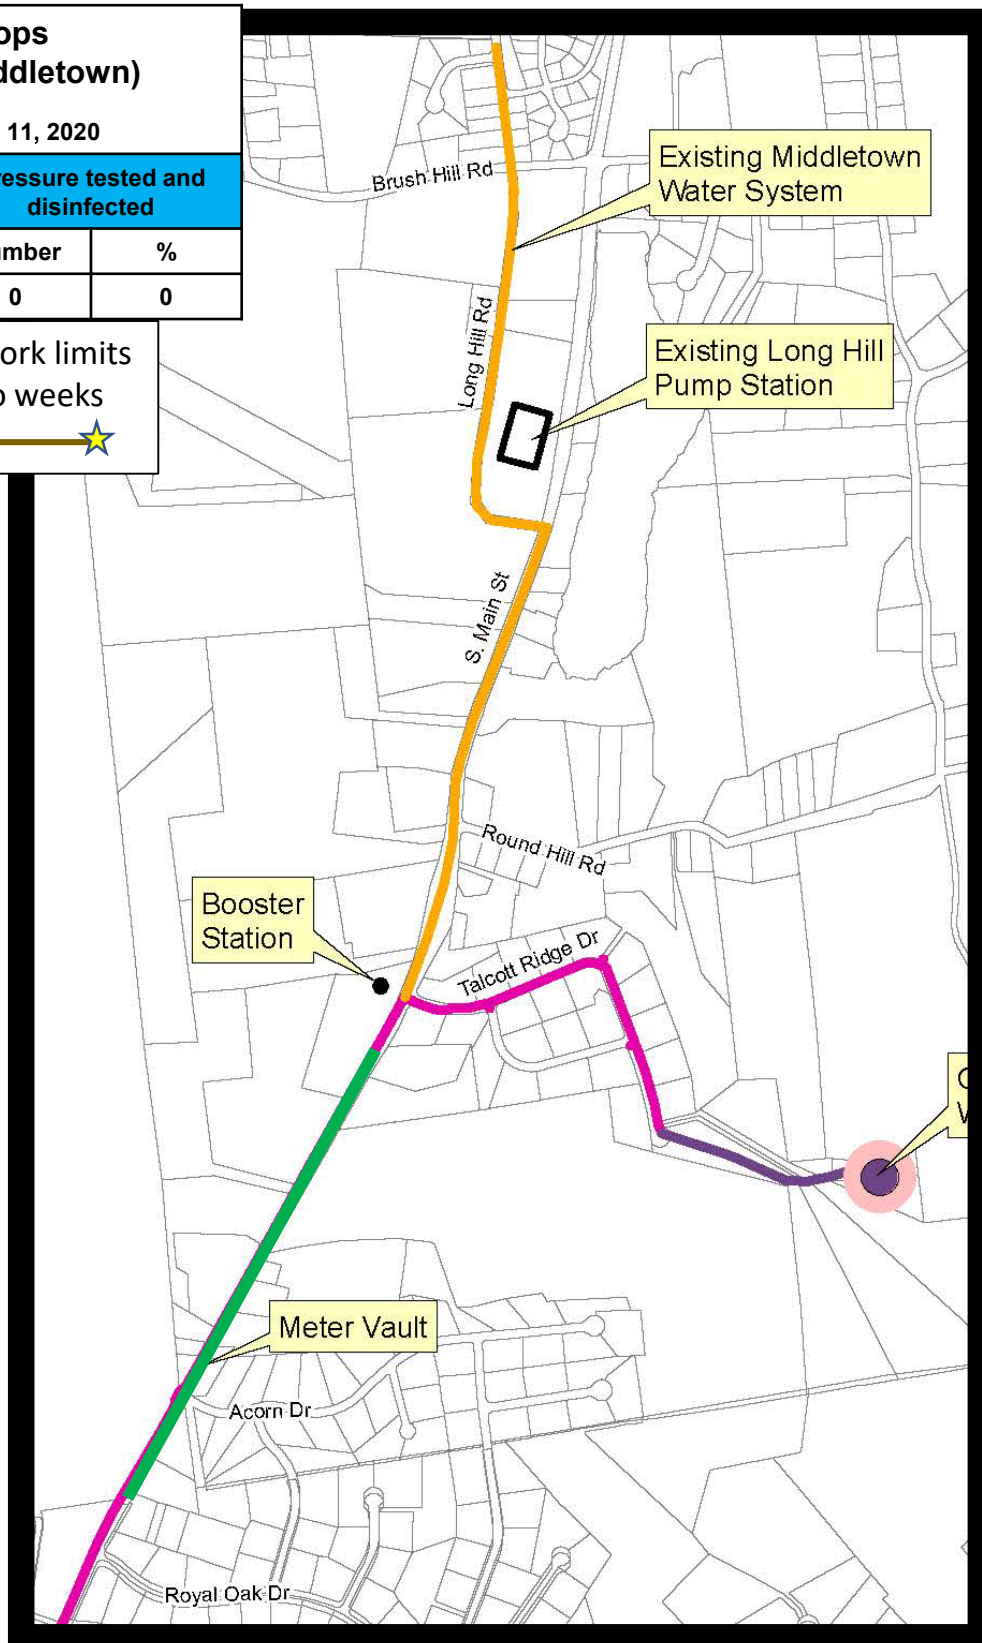




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

June 19, 2020

**Figure 3: Curb Stop Installation Summary
Durham**

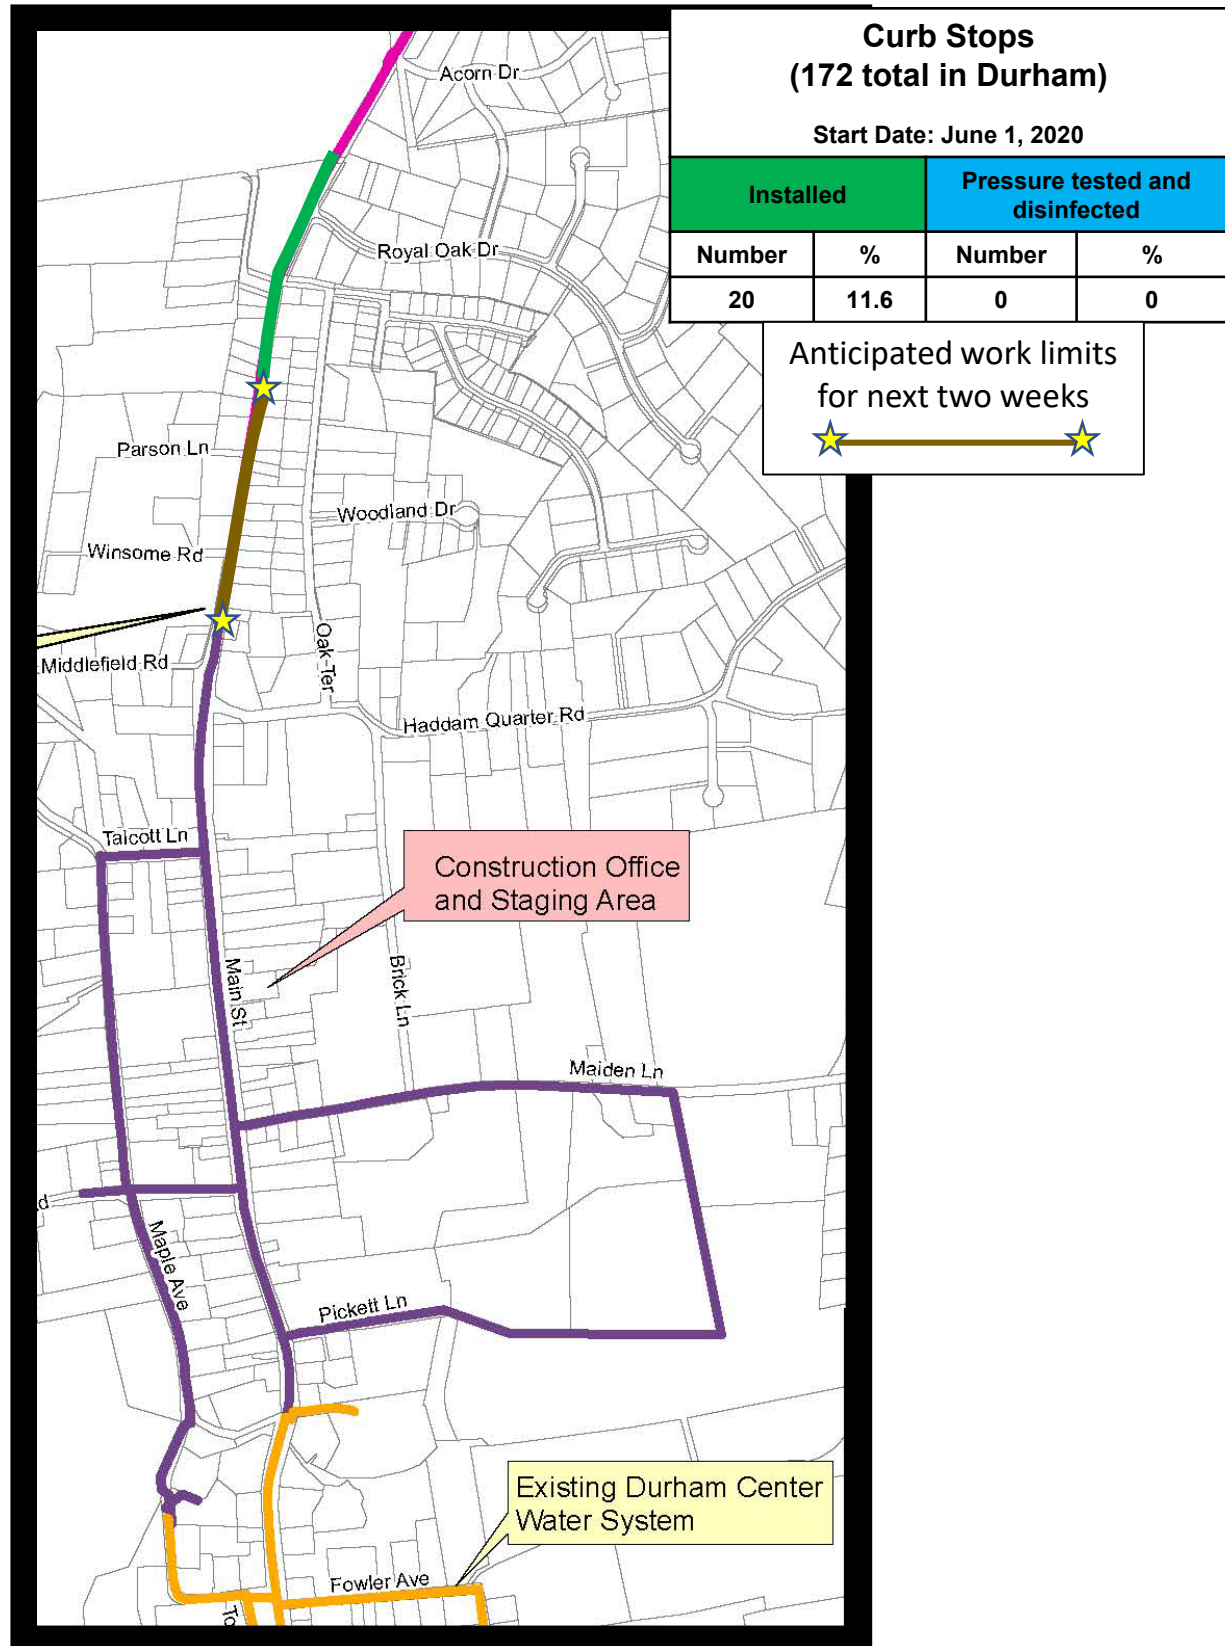




Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

June 19, 2020

Figure 4: Full Service Connection Summary
Durham

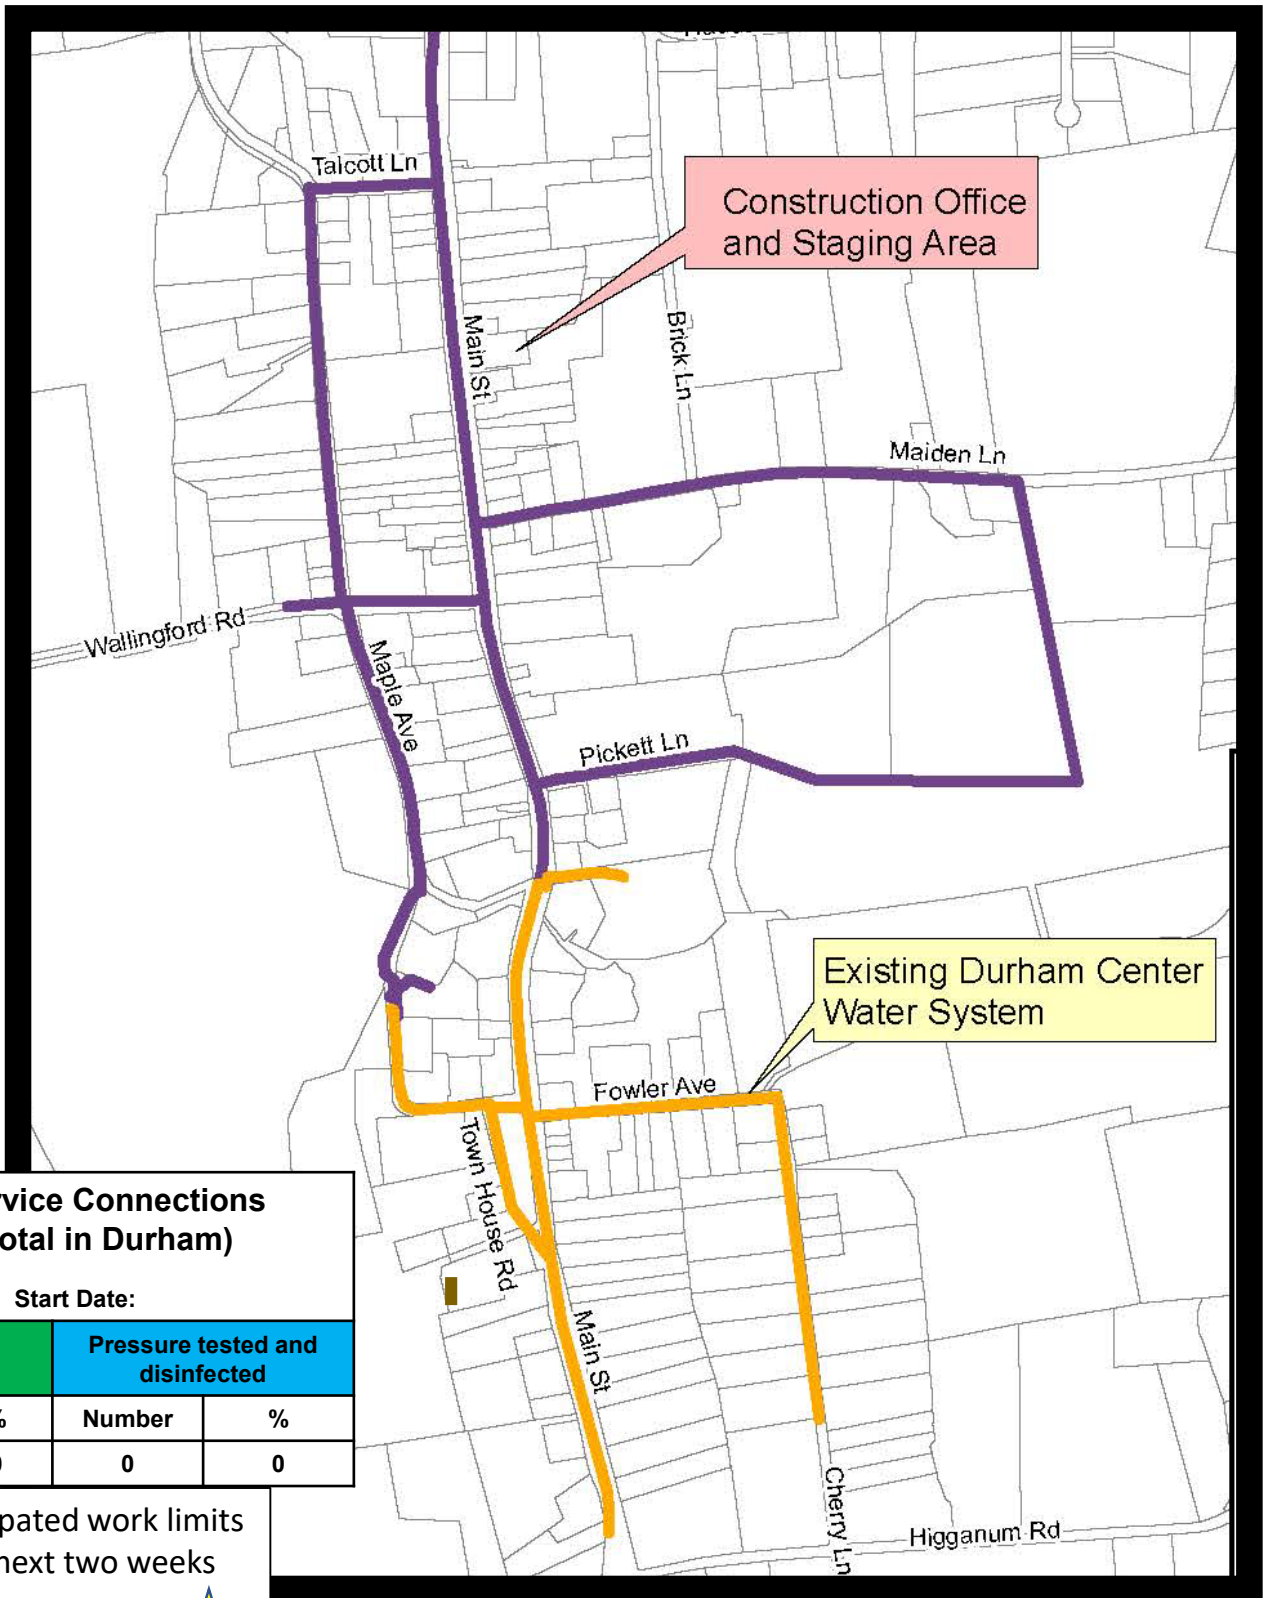

Full Service Connections (117 total in Durham)			
Start Date:			
Installed		Pressure tested and disinfected	
Number	%	Number	%
0	0	0	0

Anticipated work limits
for next two weeks

★—————★



Bi-Weekly Progress Report

Durham Meadows Superfund Project, Durham & Middletown, CT

US Army Corps of Engineers Contract No. W912WJ19C0002

June 19, 2020

Water Tank Construction (72 Feet Height)

Start Date:

Installed

Feet of Tank Height
Completed

%

0


0

100%

Percent Complete

50%

0%

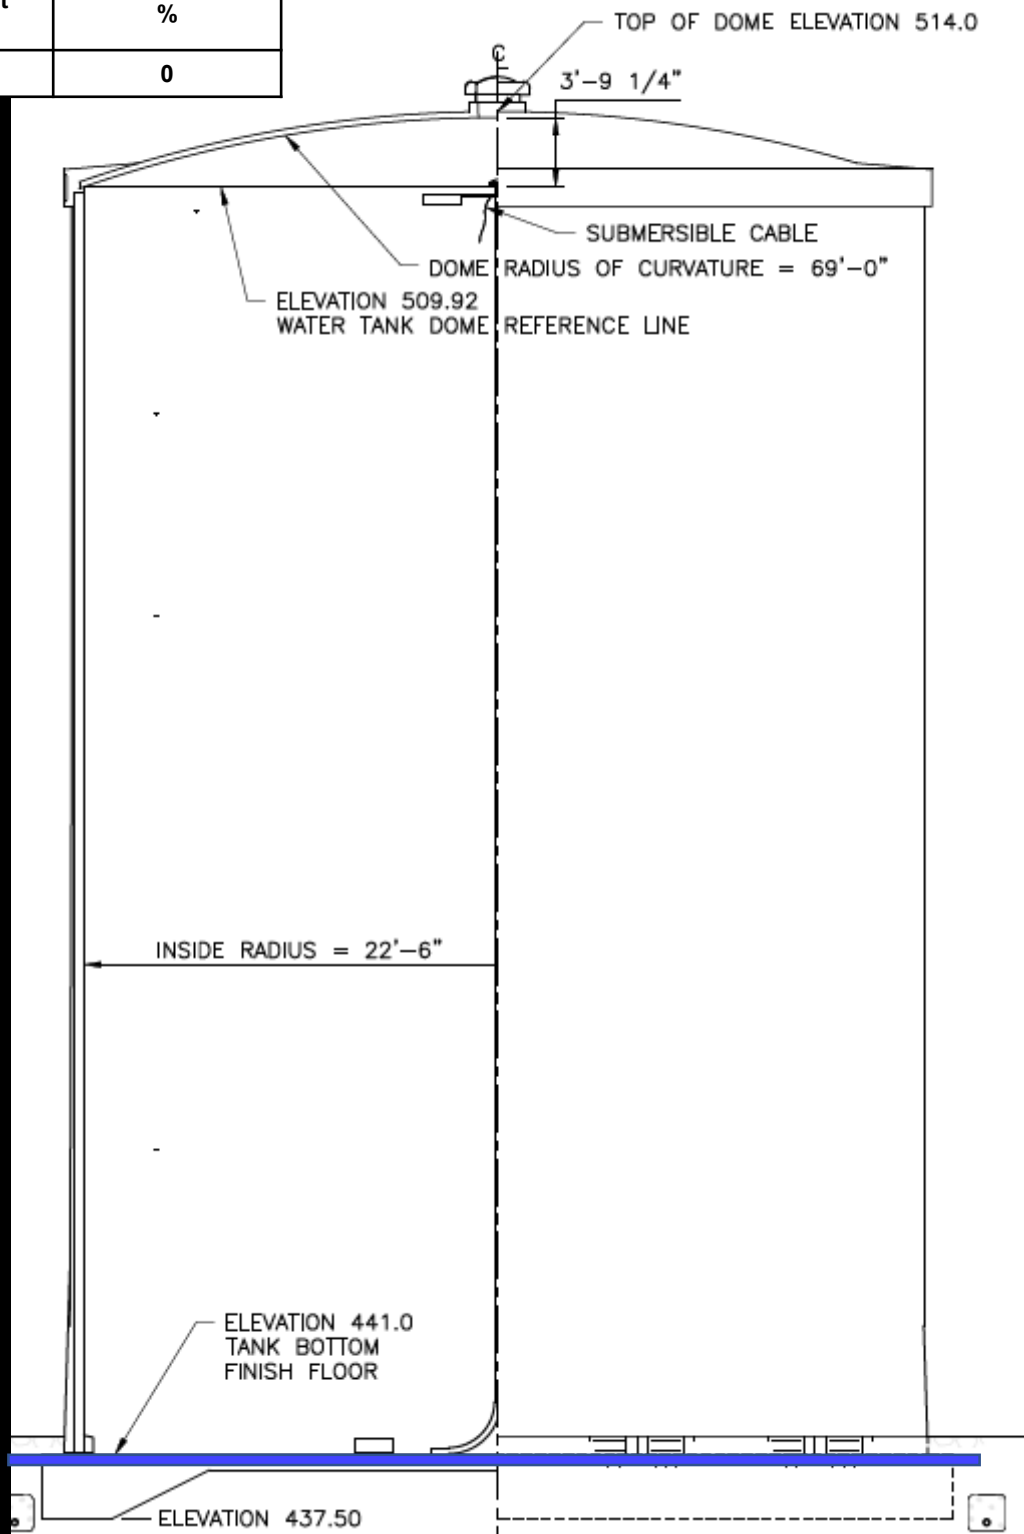



Bi-Weekly Progress Report
Durham Meadows Superfund Project, Durham & Middletown, CT
US Army Corps of Engineers Contract No. W912WJ19C0002
June 19, 2020



Ledge on route 68 in Durham

Ledge on Route 68 in Durham



Curbstop Installation
on Main Street
