

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 23, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Wednesday
Project #:	AECOM: 60445033	Report No:	17
Contractor:	Ludlow Construction	Page:	1 of 8

Weather Conditions

Conditions: Night
Temperature (°F): High 60°F Low 53°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	x	hrs
				Ludlow Construction			
				Superintendent	1	x	8
				Safety Officer	1	x	8
USACE				Dump truck Operator	3	x	8
Field Engineer	1	x	8	Excavator Operator	1	x	8
				Skid Steer Operator	1	x	8
				Laborers	4	x	8
				Sub-contractor			
				Dump truck Operator	1	x	8
				Flaggers	2	x	8
				Compression tester	1	x	8
				Middletown Police Dept.			
				Traffic officer			

Summary of Work

Visitors:

Notes:

- Starting from Sta. 129+94

- 1900 – on site
- 1910 – traffic system in place
- 1930 – starting to trench, lay pipe
- 1945 – laying geotextile and stone bedding for first section
- 1950 – 1st section in, compacting pipe bedding and laying warning tape
- 2000 – 2nd section in, compacting pipe bedding and laying warning tape
- 2030 – 3rd section in, compacting pipe bedding and laying warning tape
- 2040 – compacting over pipes 1-2, trenching for 4th section
- 2045 – 4th section in, compacting pipe bedding and laying warning tape
- 2055 – trenching for 5th section
- 2100 – backfill lift placed over pipe sections 1-2
- 2120 – 5th section in, compacting pipe bedding and laying warning tape
 - Trenching for 6th section
- 2135 – 6th section in, compacting pipe bedding and laying warning tape
- 2205 – 7th section in, compacting pipe bedding and laying warning tape
- 2220 – 8th section in, compacting pipe bedding and laying warning tape
- 2230 – placing top backfill lift over pipes 6-7
 - Compacting top backfill lift over 1-5
 - Assembling air release valve on 9th section
 - Air release valve at Sta. 130+60

Res. Representative:	F. Grimberg	Date:	10/23/19
-----------------------------	-------------	--------------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 23, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Wednesday
Project #:	AECOM: 60445033	Report No:	17
Contractor:	Ludlow Construction	Page:	2 of 8

2240 – placing backfill over 1-3
2255 – 9th pipe in, compacting pipe bedding and laying warning tape
- Air release valve attached and assembled
2300 – break time
2305 – leaving site now

Payment Items:

Res. Representative:

F. Grimberg

Date: 10/23/19

Daily Report

Project: Durham Meadows Pipeline Installation
Location: South Main Street, Middletown CT
Project #: AECOM: 60445033
Contractor: Ludlow Construction

Date: October 23, 2019
Day of Week: Wednesday
Report No: 17
Page: 3 of 8



Figure 1 – 2nd section with warning tape, 1st section with loose 1st backfill lift

Daily Report

Project: Durham Meadows Pipeline Installation
Location: South Main Street, Middletown CT
Project #: AECOM: 60445033
Contractor: Ludlow Construction

Date: October 23, 2019
Day of Week: Wednesday
Report No: 17
Page: 4 of 8

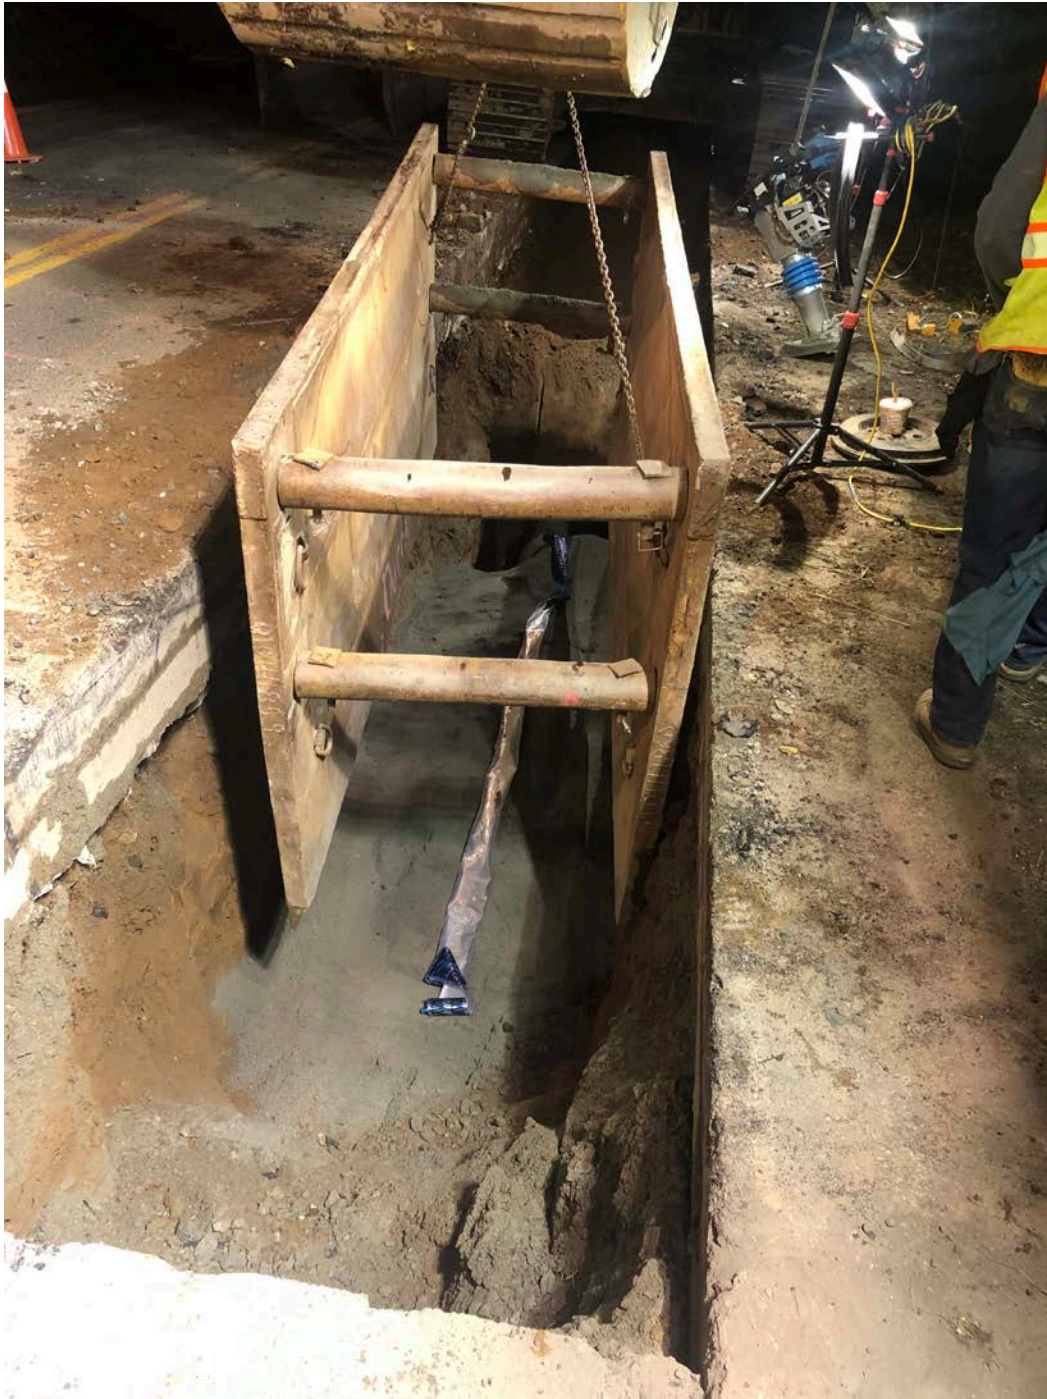


Figure 2 –First pipe in at Sta. 126+74, covered with bedding and warning tape

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 23, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Wednesday
Project #:	AECOM: 60445033	Report No:	17
Contractor:	Ludlow Construction	Page:	5 of 8



Figure 3 – Compacting top backfill lift over sections 1-7, processed aggregate pile in background

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 23, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Wednesday
Project #:	AECOM: 60445033	Report No:	17
Contractor:	Ludlow Construction	Page:	6 of 8



Figure 4 – Backfill pile at Sta. 129+94

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 23, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Wednesday
Project #:	AECOM: 60445033	Report No:	17
Contractor:	Ludlow Construction	Page:	7 of 8

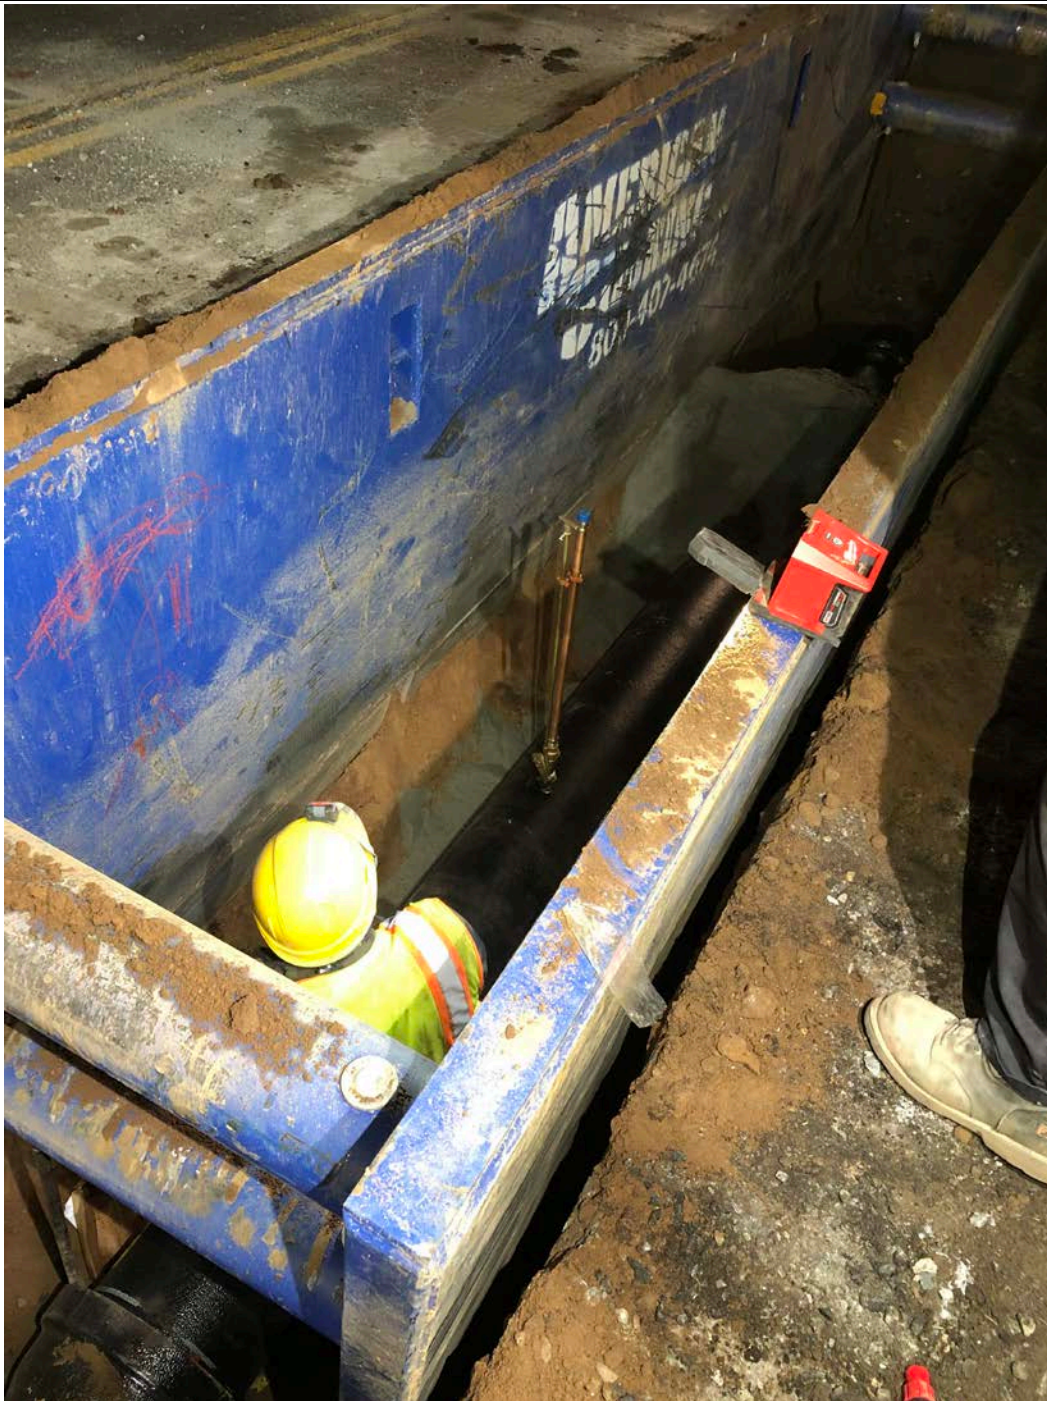


Figure 5 – Air release valve being assembled at Sta. 130+60

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 23, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Wednesday
Project #:	AECOM: 60445033	Report No:	17
Contractor:	Ludlow Construction	Page:	8 of 8



Figure 6 – Uncompact processed aggregate over sections 1-5
