

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 29, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Tuesday
Project #:	AECOM: 60445033	Report No:	20
Contractor:	Ludlow Construction	Page:	2 of 6

- Placing, compacting pipe bedding and laying warning tape
 - Placing 2nd backfill lift over 1st-4th sections
- 2230 – trenching for 8th, 9th sections
2240 – laborers taking lunch break
2250 – leaving site now

Payment Items:

Res. Representative:

F. Grimberg

Date: 10/29/19

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 29, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Tuesday
Project #:	AECOM: 60445033	Report No:	20
Contractor:	Ludlow Construction	Page:	3 of 6

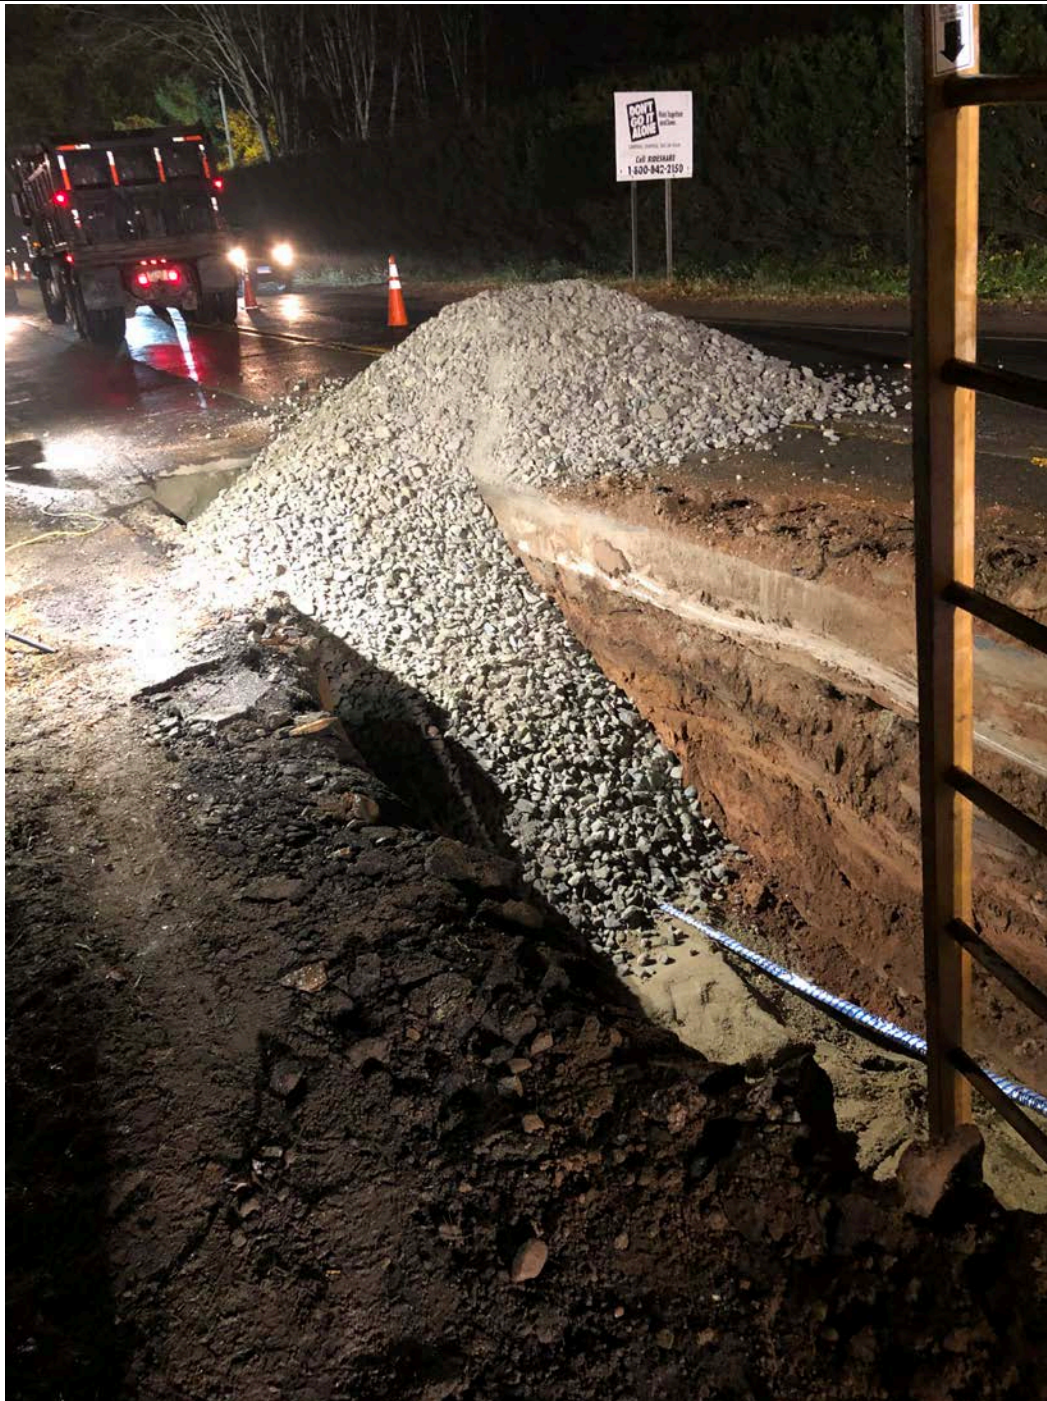


Figure 1 – Processed stone backfill pile at Sta. 134+63

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 29, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Tuesday
Project #:	AECOM: 60445033	Report No:	20
Contractor:	Ludlow Construction	Page:	4 of 6

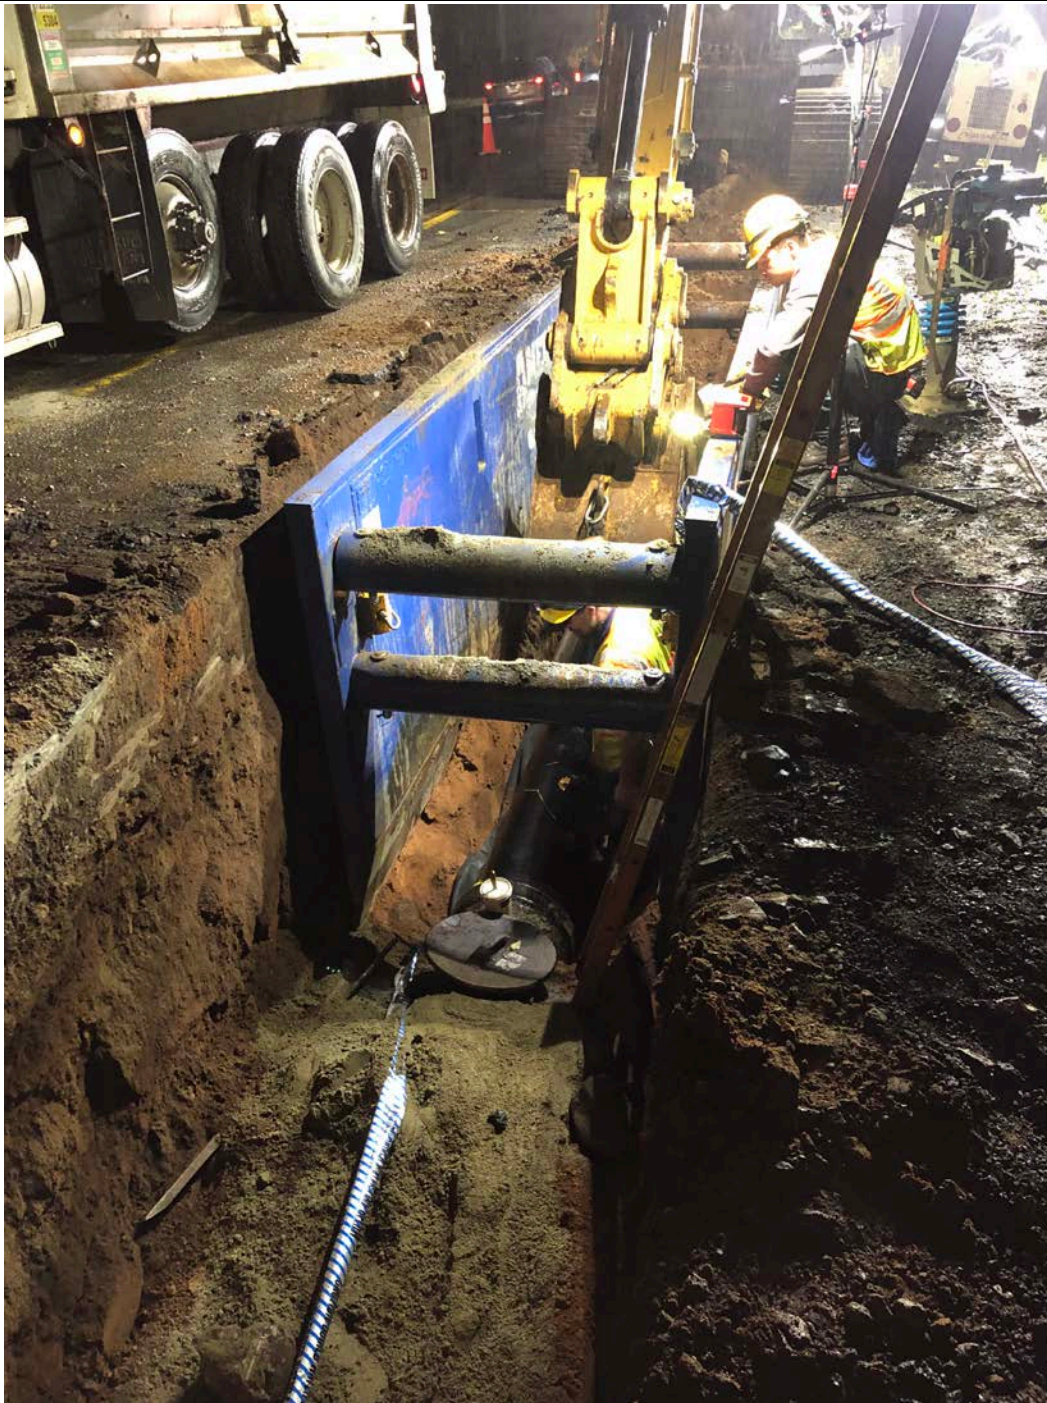


Figure 2 –Placing 3rd pipe section

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	October 29, 2019
Location:	South Main Street, Middletown CT	Day of Week:	Tuesday
Project #:	AECOM: 60445033	Report No:	20
Contractor:	Ludlow Construction	Page:	5 of 6



Figure 3 – Compacted 1st lift over section 1, warning tape laid over section 2, backfill pile at Sta. 134+63

Daily Report

Project: Durham Meadows Pipeline Installation
Location: South Main Street, Middletown CT
Project #: AECOM: 60445033
Contractor: Ludlow Construction

Date: October 29, 2019
Day of Week: Tuesday
Report No: 20
Page: 6 of 6



Figure 4 – Attaching 7th section
