

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	1 of 12

Weather Conditions

Conditions: Daylight hours: Cloudy. Winds variable 0-1 mph.
 Temperature (°F): High 52°F Low 30°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	2	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
				Foreman	1	X	8
				Dump truck Operator	0	X	8
				Excavator Operator	0	X	8
Eagle Fence	2	X	8	Skid Steer/ Bucket Loader	0	X	8
Fazzino Plumbing	2	X	8	Laborers	1	X	8
United Concrete	0	X	8	Note that some persons operate			
Frontier	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
CT Traffic Control	0	x	8	Sub-contractor	4	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Pipe Connections, Installations, and Other Work

Fazzino Plumbing worked on replacing brass tees on the final water system components they previously installed at the 13 and 146 Maple Avenue properties; 24 Maiden Lane; and 127, 253, 303, and 305 Main Street, Durham. Eagle Fence and Guardrail began work on installing a permanent fence around the water tank work zone located east of the Shared Access Driveway in Middletown.

Daily Activities – Fence installation, Shared Access Driveway, Middletown

Eagle Fence and Guardrail began work on installing a permanent fence around the water tank work zone located east of the Shared Access Driveway in Middletown.

0718: Eagle Fence and Guardrail has mobilized to the water tank work zone located east of the Shared Access Driveway in Middletown to install permanent fencing.

0737: Eagle Fence and Guardrail is currently setting up guide lines to mark out where the fence will be installed at the water tank work zone.

Res. Representative:	J. Meunier	Date:	12/14/21
-----------------------------	------------	--------------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	2 of 12

0857: Eagle Fence and Guardrail continues to set up for the installation of a permanent fence that will surround the water tank and altitude vault located east of the Shared Access Driveway in Middletown.

1025: Eagle Fence and Guardrail is using a bobcat with an auger attachment to drill holes in the ground to place fence posts as part of installing permanent fencing around the water tank work zone.

1229: Eagle Fence and Guardrail continues to drill holes in the ground to place fence posts as part of installing permanent fencing around the water tank work zone.

1422: Eagle Fence and Guardrail continues work on installing a permanent fence around the water tank work zone.

1500: Eagle Fence and Guardrail continues work on installing a permanent fence around the water tank work zone.

Daily Activities – Replacement of brass tees, Maple Avenue and Main Street, Durham

Fazzino Plumbing worked on replacing brass tees on the final water system components they previously installed at the 13 and 146 Maple Avenue properties; 24 Maiden Lane; and 127, 253, 303, and 305 Main Street, Durham.

0941: Fazzino Plumbing has mobilized to the 146 Maple Avenue residence to change out the brass tees on the final water system components they previously installed at the residence.

1018: Fazzino Plumbing has finished changing out the brass tees on the final water system components they previously installed at the 146 Maple Avenue residence and is preparing to mobilize to the 24 Maiden Lane residence.

1128: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 303 Main Street residence.

1210: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 305 Main Street residence.

1258: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 127 Main Street residence.

1357: Fazzino Plumbing has finished changing out the brass tees on the final water system components they previously installed at the 127 Main Street residence.

1413: Fazzino has just mobilized to the 253 Main Street property to change out the brass tees on the final water system components they previously installed at the residence.

1435: Fazzino Plumbing continues to change out the brass tees on the final water system components they previously installed at the 253 Main Street residence.

1523: Fazzino Plumbing is changing out the brass tees on the final water system components they previously installed at the 13 Maple Avenue residence.

Res. Representative:	J. Meunier	Date:	12/14/21
-----------------------------	------------	--------------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	3 of 12



Picture 1: Ludlow grinding the top of a road box on Brick Lane to lower the profile of the lip. View to the west.

Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	4 of 12



Picture 2: Eagle Fence and Guardrail drilling a hole for the installation of a fence post to the northeast of the water tank located east of the Shared Access Driveway in Middletown. View to the north.

Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	5 of 12



Picture 3: Eagle Fence and Guardrail drilling holes for the installation of fence posts to the south of the water tank located east of the Shared Access Driveway in Middletown. View to the west.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	6 of 12



Picture 4: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 146 Maple Avenue, Durham, residence.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	7 of 12



Picture 5: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 24 Maiden Lane, Street, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	8 of 12



Picture 6: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 303 Main Street, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	9 of 12



Picture 7: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 305 Main Street, Durham, residence.

Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	10 of 12



Picture 8: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 127 Main Street, Durham, property.


Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	11 of 12

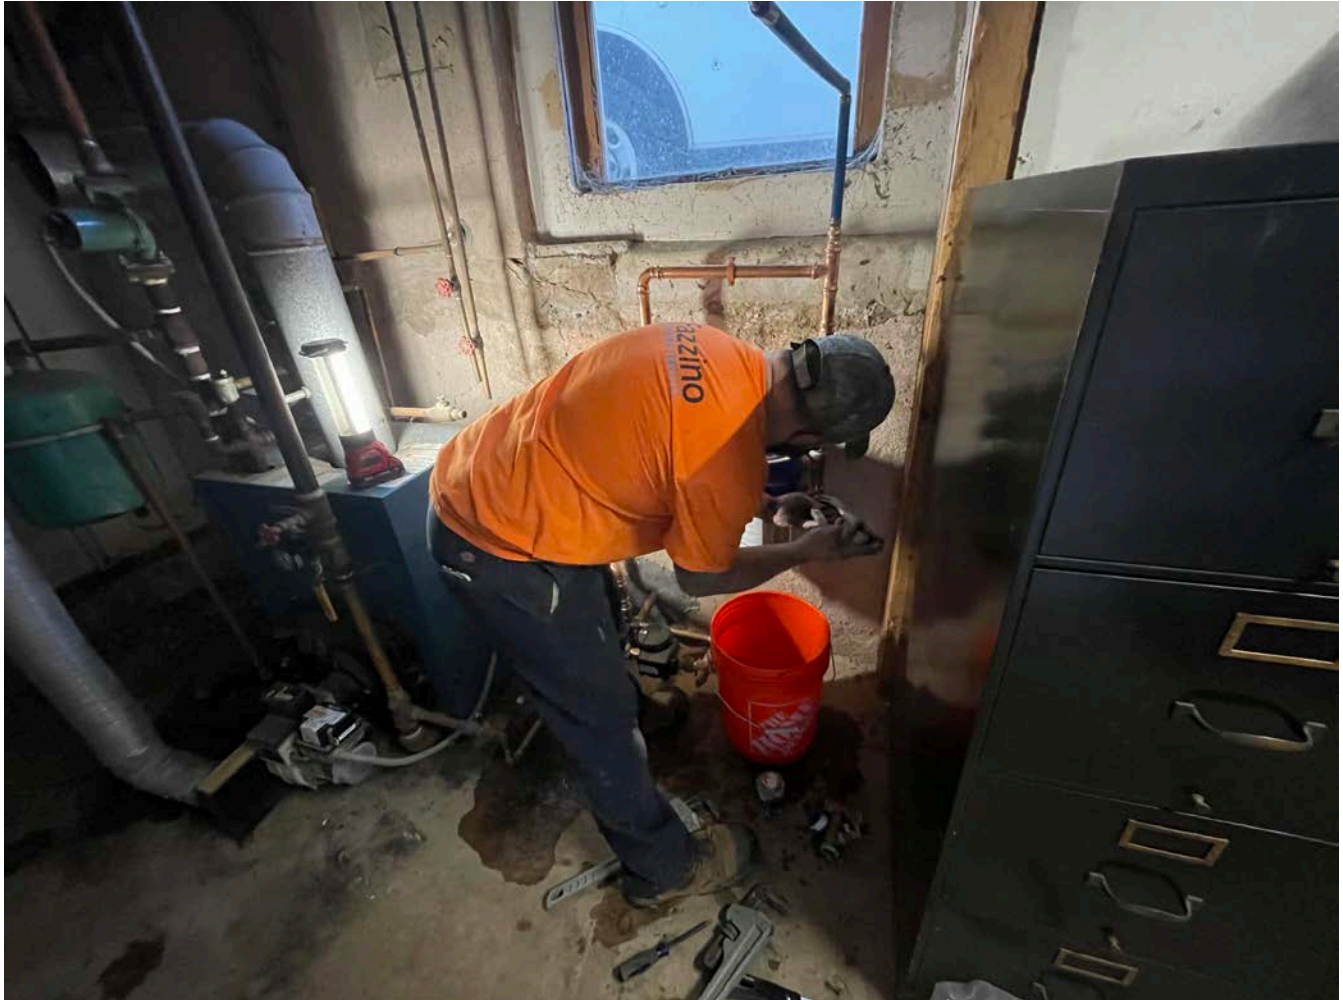

Picture 9: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 253 Main Street, Durham, property.

Res. Representative:

J. Meunier

Date: 12/14/21

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	December 14, 2021
Location:	Main Street, Maiden Lane, and Maple Avenue, Durham; Shared Access Driveway, Middletown	Day of Week:	Tuesday
Project #:	AECOM: 6061487	Report No:	382
Contractor:	Ludlow Construction	Page:	12 of 12



Picture 10: Fazzino Plumbing replacing the brass tees on the final water service components that they previously installed at the 13 Maple Avenue, Durham, property.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>12/14/21</u>
-----------------------------	-------------------	--------------	-----------------
