

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	1 of 9

Weather Conditions			
Conditions:	Daylight hours: Cloudy. Winds variable 0-7 mph.		
Temperature (°F):	High 63°F	Low	46°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
				Foreman	1	X	8
				Dump truck Operator	0	X	8
				Excavator Operator	0	X	8
Knapp Engineering	1	X	8	Skid Steer/ Bucket Loader	0	X	8
Fazzino Plumbing	2	X	8	Laborers	0	X	8
United Concrete	0	X	8	Note that some persons operate			
Frontier	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
CT Traffic Control	0	x	8	Sub-contractor	3	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Pipe Connections, Installations, and Other Work

Fazzino Plumbing installed final water service components at the 176, 184, and 244 Main Street, Durham, residences. Knapp Engineering worked on the communication system inside of the water meter building.

Daily Activities – Full water service installation activities, Main Street, Durham

Fazzino Plumbing installed final water service components at the 176, 184, and 244 Main Street, Durham, residences.

0756: One of the plumbers from Fazzino Plumbing arrives at the 244 Maple Avenue, Durham, residence to install final water service components.

0811: A second plumber from Fazzino Plumbing arrives at the 244 Maple Avenue, Durham, residence.

0905: Fazzino Plumbing continues work on installing final water service components at the 244 Maple Avenue residence.

0954: Fazzino Plumbing is finishing the installation of final water service components at the 244 Maple Avenue residence. The water pressure being delivered to the house is slightly under 60 PSI.

Res. Representative:	J. Meunier	Date:	03/07/22
-----------------------------	------------	--------------	----------

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	2 of 9

1015: Fazzino Plumbing arrives at the 184 Maple Avenue, Durham, residence to install final water service components.

1122: Fazzino Plumbing is removing the hydropneumatic tank from the basement of the 184 Maple Avenue residence.

1134: Fazzino Plumbing continues to work on installing new water service components at the 184 Maple Avenue residence. The water pressure being delivered to the house is 60 PSI.

1154: Fazzino Plumbing has finished the installation of final water service components at the 184 Maple Avenue residence. Fazzino has attempted to contact the owners of the 176 Maple Avenue, Durham, residence (which is the next residence that Fazzino is scheduled to work at today) but were unable to make contact with the property owner.

1214: Fazzino Plumbing is waiting to gain entrance to the 176 Maple Avenue residence.

1258: Fazzino Plumbing has made entrance to the 176 Maple Avenue residence and has begun work on installing final water service components.

1343: Fazzino Plumbing has had to shift the location of some of the final water service components from the northeast corner of the basement at the 176 Maple Avenue residence (due to the presence of an electrical panel and an oil tank) to the west wall of the home's basement. Moving these components necessitates the installation of additional copper water line between the copper water service line that enters the home on the eastern foundation the filter assembly that is part of the final water service components being installed today.

1513: Fazzino Plumbing is finishing up the installation of final water service components at the 176 Maple Avenue residence.

Daily Activities – Water meter building, S. Main Street, Middletown

Knapp Engineering worked on the instrumentation system inside of the water meter building.

Res. Representative:	J. Meunier	Date:	03/07/22
-----------------------------	------------	--------------	----------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	3 of 9



Picture 1: Final water system components at the 244 Maple Avenue, Durham, residence being installed by Fazzino Plumbing.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	4 of 9



Picture 2: Final water system components installed at the 244 Maple Avenue, Durham, residence by Fazzino Plumbing.

Res. Representative:

J. Meunier

Date: 03/07/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	5 of 9



Picture 3: Final water system components at the 184 Maple Avenue, Durham, residence being installed by Fazzino Plumbing.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>03/07/22</u>
-----------------------------	-------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	6 of 9



Picture 4: Final water system components at the 184 Maple Avenue, Durham, residence installed by Fazzino Plumbing.


Res. Representative:

J. Meunier

Date: 03/07/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	7 of 9

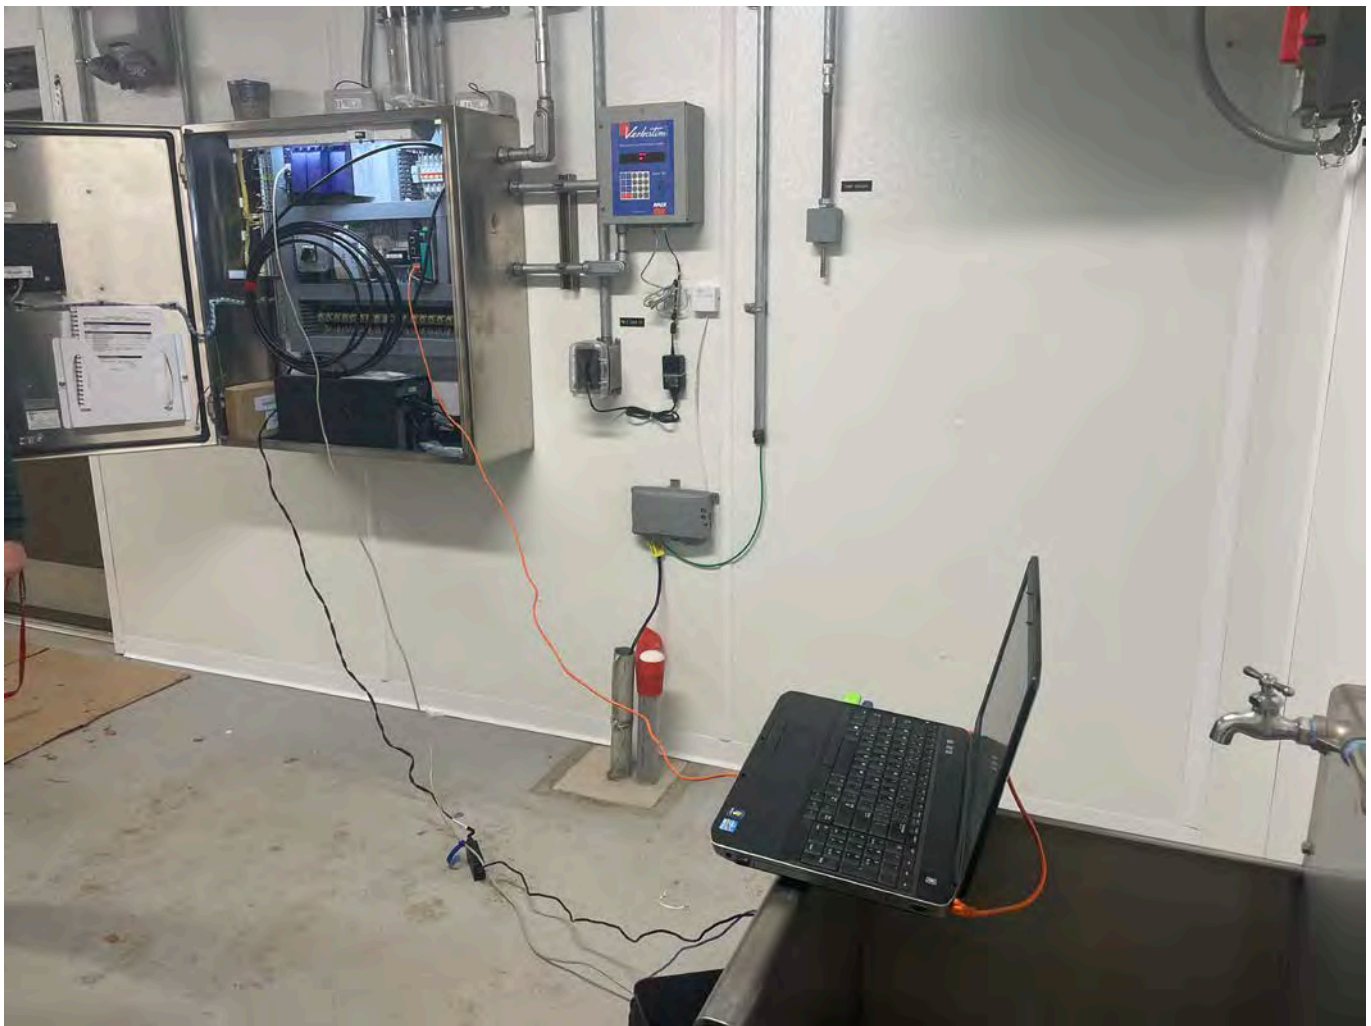

Picture 5: Knapp Engineering is currently working on the instrumentation system inside of the water meter vault. View to the west.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	8 of 9



Picture 6: Final water system components at the 176 Maple Avenue, Durham, residence being installed by Fazzino Plumbing. View to the northwest

Res. Representative:	<u>J. Meunier</u>	Date:	<u>03/07/22</u>
-----------------------------	-------------------	--------------	-----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	March 7, 2022
Location:	Maple Avenue Durham; S. Main Street, Middletown	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	389
Contractor:	Ludlow Construction	Page:	9 of 9



Picture 7: Water service line entering the east wall of the foundation at 176 Maple Avenue. The breaker panel that obstructed the original spot selected for the installation of the final water service components is visible at the top of the photograph.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>03/07/22</u>
-----------------------------	-------------------	--------------	-----------------
