

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	March 21, 2022
<b>Location:</b>	Maple Avenue, Durham	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	397
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 6

### Weather Conditions

Conditions: Daylight hours: Overcast/rainy. Wind variable 0-10 mph.  
 Temperature (°F): High 51°F Low 34°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
				Foreman	1	X	8
				Dump truck Operator	0	X	8
				Excavator Operator	0	X	8
Knapp Engineering	0	X	8	Skid Steer/Bucket Loader	0	X	8
Fazzino Plumbing	2	X	8	Laborers	0	X	8
United Concrete	0	X	8	Note that some persons operate			
Frontier	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
CT Traffic Control	0	x	8	Sub-contractor	2	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

### Pipe Connections, Installations, and Other Work

Fazzino Plumbing installed final water service components at the residences located at 166 and 230 Maple Avenue.

### Daily Activities – Full water service installation activities, Durham

Fazzino Plumbing installed final water service components at the residences located at 166 and 230 Maple Avenue.

0814: AECOM arrives at the 166 Maple Avenue, Durham, residence, where Fazzino Plumbing will be installing final water service components.

0921: Fazzino Plumbing has begun the installation of final water service components at the 166 Maple Avenue residence.

1032: Fazzino Plumbing continues with the installation of final water service components at the 166 Maple Avenue residence.

1128: Fazzino Plumbing continues with the installation of final water service components at the 166 Maple Avenue residence. The final water system components are being installed in the north west corner of the home's basement on the north wall. The

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	3/21/22
-----------------------------	------------	--------------	---------

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	March 21, 2022
<b>Location:</b>	Maple Avenue, Durham	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	397
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 6

PVC blank where the water meter will be installed has been placed on the foundation's east wall, where the 1" water service pipe enters the basement.

1214: Fazzino Plumbing continues with the installation of final water service components at the 166 Maple Avenue residence.

1246: Fazzino Plumbing just charged the new system at the 166 Maple Avenue residence with water and is checking for leaks.

1300: Fazzino Plumbing has completed the installation of final water service components at the 166 Maple Avenue residence and is preparing to depart.

1319: Fazzino Plumbing has mobilized to the residence located at 230 Maple Avenue, Durham, to begin the installation of final water system components.

1352: Fazzino Plumbing continues to install final water service components at the 230 Maple Avenue, Durham, residence.


1437: Fazzino Plumbing continues to install final water service components at the 230 Maple Avenue residence.

1503: Fazzino Plumbing has partially installed final water service components at the 230 Maple Avenue residence. Fazzino will return to finish installation activities on Thursday of this week.

<b>Res. Representative:</b>	<u>J. Meunier</u>	<b>Date:</b>	<u>3/21/22</u>
-----------------------------	-------------------	--------------	----------------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	March 21, 2022
<b>Location:</b>	Maple Avenue, Durham	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	397
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 6

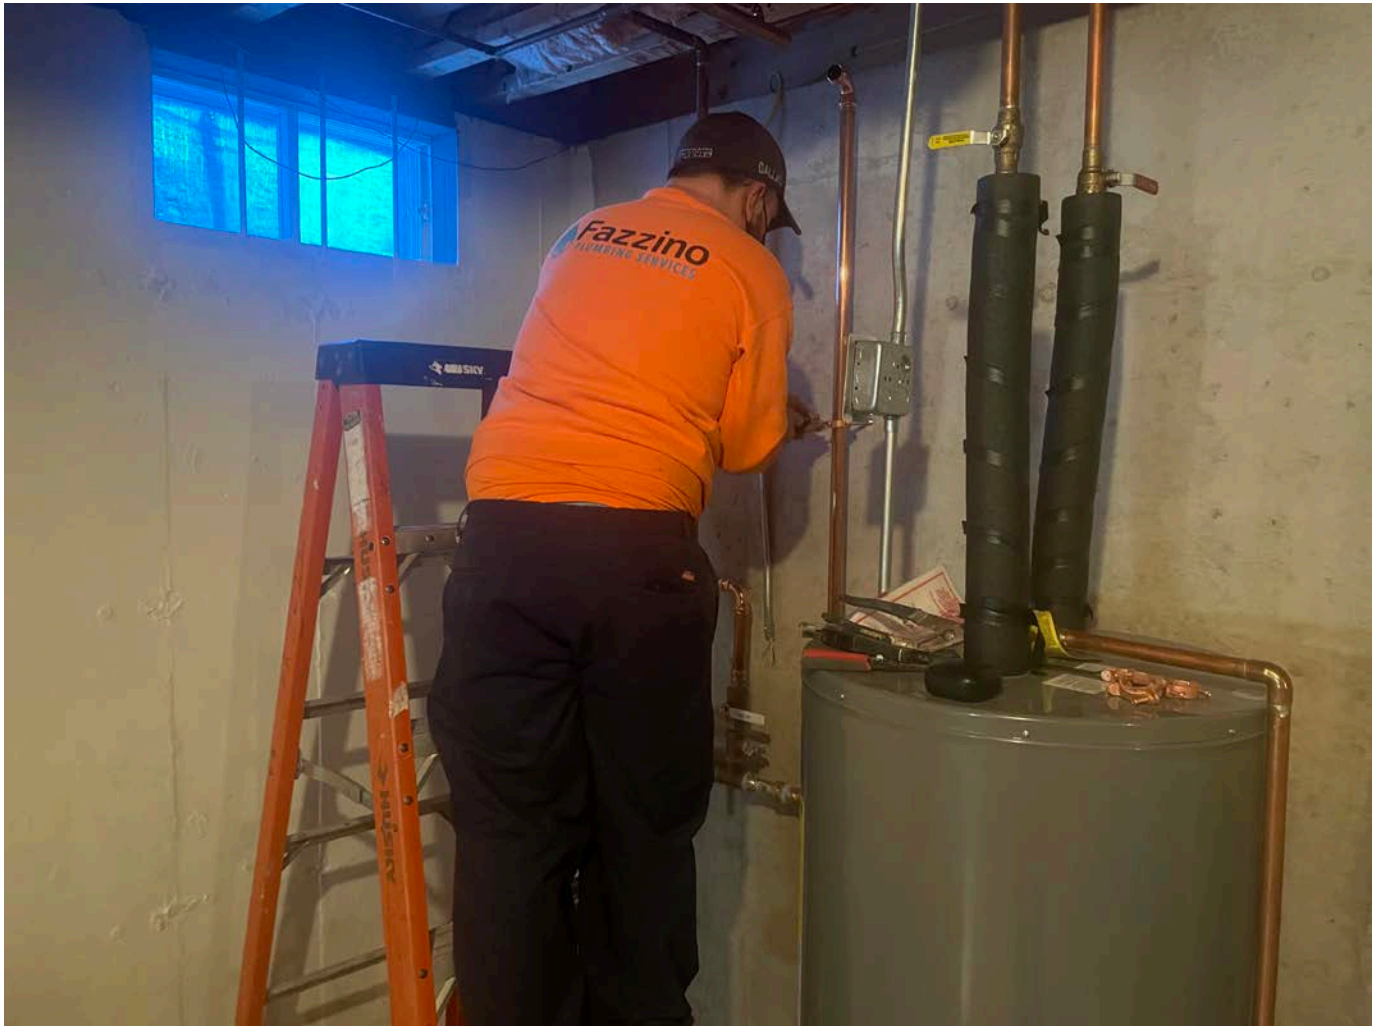

Picture 1: Final water system components at the 166 Maple Avenue, Durham, residence being installed by Fazzino Plumbing.


Res. Representative:

J. Meunier

Date: 3/21/22

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	March 21, 2022
<b>Location:</b>	Maple Avenue, Durham	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	397
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 6

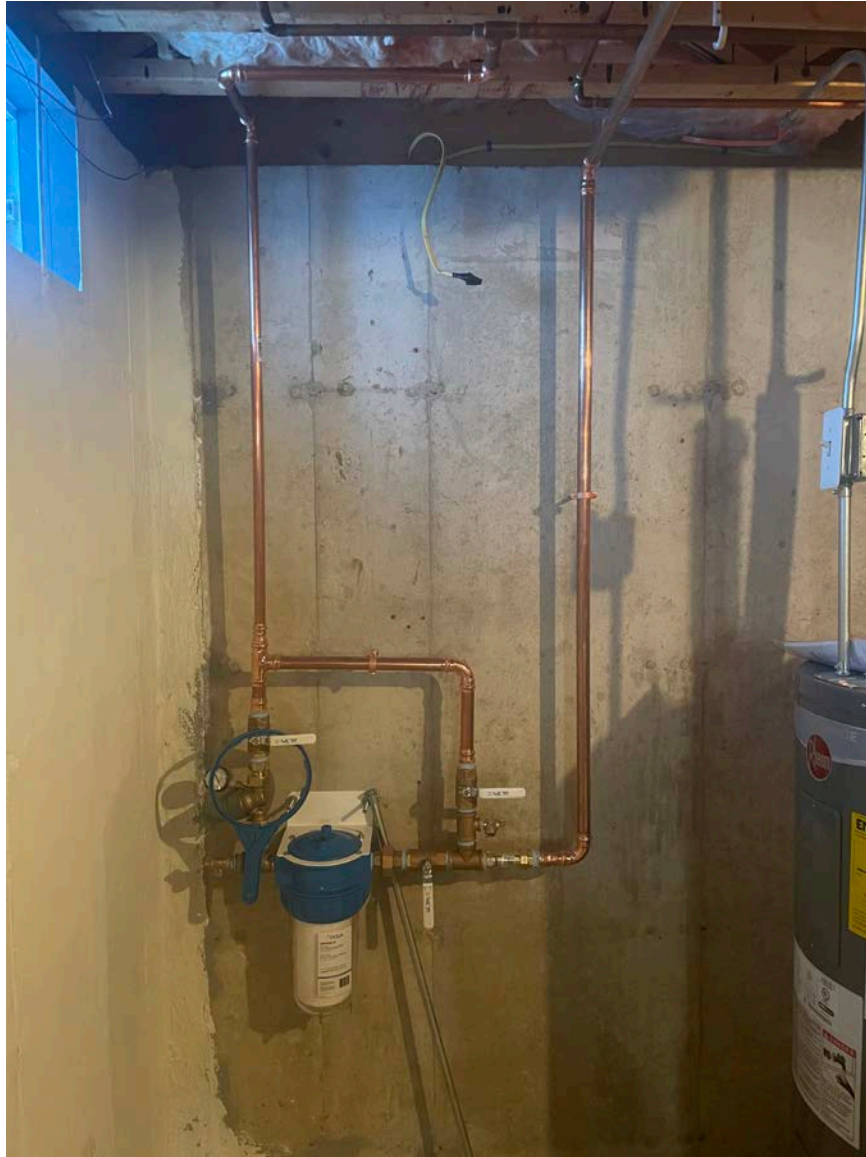

**Picture 2: Final water system components that were installed at the 166 Maple Avenue, Durham, residence by Fazzino Plumbing.**

**Res. Representative:**

J. Meunier

**Date:** 3/21/22

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	March 21, 2022
<b>Location:</b>	Maple Avenue, Durham	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	397
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 6




**Picture 3: Fazzino Plumbing inspecting the final water system components they installed today at the 166 Maple Avenue residence in Durham.**



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	March 21, 2022
<b>Location:</b>	Maple Avenue, Durham	<b>Day of Week:</b>	Monday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	397
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 6

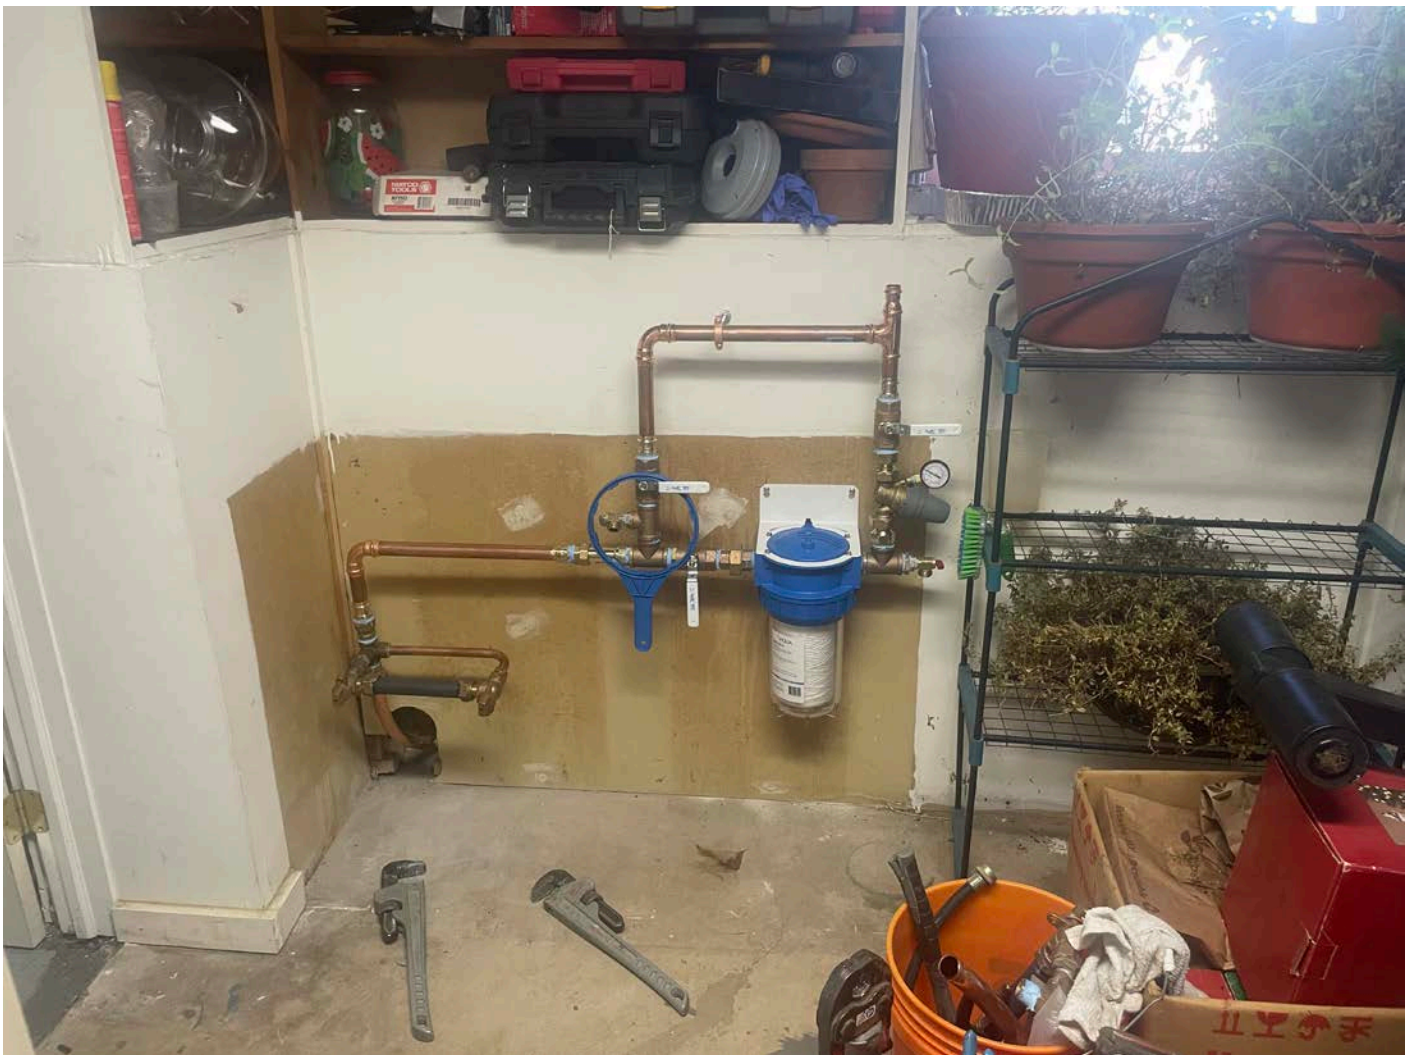

Picture 4: Partial installation of final water system components at the 230 Maple Avenue, Durham, residence by Fazzino Plumbing.

Res. Representative:

J. Meunier

Date: 3/21/22
