

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	1 of 9

Weather Conditions

Conditions: Daylight hours: Mostly sunny. Wind variable 0-7 mph.
 Temperature (°F): High 81°F Low 54°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
				Foreman	1	X	8
				Dump truck Operator	0	X	8
John Turner Consulting	0	x	8	Excavator Operator	1	X	8
Grela Well Drilling	0	x	8	Skid Steer/ Bucket Loader	0	X	8
Fazzino Plumbing	0	x	8	Laborers	2	X	8
United Concrete	0	x	8	Note that some persons operate			
Knapp Engineering	1	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Harper Haines	0	x	8	Sub-contractor	1	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Pipe Connections, Installations, and Other Work

Ludlow finished work on the sidewalk they constructed around the perimeter of the water tank located east of the Shared Access Driveway in Middletown. Ludlow finished placing 3/8" rock on top of black geofabric at the toe of the chain-link fence that surrounds the water tank. Ludlow compacted the fill surrounding the water tank to prepare for the placement of pavement later this month. Knapp Engineering worked at the Long Hill pump station

Daily Activities – Water tank work zone, Shared Access Driveway, Middletown

Ludlow finished work on the sidewalk they constructed around the perimeter of the water tank located east of the Shared Access Driveway in Middletown. Ludlow finished placing 3/8" rock on top of black geofabric at the toe of the chain-link fence that surrounds the water tank. Ludlow compacted the fill surrounding the water tank to prepare for the placement of pavement later this month.

0702: Ludlow has mobilized to the water tank work zone located east of the Shared Access Driveway in Middletown.

Res. Representative:	J. Meunier	Date:	5/12/22
-----------------------------	------------	--------------	---------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	2 of 9

0717: Ludlow begins to demobilize unused materials from the water tank work zone. Ludlow is sweeping the panels of concrete that they poured yesterday as they prepare to spray Cure Shield X onto the panels.

0733: Ludlow is removing the formwork from the concrete sidewalk that surrounds the perimeter of the water tank.

0802: Ludlow has finished removing the formwork from the sidewalk surrounding the water tank.

0833: Ludlow continues to sweep the surface of the sidewalk that surrounds the perimeter of the water tank base.

0840: Ludlow is placing 3/8" rock on top of black geofabric at the toe of the chain-link fence located on the north side of the water tank.

0917: Ludlow continues placing 3/8" rock on top of black geofabric at the toe of the chain-link fence located on the north side of the water tank. Ludlow is using a Cat 279D to grade fill around the sidewalk that surrounds the water tank.

0925: Ludlow is using a rolling compactor on the fill surrounding the water tank as they prepare to place pavement later this month.

1123: Ludlow is applying Cure Shield X sealant on the concrete that was placed yesterday around the perimeter of the water tank.

1233: Ludlow continues to grade and compact the fill surrounding the water tank.

1321: Ludlow continues to grade and compact the fill surrounding the water tank.

1409: Ludlow continues to grade and compact the fill surrounding the water tank.

1430: Ludlow has departed the water tank work zone.

Daily Activities – Long Hill pump station, Long Hill Road, Middletown

Knapp Engineering worked at the Long Hill pump station.

0903: Knapp Engineering is working at the Long Hill pump station.

1305: Knapp Engineering continues working at the Long Hill pump station.

1415: Knapp Engineering continues working at the Long Hill pump station.

Res. Representative:	J. Meunier	Date:	5/12/22
-----------------------------	------------	--------------	---------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	3 of 9



Picture 1: Ludlow removing the form work from around the concrete sidewalk they constructed around the perimeter of the water tank located east of the Shared Access Driveway in Middletown. View to the southeast.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	4 of 9



Picture 2: Ludlow sweeping the concrete sidewalk they constructed around the perimeter of the water tank located east of the Shared Access Driveway in Middletown. View to the southwest.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	5 of 9



Picture 3: Ludlow cleaning up gravel and waste asphalt located at the northeast side of the water tank located east of the Shared Access Driveway in Middletown. View to the southeast.

Res. Representative:

J. Meunier

Date: 5/12/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	6 of 9



Picture 4: Ludlow is placing 3/8" rock on top of black geofabric at the toe of the chain-link fence located on the north side of the water tank. View to the west.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	7 of 9



Picture 5: Ludlow grading and compacting fill surrounding the water tank.

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	8 of 9




Picture 6: Ludlow applying Cure Shield X sealant on the concrete that was placed yesterday around the perimeter of the water tank located east of the Shared Access Driveway in Middletown.

Res. Representative:	<u>J. Meunier</u>	Date:	<u>5/12/22</u>
-----------------------------	-------------------	--------------	----------------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	May 12, 2022
Location:	Long Hill Road and the Shared Access Driveway, Middletown	Day of Week:	Thursday
Project #:	AECOM: 6061487	Report No:	424
Contractor:	Ludlow Construction	Page:	9 of 9

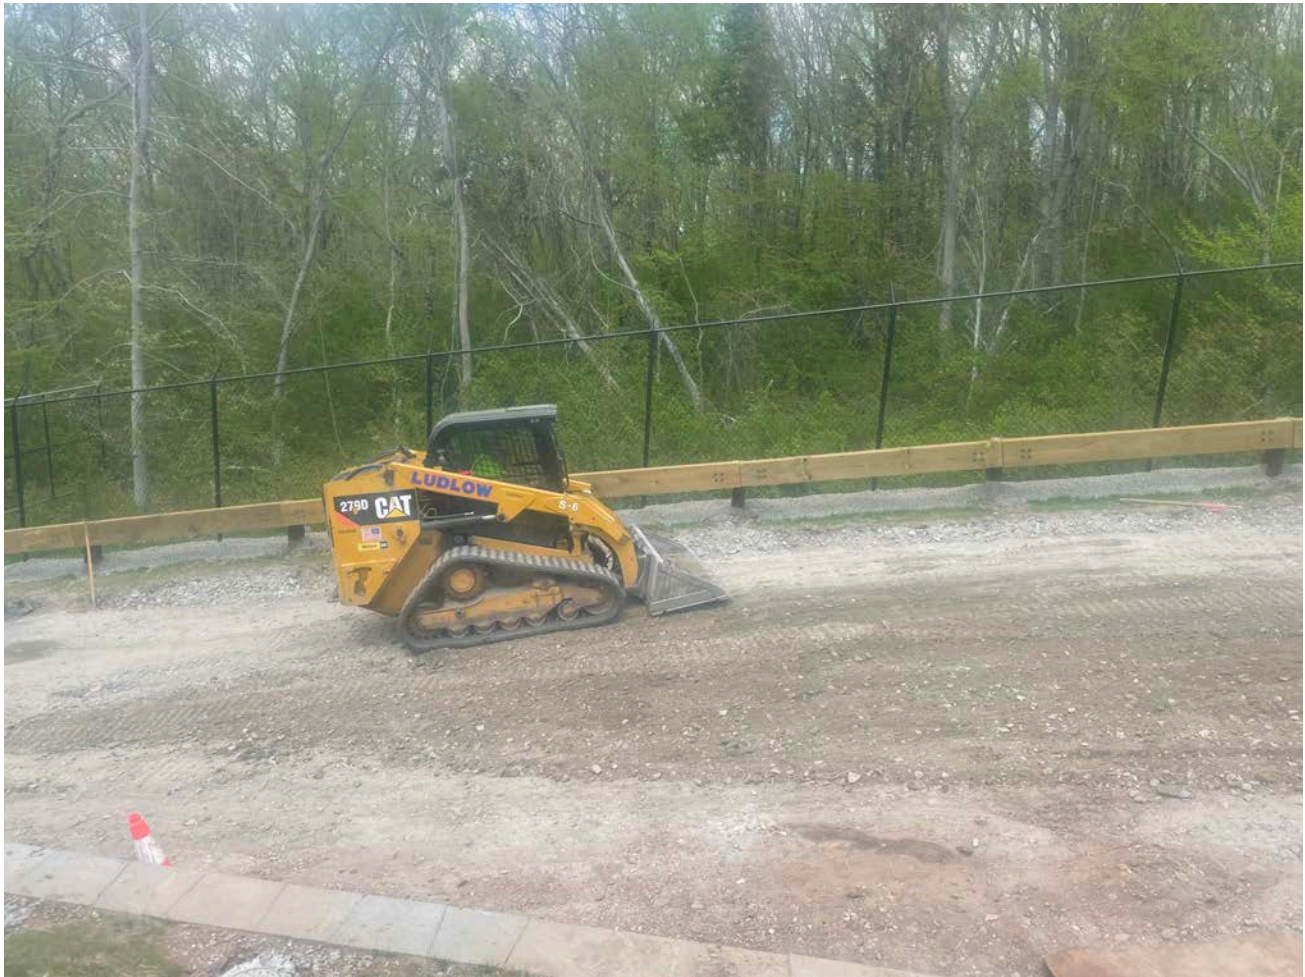

Picture 7: Ludlow using a Cat 279D to grade fill along the water tank driveway. View to the north.

Res. Representative:

J. Meunier

Date: 5/12/22
