

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	July 06, 2022
<b>Location:</b>	Main Street, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	461
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 5

### Weather Conditions

Conditions: Daylight hours: Sunny. Wind variable 0-5 mph.  
 Temperature (°F): High 81°F Low 61°F

Contractors & Subcontractors Workforce				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	1	X	8
Jay's Landscaping	0	x	8	Foreman	0	X	8
West State Mechanical	1	x	8	Dump truck Operator	0	X	8
A&J Construction	0	x	8	Excavator Operator	0	X	8
Grela Well Drilling	0	X	8	Skid Steer/ Bucket Loader	0	X	8
Fazzino Plumbing	0	X	8	Laborers	0	X	8
United Concrete	0	x	8	Note that some persons operate			
Knapp Engineering	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Alarm Systems, Inc.	0	x	8	Sub-contractor	1	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

### Pipe Connections, Installations, and Other Work

Ludlow subcontractor West State Mechanical Inc. continued work at the Durham Manufacturing facility located at 201 Main Street in Durham to install a backflow preventer, 4" copper water line, and other hardware associated with the facility's water service.

### Daily Activities – Installation of water service hardware, 201 Main Street, Durham

Ludlow subcontractor West State Mechanical Inc. continued work at the Durham Manufacturing facility located at 201 Main Street in Durham to install a backflow preventer, 4" copper water line, and other hardware associated with the facility's water service.

0719: West State Mechanical has returned to the Durham Manufacturing facility to resume work on the plumbing associated with the municipal water service that was recently brought into the facility.

1022: West State Mechanical has drilled holes and set anchors into the concrete floor immediately north of where Ludlow brought water service into the Durham Manufacturing facility to secure the backflow preventer stand they fabricated.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	7/06/22
-----------------------------	------------	--------------	---------

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	July 06, 2022
<b>Location:</b>	Main Street, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	461
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 5

1146: West State Mechanical has laid out the path where a 4" copper water feed line will be installed on the ceiling of the Durham Manufacturing facility.

1218: West State Mechanical has just received a shipment of plumbing supplies for the project and is currently taking inventory.


1340: West State Mechanical has hung several pipe support hangers and installed several sections of 4" copper water feed line on the hangers.

1422: West State Mechanical has fabricated and installed the second part of a stand that West State Mechanical will use to support the backflow preventor they will be installing on the west side of the Durham Manufacturing facility.

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	7/06/22
-----------------------------	------------	--------------	---------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	July 06, 2022
<b>Location:</b>	Main Street, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	461
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 5

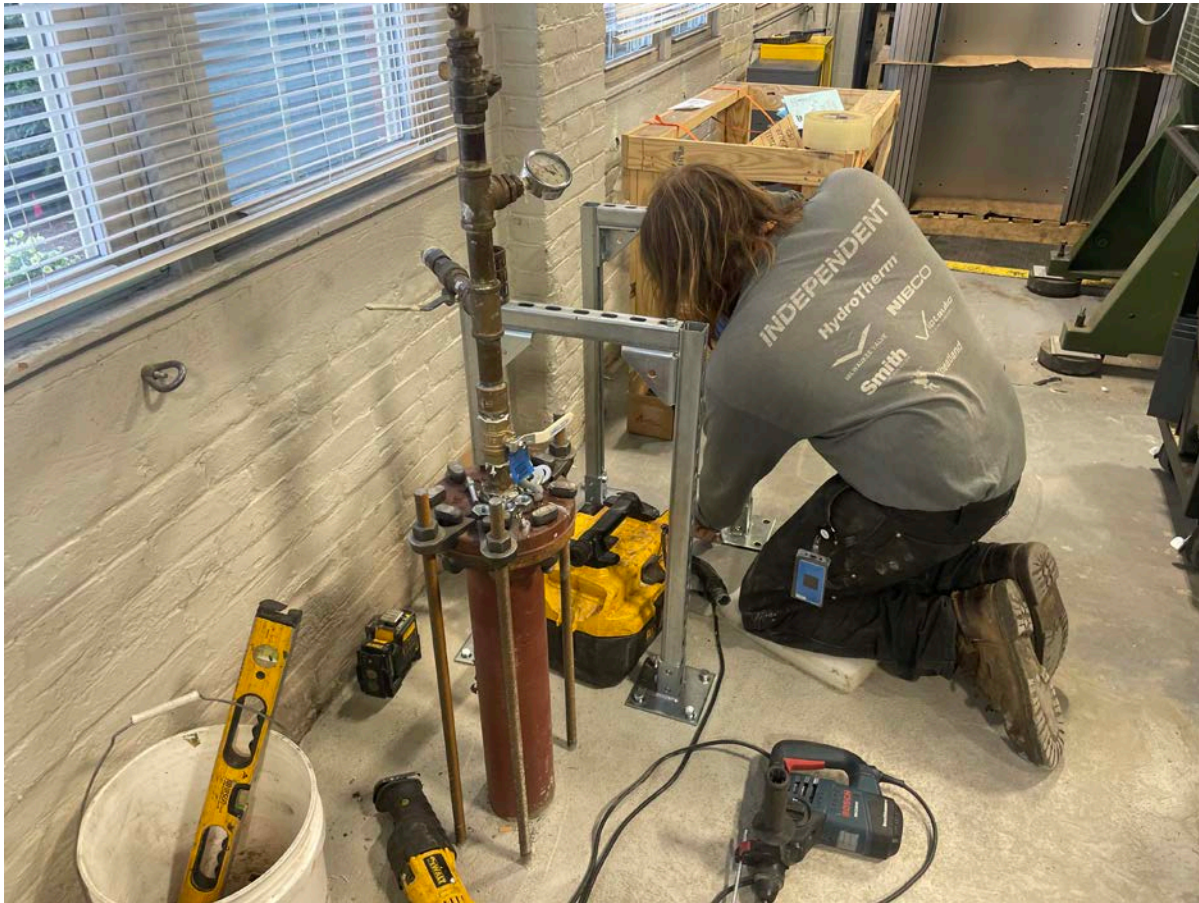

**Picture 1: West State Mechanical securing the second section of the backflow preventer stand on the north side of the water service line that Ludlow previously brought into the Durham Manufacturing facility through the west side of the building. View to the northwest.**

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	7/06/22
-----------------------------	------------	--------------	---------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	July 06, 2022
<b>Location:</b>	Main Street, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	461
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 5



**Picture 2: West State Mechanical cutting sections of threaded rod they will use on the pipe support hangers they are attaching to the ceiling of the Durham Manufacturing Facility.**

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	July 06, 2022
<b>Location:</b>	Main Street, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	461
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 5



**Picture 3: A section of 4" copper water feed line that West State Mechanical installed on the ceiling of the Durham Manufacturing facility.**

<b>Res. Representative:</b>	J. Meunier	<b>Date:</b>	7/06/22
-----------------------------	------------	--------------	---------
