

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 7

### Weather Conditions

Conditions: Daylight hours: Partly Cloudy. Wind variable 0-6 mph.  
 Temperature (°F): High 89°F Low 66°F

Contractors & Subcontractors Workfor57				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	0	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
Flow Tech	0	X	8	Foreman	1	X	8
Matt Chlor	0	x	8	Dump truck Operator	0	X	8
A&J Construction	0	x	8	Excavator Operator	1	X	8
Grela Well Drilling	3	X	8	Skid Steer/ Bucket Loader	0	X	8
Fazzino Plumbing	0	X	8	Laborers	2	X	8
United Concrete	0	x	8	Note that some persons operate			
Knapp Engineering	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Alarm Systems, Inc.	0	x	8	Sub-contractor	3	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Type	#	x	hrs
Concrete/Asphalt Road Saw	0	x	8
Dump truck	2	x	8
Excavator – Large	1	x	8
Excavator - Mid-Size	0	x	8
Excavator - Rubber Wheeled	0	x	8
Skid Steer / Bucket Loader	0	x	8
Rolling Compactor	1	x	8
Plate Compactor	0	x	8
Jumping Jack Compactor	0	x	8
Street Sweeper (Broce Broom)	1	x	8
Material Hopper	0	x	8
Cutoff saw	1	x	8
Light Tower	0	x	8

Visitors: None.

### Daily Activities- Ludlow Construction: Installation of water service, and Permanent Pavement Replacement, Durham, CT

0802: Ludlow Construction is at 63 Maiden Lane excavating a small trench to install a water service at 63 Maiden Lane.

0833: Ludlow Construction has installed a water service to 63 Maiden Lane. Ludlow Construction is backfilling the excavated trench with sand, soil, and gravel.

0959: Ludlow Construction is at 243 Main St saw cutting a section of the blacktop driveway.

1015: Ludlow Construction is at 243 Main St and continues to excavate the driveway.

1056: Ludlow Construction is at 243 Main St and continues to excavate the blacktop using an excavator.

1157: Ludlow construction is at 243 Main St and has finished removing the section of blacktop that was marked previously. Ludlow Construction has laid the base course for the driveway. An excavator and a roller are being used to prepare and compact the base course to prep for asphalt paving.

1234: Ludlow Construction is at 243 Main St placing asphalt.

<b>Res. Representative:</b>	A. Mora	<b>Date:</b>	8/2/22
-----------------------------	---------	--------------	--------

# AECOM

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 7

1317: Ludlow Construction is at 243 Main St and continues to place asphalt on the driveway.

1401: Ludlow Construction is at 243 Main St finishing up rolling the asphalt that was placed on the driveway.


**Res. Representative:**

A. Mora

**Date:** 8/2/22

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 7

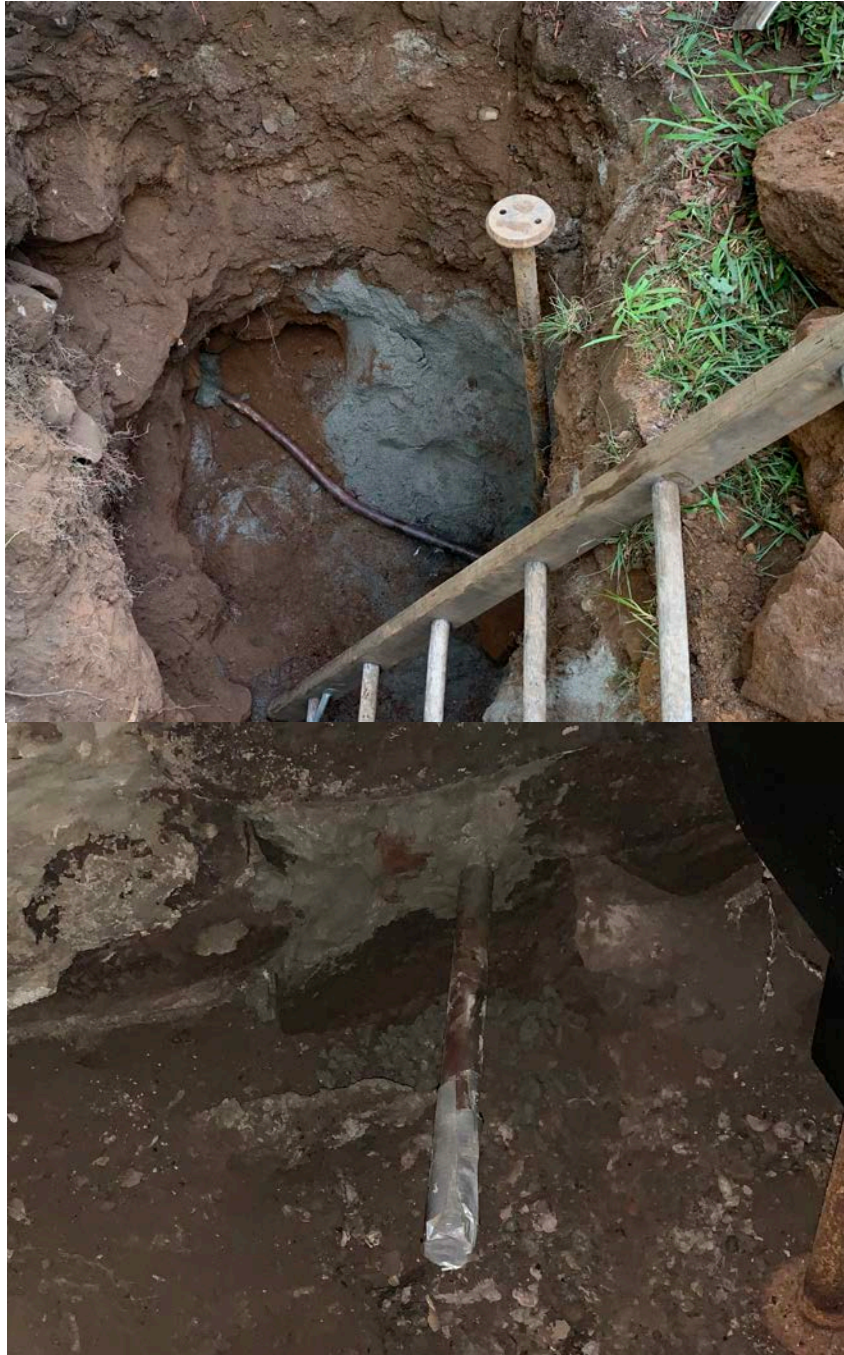

**Picture 1: Ludlow Construction at 63 Maiden Lane installing a water service. (First image represent the outside side of the building foundation, the second image represents the inside side of the building foundation.)**

**Res. Representative:**

A. Mora

**Date:** 8/2/22

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 7



Picture 2: Ludlow Construction is at 243 Main St saw cutting the pavement for permanent driveway pavement repair.

Res. Representative:

A. Mora

Date: 8/2/22



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 7



**Picture 3: Ludlow Construction is at 243 Main St using a roller to compact the driveway base course in preparation for paving.**

**Res. Representative:**

A. Mora

**Date:** 8/2/22

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 7



Picture 4: Ludlow Construction is at 243 Main St continuing to add a combination of soil and gravel using an excavator to prepare for asphalt paving.

<b>Res. Representative:</b>	A. Mora	<b>Date:</b>	8/2/22
-----------------------------	---------	--------------	--------



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 2, 2022
<b>Location:</b>	Main Street and Maiden Lane, Durham	<b>Day of Week:</b>	Tuesday
<b>Project #:</b>	AECOM: 6061487	<b>Report No:</b>	480
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	7 of 7



Picture 5: Ludlow Construction is at 243 Main St laying asphalt on the section of blacktop that was previously removed.

Res. Representative:

A. Mora

Date: 8/2/22
