

AECOM

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	1 of 7

Weather Conditions

Conditions: Daylight hours: Most Sunny. Wind variable 0-6 mph.
 Temperature (°F): High 90°F Low 74°F

Contractors & Subcontractors Workfor57				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	0	X	8
Flow Tech	0	X	8	Foreman	1	X	8
Matt Chlor	0	X	8	Dump truck Operator	0	X	8
A&J Construction	0	X	8	Excavator Operator	1	X	8
Grela Well Drilling	0	X	8	Skid Steer/Bucket Loader	0	X	8
Fazzino Plumbing	0	X	8	Laborers	2	X	8
United Concrete	0	X	8	Note that some persons operate			
Knapp Engineering	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Alarm Systems, Inc.	0	x	8	Sub-contractor	3	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

Daily Activities Ludlow Construction, Water Service Installation activities, Durham, CT.

0741: Ludlow Construction is releasing all the water from the blow-off valve on the west side of the Regional District Superintendent building parking lot. The blow-off valve is being removed by disassembling it. Ludlow Construction uses a pump to take out the water from the excavation.

0825: Ludlow Construction continues to connect the 2-inch pipe that was recently installed to the existing sprinkler system vault.

0858: Ludlow Construction continues to connect the 2-inch pipe that was recently installed to the existing sprinkler system vault.

0958: Ludlow Construction has finished connecting the new fire service to the existing sprinkler system vault.

1045: Ludlow Construction has begun to backfill the excavated area.

1107: Ludlow Construction finishes up backfilling of the excavated area.

Res. Representative:	A. Mora	Date:	8/8/22
-----------------------------	---------	--------------	--------

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	2 of 7

1148: Ludlow Construction compacts the backfilled area with a compactor.

1247: Ludlow Construction is placing loam and seed on top of the excavated area. Loam is being raked by Ludlow Construction's personnel. Ludlow Construction places seeds on top of the topsoil.

Res. Representative:

A. Mora

Date: 8/8/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	3 of 7



Picture 1: Ludlow Construction is disassembling a temporary blow-off valve that is in an excavation trench west of the District 13 regional superintendent parking lot.


Res. Representative:

A. Mora

Date: 8/8/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	4 of 7

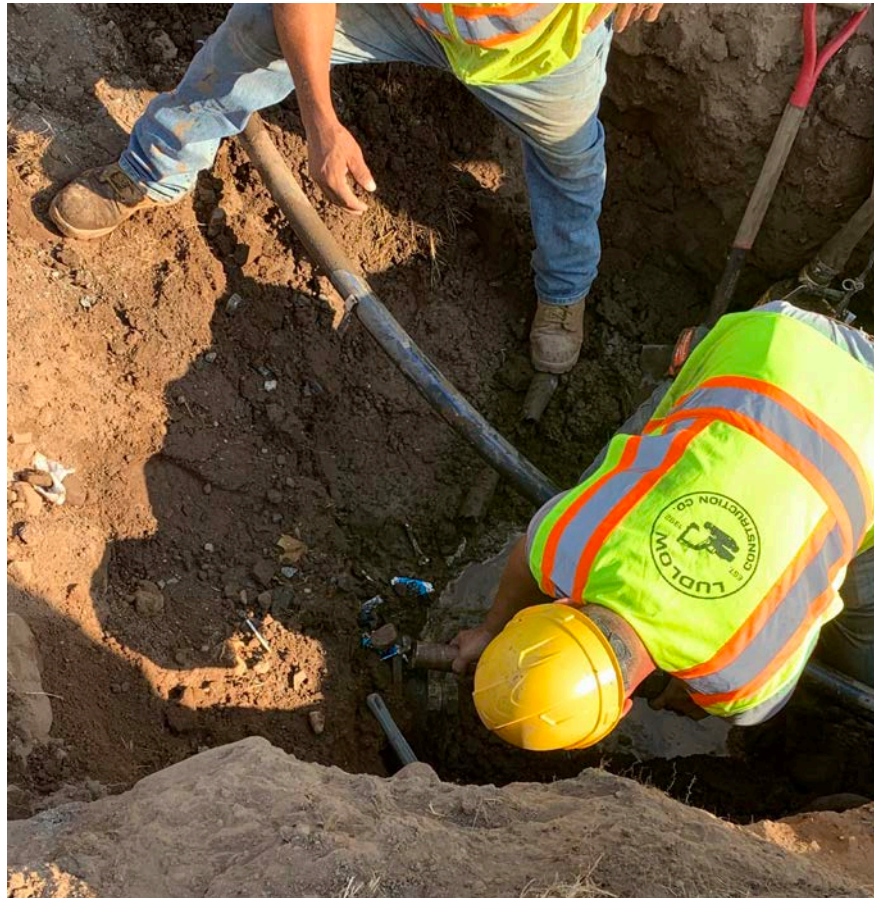

Picture 2: Ludlow Construction is tying in a newly installed pipe to the existing District 13 sprinkler system vault.


Res. Representative:

A. Mora

Date: 8/8/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	5 of 7

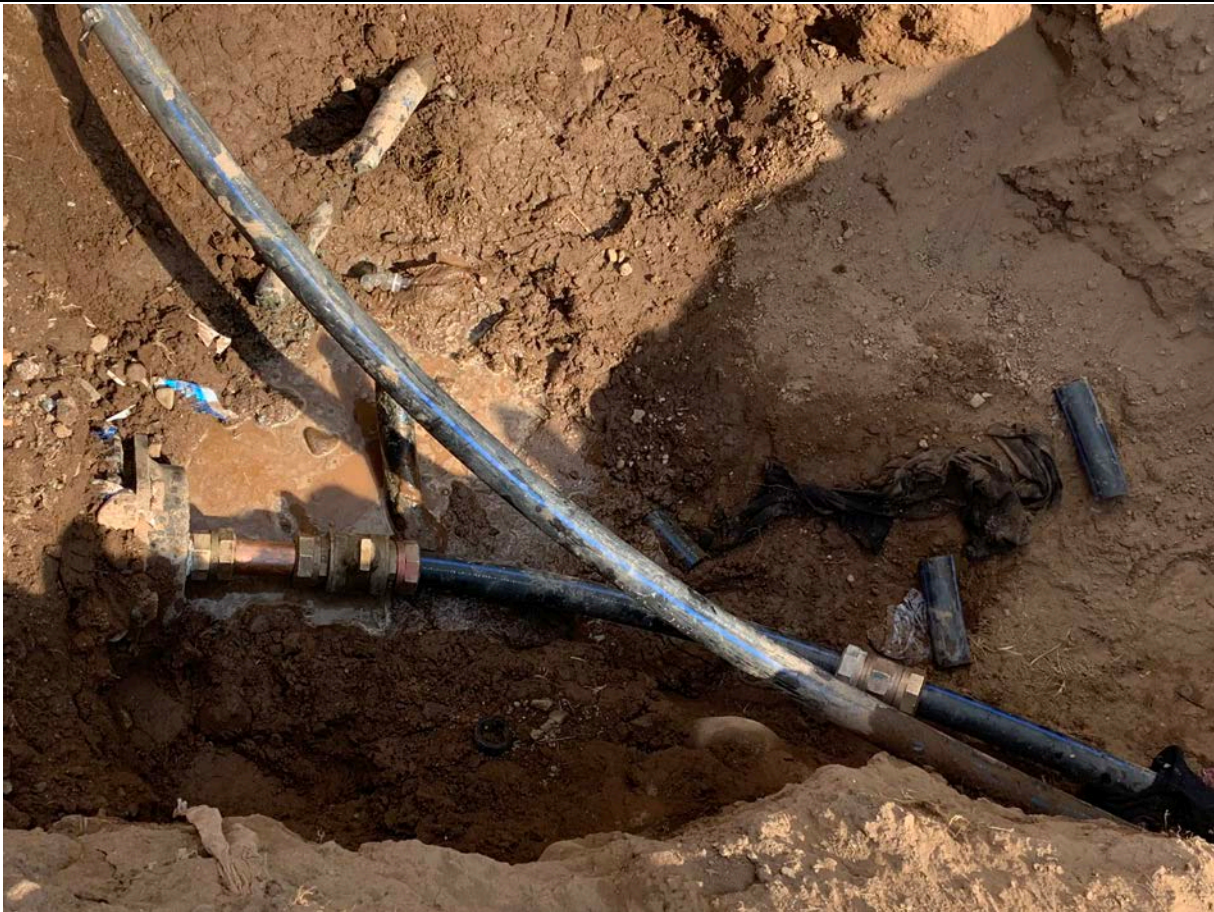

Picture 3: Ludlow Construction is in an excavation trench west of the District 13 regional superintendent parking lot and have completed the tying the new fire service supply pipe to the existing fire service system.

Res. Representative:

A. Mora

Date: 8/8/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	6 of 7



Picture 4: Ludlow Construction is backfilling the trench excavation near the District 13 sprinkler system vault with a combination of soil, gravel, and sand with an excavator.

Res. Representative:

A. Mora

Date: 8/8/22

Daily Report

Project:	Durham Meadows Pipeline Installation	Date:	August 8, 2022
Location:	Coginchaug Regional High School, Pickett Lane, Durham	Day of Week:	Monday
Project #:	AECOM: 6061487	Report No:	484
Contractor:	Ludlow Construction	Page:	7 of 7



Picture 5: Ludlow Construction is at an excavation trench west of the District 13 regional superintendent parking lot and has fully backfilled the trench by topping it off with loam. Ludlow construction uses an excavator, and personnel to rake the topsoil.

Res. Representative:	<u>A. Mora</u>	Date:	<u>8/8/22</u>
-----------------------------	----------------	--------------	---------------
