

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	1 of 11

Weather Conditions			
Conditions:	Daylight hours: Partly cloudy. Wind variable 0-10 mph.		
Temperature (°F):	High 84°F	Low	70°F

Contractors & Subcontractors Workfor57				Equipment in Use			
Trade	#	x	hrs	Trade	#	X	hrs
USACE				Ludlow Construction			
Field Engineer	1	x	8	Superintendent	0	X	8
				Safety Officer	1	X	8
Flow Tech	0	x	8	Foreman	1	X	8
Matt Chlor	0	x	8	Dump truck Operator	1	X	8
A&J Construction	0	x	8	Excavator Operator	1	X	8
Grela Well Drilling	0	X	8	Skid Steer/Bucket Loader	1	X	8
Fazzino Plumbing	0	X	8	Laborers	3	X	8
United Concrete	0	x	8	Note that some persons operate			
Knapp Engineering	0	x	8	Multiple pieces equipment.			
Apuzzo Electric	0	x	8				
Alarm Systems, Inc.	0	x	8	Sub-contractor	0	X	8
A&R Electrical	0	x	8	Municipal Police Detail	0	X	8
				State Police Detail	0	X	8

Visitors: None.

### Daily Activities – Miscellaneous Activities, Durham

0751: Ludlow Construction is saw cutting a section of the road at Pickett Lane.

0831: Ludlow Construction is excavating to remove blow-offs at Pickett Lane

0904: Fazzino Plumbing is at 200 Maple Ave preparing to install the final interior water service connection.

0914: Ludlow Construction has excavated a section of road at Pickett Lane to remove two blow-off valves and is compacting the soil within the excavated trench.

0948: Ludlow Construction is placing loam and seed on top of an excavated area to restore the area back to its original condition.

1015: Ludlow Construction is saw cutting a section of blacktop at the United Methodist Church of Durham.

1042: Ludlow has removed a section of blacktop at the United Methodist Church of Durham and is using a compactor to compact the base course for paving.

<b>Res. Representative:</b>	A. Mora	<b>Date:</b>	8/10/22
-----------------------------	---------	--------------	---------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	2 of 11

1058: Fazzino Plumbing is at 200 Maple Ave finishing up the final interior water service connection.

1225: Ludlow Construction is on 208 Main St and has removed the blacktop portion of the driveway.

1302: Ludlow Construction is laying gravel and soil on the section of the area where the blacktop was removed. Ludlow Construction is using a compactor to compact the area where the blacktop was removed.

1320: Fazzino Plumbing is at 63 Maiden Lane finishing the installation of the final interior water service.

1348: Ludlow Construction is at 208 Main Street placing asphalt.

1430: Ludlow Construction is at the United Methodist Church of Durham laying asphalt.

1458: Ludlow Construction is laying asphalt west of District 13 regional superintendent high school parking lot to restore the pavement area. Ludlow Construction uses a roller to compact the asphalt.

<b>Res. Representative:</b>	<u>A. Mora</u>	<b>Date:</b>	<u>8/10/22</u>
-----------------------------	----------------	--------------	----------------

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	3 of 11



**Photo 1: Ludlow Construction begins to cut a section of the road on Pickett Lane.**

**Res. Representative:**

A. Mora

**Date:** 8/10/22



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	4 of 11



**Photo 2: Ludlow Construction removes the blacktop of the two sections that were cut prior. Ludlow Construction begins the excavation to remove two blow-off valves in each of the respective locations.**

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	5 of 11

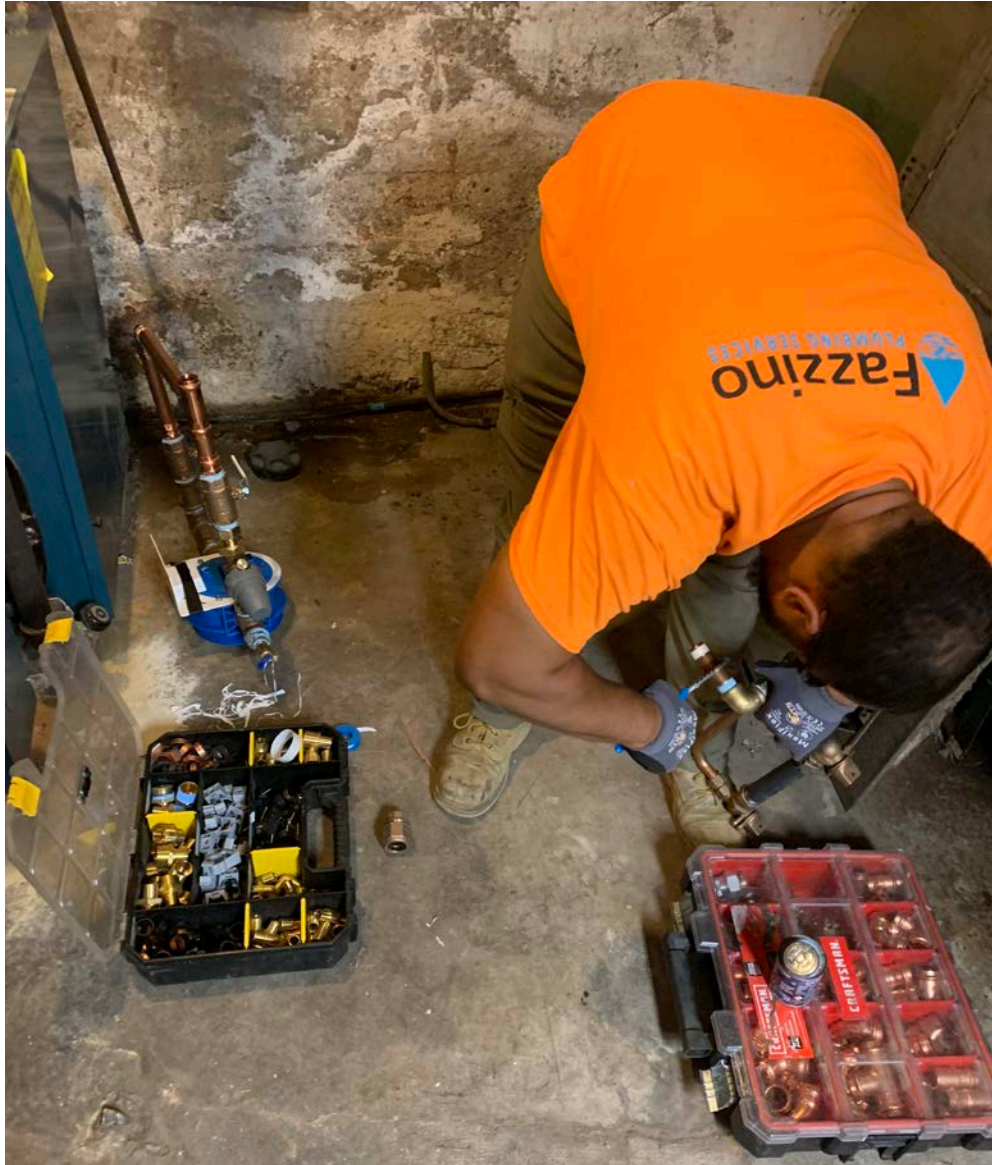


Photo 3: Fazzino Plumbing begins piping work to connect the residence with the city water.



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	6 of 11



**Photo 4: Ludlow construction placing loam and seed at Korn School.**



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	7 of 11



Photo 5: Ludlow Construction using a saw to cut the blacktop at United Methodist Church of Durham.



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	8 of 11



Photo 6: Fazzino Plumbing is at 200 Maple Ave installing the final interior water service connection.

<b>Res. Representative:</b>	<u>A. Mora</u>	<b>Date:</b>	<u>8/10/22</u>
-----------------------------	----------------	--------------	----------------



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	9 of 11



Photo 7: Ludlow Construction is removing the blacktop on 208 Main St.

## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	10 of 11



**Photo 8: Fazzino Plumbing is at 63 Maiden Lane installing the final interior water service connection.**

<b>Res. Representative:</b>	<u>A. Mora</u>	<b>Date:</b>	<u>8/10/22</u>
-----------------------------	----------------	--------------	----------------



## Daily Report

<b>Project:</b>	Durham Meadows Pipeline Installation	<b>Date:</b>	August 10, 2022
<b>Location:</b>	Coginchaug Regional High School, Pickett Lane, Durham	<b>Day of Week:</b>	Wednesday
<b>Project #:</b>	AECOM: 60614871	<b>Report No:</b>	486
<b>Contractor:</b>	Ludlow Construction	<b>Page:</b>	11 of 11



**Photo 9: Ludlow Construction is laying asphalt at the 208 Main St. driveway.**

<b>Res. Representative:</b>	<u>A. Mora</u>	<b>Date:</b>	<u>8/10/22</u>
-----------------------------	----------------	--------------	----------------
